CIN: U74120MH2010PTC207869 MSME Reg. No.: UDYAM-MH-18-0083617 An ISO 9001: 2015 Certified Company





# **COST VETTING REPORT**



#### Details of the property under consideration:

Name of Project: "Sheetal Ekta"

"Sheetal Ekta", Proposed Redevelopment of existing building No. 18 – A & B, known as Dindoshi Ekta CHSL on Plot bearing S. No. 31 & 39, CTS. No. 110(pt.) & 146 (pt.), Shivdham Complex, Gen. A. K. Vaidya Marg, Village – Dindoshi, Malad (East), Mumbai – 400 097, State – Maharashtra, Country – India

Think.Innovate.Create

Latitude Longitude: 19°10'32.1"N 72°51'40.3"E

# Valuation Done for: State Bank of India SME Chembur Branch

Unit No. 11, Building No. 11, Ground Floor, Corporate Park, Sion Trombay Road, Chembur, Mumbai, Pin Code – 400 071, State - Maharashtra, Country – India.



Ou	r Pan	India Pres	ence	at:	
Q T	Aumbai hane Ielhi NCR	♥ Aurangabad ♥ Nanded ♥ Nashik	Pundo Indo Ahm		Rajkot Raipur Jaipur

Regd. Office: B1-001, U/B Floor, Boomerang, Chandivali Farm Road, Andheri (East), Mumbai - 400 072, (M.S.), INDIA

TeleFax: +91 22 28371325/24
mumbai@vastukala.org

CIN: U74120MH2010PTC207869 MSME Reg. No.: UDYAM-MH-18-0083617 An ISO 9001:2015 Certified Company





Vastu/SBI/Mumbai/12/2023/5368/2304028 18/11-257-PY

Date: 18.09.2023

To,
The Branch Manager,
State Bank of India
SME Chembur Branch
Unit No. 11, Building No. 11,
Ground Floor, Corporate Park,
Sion Trombay Road, Chembur,
Mumbai, Pin Code – 400 071,
State - Maharashtra, Country – India.

Sub: Cost Vetting Report for "Sheetal Ekta" at Malad (East) Mumbai, Pin Code – 400 097.

Ref: As per your mail dated 01.12,2023

Dear Sir.

In accordance with your letter of engagement as stated above, we enclose our Report on Cost Vetting for "Sheetal Ekta", Proposed Redevelopment of existing building No. 18 – A & B, known as Dindoshi Ekta CHSL on Plot bearing S. No. 31 & 39, CTS. No. 110(pt.) & 146 (pt.), Shivdham Complex, Gen. A. K. Vaidya Marg, Village – Dindoshi, Malad (East), Mumbai – 400 097, State – Maharashtra, Country – India.

M/s. DGS Township Pvt. Ltd., making a difference requires consistent effort and a commitment to quality. DGS Group have been committed to constructing architectural landmarks that redefine the Mumbai skyline. Over the years, they have garnered a reputation for delivering exceptional properties and world-class infrastructure, with an enhanced focus on affordable housing and sustainable growth. Their dedication to innovation, integrity, and quality shows in every project they undertake. From conception to completion, they develop each of their unique projects with passion, creativity, and expertise. They strive to add to the alluring landscape of the thriving city of dreams, Mumbai. When looking to construct an enduring, excellent structure, trusting the skills and efficiency of the DGS team.

M/s. DGS Township Pvt. Ltd. is proposing redevelopment of existing building No. 18 – A & B, known as Dindoshi Ekta CHSL on Plot bearing S. No. 31 & 39, CTS. No. 110(pt.) & 146 (pt.), Shivdham Complex, Gen. A. K. Vaidya Marg, Village – Dindoshi, Malad (East), Mumbai – 400 097, State – Maharashtra, Country – India. Project is comprising Commercial cum Residential of Rehab cum Sale Building.





Regd. Office: B1-001, U/B Floor, Boomerang, Chandivali Farm Road, Andheri (East), Mumbai - 400 072, (M.S.), INDIA
TeleFax: +91 22 28371325/24

mumbai@vastukala.org

Commercial cum Residential of Rehab cum Sale Building is proposed of Basement + Ground Floor + 1st to 33rd Upper Floors with total RERA carpet area of 92,490.42 Sq. Ft. which consists 2 BHK, Offices and Shops units with 73 nos. of Sell flats, 48 Tenant Flats, 4 Security to Society Flats, 4 Sell Offices, 9 Tenant Offices & 4 Tenant Shops providing with Fitness Centre, Society Office, & Other Amenities.

In this regard, SBI, SME Chembur Branch, Unit No. 11, Building No. 11, Ground Floor, Corporate Park, Sion Trombay Road, Chembur, Mumbai, Pin Code – 400 071, has approached Vastukala Consultants (I) Pvt. Ltd. (VCIPL) to conduct a Cost Vetting of the said project.

Our analysis of the cost vetting is enclosed in this report. This Report forms an integral whole and cannot be split in parts. The outcome of the report/ study can only lead to proper conclusions if the Report as a whole is taken into account.

The information used by Vastukala Consultants (I) Pvt. Ltd. (VCIPL) in preparing this report has been obtained from a variety of sources and other relevant documents provided by the client & bank. As agreed, we have performed our cost vetting exercise with the data available related to the business, considering the market prospects and projections. Our results are dependent on documents provided by client & bank, the underlying assumptions, which has been analyzed at a broader level by VCIPL while assessing their reasonableness.

Total Project Cost for the completion of Project will be ₹ 116.48 Cr.

For Vastukala Consultants (I) Pvt. Ltd.

# Manoj Chalikwar

Digitally signed by Manoj Chalikwar DN: cn=Manoj Chalikwar, o=Vastukala Consultants (I) Pvt. Ltd., ou=Mumbai, email=manoj@vastukala.org, c=IN

Manoj B. Chalikwar

Registered Valuer Chartered Engineer (India) Reg. No. IBBI / RV / 07/2018/10366 Reg. No. CAT-I-F-1763

SBI Empanelment No.: SME/TCC/2021-22/86/3





Valuation Report Prepared For: SBI / SME Chembur Branch / Sheetal Ekta (5368/2304028) Page 4 of 16 About the Project:

Proposed Redevelopment of existing building No. 18 – A & B, known as Dindoshi Ekta CHSL on Plot bearing S. No. 31 & 39, CTS. No. 110(pt.) & 146 (pt.), Shivdham Complex, Gen. A. K. Vaidya Marg, Village – Dindoshi, Malad (East), Mumbai – 400 097. It is about 2.60 Km. travelling distance from Malad (East) Railway station.

#### Area Statement as per Approved Plan

A	AREA STATEMENT	
1	Area of the plot (As per MHADA NOC & Demarcation)	1,128.58
2	Deduction for	
а	Road Set back area	34.25
b	Proposed Road	-
С	Any reservation	-
d	% Amenity space as per DCR 56 / 57 (Sub plot)	-
е	Other	
	Total ( a + b + c + d + e)	34.25
3	Balance Area of the plot (1 – 2)	1,094.33
4	Deduction for 15% recreational ground	-
	10% Amenity space (If deductible for IND)	
5	Net Area of Plot (3 – 4)	1,094.33
6	Additions for FSI purpose	
2a	100% for DP Road	
2b	100% for Set – back	34.25
	Total (2a + 2b)	34.25
7	Total Area (5 + 6)	1,128.58
8	FSI Permissible	3.00
9	i) Permissible Floor Area (7 X 8)	3,385.74
	ii) Additional Layout FSI	3,760.00
	Total Permissible Area 9 (i) + 9 (ii)	7,145.74
10	Proposed Built up Area	6,436.21
11	Excess Balcony Area taken in floor space index	N.A.
12	Total Proposed Area (10 + 11)	6,436.21
В	Details of FSI Availed as per DCR 35 (4)	
1	Fungible Built up area component proposed vide DCR 35 (4) for purely residential = OR < (D(i) X 0.35)	172.82
2	Fungible Built up area component proposed vide DCR 35 (4) for non – residential = OR < (12 X 0.20)	615.34
3	Total Fungible Built up area vide DCR 35 (4)	788.16
4	Total BUA proposed including fungible compensatory area (12 + B(3))	7,224.37
5	Permissible fungible area	2,501.00
C	Prorata shares as per MHADA	
1	Prorata share as per letter No. CO/MB/REE/NOC/F-337/84 X 40 = 3,360 M.	3,760.00
2	Total Gross Built up area permissible	9,646.74
3	Total Gross Built up area proposed	7,224.37
4	No. CO/MB/REF/NOC/F-337/1047/2019	
D	Tenement Statement	
i	Total Gross Built up area proposed	7,224.37
ii	Less Deduction of Non – Residential area (Shop, etc.)	1,799.71
M	Area available for tenements	5,424.66
iv	FSI consumed on net holding	
V	Fungible FSI consumed on net holding	-



Valuation Report Prepared For: SBI / SME Chembur Branch / Sheetal Ekta (5368/2304028) Page 5 of 16

A	AREA STATEMENT	
vi	Tenements permissible	381 nos.
vii	Tenements proposed	60 nos.
viii	Tenements existing	4. (9.1)
	Total Tenements on the plot	1 1 1 1 1 1
E,	Parking Statement	¥ .
i	Parking required by regulations for	51 nos.
	Car / Scooter / Motor cycle	
	Outsiders (visitors)	3
íi	Covered garages permissible	A
iii	Covered garages provided	As per area statement
	Car	Statement
	Scooter / Motor Cycle	
7	Outsiders (visitors)	
iv	Total Parking Provided	77 nos.
F	Transport Vehicles parking	
1	Spaces for transport vehicles parking required by regulations	
ii	Total no. of transport vehicles parking spaces provided	14:

# Area Statement as per Concession Drawing Plan

A	AREA STATEMENT	
1	Area of the plot (As per MHADA NOC & Demarcation)	1,128.58
2	Deduction for	- 12 1/61x
a	Road Set back area	34.25
b	Proposed Road	J. 191-
С	Any reservation	
d	% Amenity space as per DCR 56 / 57 (Sub plot)	
9	Other Annual Control of the Control	JE JEST
	Total ( a + b + c + d + e)	34.25
3	Balance Area of the plot (1 – 2)	1,094.33
4	Deduction for 15% recreational ground	1412 17
	10% Amenity space (If deductible for IND)	-
5	Net Area of Plot (3 – 4)	1,094.33
6	Additions for FSI purpose	
2a	100% for DP Road	100
2b	100% for Set – back	34.25
10	Total (2a + 2b)	34.25
7	Total Area (5 + 6)	1,128.58
8	FSI Permissible	3.00
9	a) FSI credit available by development right (restricted to % of the balance area vide 3 above)	THE THE
	Additions for FSI purpose	17.9
	b) 33% as per DCR 32 (2754.57 X 33%)	
	c) External TDR (As per App. VII – B) (67%)	*
	d) Other	
	Total	V 8
10	i) Permissible Floor Area (7 X 8) + 9	3,385.74
	ii) Additional Layout FSI	3,760.00
	Total Permissible Area 10 (i) + 10 (ii)	7,145.74
11	Proposed Built up Area	7,120.51
	i) Existing Floor Area	N.A.





Valuation Report Prepared For: SBI / SME Chembur Branch / Sheetal Ekta (5368/2304028) Page 6 of 16

Valuatio	n Report Prepared For: SBI / SME Chembur Branch / Sheetal Ekta (5368/2304028) Page 6 of 16	
A	AREA STATEMENT	THE PARTY OF
12	Excess Balcony Area taken in floor space index	N.A.
13	Total Proposed Area (10 + 11 + 12)	
В	Details of FSI Availed as per DCR 35 (4)	
1	Fungible Built up area component proposed vide DCR 35 (4) for purely residential = OR < (D(i) X 0.35)	2,124.31
2	Fungible Built up area component proposed vide DCR 35 (4) for non – residential = OR < (12 X 0.20)	367.87
3	Total Fungible Built up area vide DCR 35 (4)	2,492.18
4	Total BUA proposed including fungible compensatory area (12 + B(3))	9,612.69
C	Prorata shares as per MHADA	
1	Prorata share as per letter No. CO/MB/REE/NOC/F-337/84 X 40 = 3,360 M.	3,760.00
2	Total Gross Built up area permissible	13,372.69
3	Total Gross Built up area proposed	9,612.69
4	No. CO/MB/REF/NOC/F-337/1047/2019	
D	Tenement Statement	
i	Total Gross Built up area proposed	9,612.69
ii	Less Deduction of Non – Residential area (Shop, etc.)	1,418.94
iii	Area available for tenements	8,193.75
iv	FSI consumed on net holding	
V	Fungible FSI consumed on net holding	
vi	Tenements permissible	381 nos.
vii	Tenements proposed	125 nos.
viii	Tenements existing	
	Total Tenements on the plot	
E	Parking Statement	
i	Parking required by regulations for	79 nos.
	Car / Scooter / Motor cycle	
	Outsiders (visitors)	
ii	Covered garages permissible	As per area
iii	Covered garages provided	statement
	Car	Statement
	Scooter / Motor Cycle	
	Outsiders (visitors)	
iv	Total Parking Provided	111 nos.
F	Transport Vehicles parking in Linnovate Create	
i	Spaces for transport vehicles parking required by regulations	
ii	Total no. of transport vehicles parking spaces provided	



### Construction Area as per Approved Plan for Rehab cum Sale Building

					POCK
Sr.	Floor	Built Up Area in	Staircase Area in	Other Area	Total Construction
No.	2 100000	Sq. M.	Sq. M.	in Sq. M.	Area in Sq. M.
1	Basement Floor	217.91	131.22	89.61	438.74
2	Ground Floor	265.24	131.22	89.61	486.07
3	1st Floor	311.93	112.53	89.61	514.07
4	2nd Floor	311.93	112.53	89.61	514.07
5	3rd Floor	311.93	112.53	89,61	514.07
6	4th Floor	253.76	115.71	89.61	459.08
7	5th Floor	253.76	115.71	89.61	459.08
8	6th Floor	191.71	115.71	158.22	465.64
9	7th Floor	203.70	115.71	89.61	459.08
10	8th Floor	253.76	115,71	89.61	459.08
11	9th Floor	253.76	115.71	89.61	459.08
12	10th Floor	253.76	115.71	89.61	459.08
13	11th Floor	253.76	115.71	89.61	459.08
14	12th Floor	253.76	115.71	89.61	459.08
15	13th Floor	191.71	115.71	158.22	465.64
16	14th Floor	253.76	115.71	89.61	459.08
17	15th Floor	253.76	115.71	89.61	459.08
18	16th Floor	253.76	115.71	89.61	459.08
19	17th Floor	253.76	115.71	89.61	459.08
20	18th Floor	253.76	115.71	89.61	459.08
21	19th Floor	253.76	115.71	89.61	459.08
22	20th Floor	183.31	115.69	169.19	468.19
23	21st Floor	253.76	115.71	89.61	459.08
24	22nd Floor	253.76	115.71	89.61	459.08
25	23rd Floor	253.76	115.71	89.61	459.08
26	24th Floor	346.03	114.42	7.7	460.45
27	25th Floor	346.03	114.42	Dyo's	460.45
28	26th Floor	346.03	114.42	7	460.45
29	27th Floor	257.62	114.39	95.97	467.98
30	28th Floor	347.94	114.39		462.33
31	29th Floor	347.94	114.39		462.33
32	30th Floor	347.94	114.39	- I	462.33
33	31st Floor	347.94	114.39		462.33
34	32nd Floor	347.94	114.39		462.33
35	33rd Floor	277.69	114.39	67.57	459.65
36	Terrace / OHT	8 12	114.39	-	114.39
	TOTAL	9,612.69	4,172.59	2,620.51	16,405.79
	× 1 2 2	No. of Stack Car I			111 Nos.



400.30

#### **Project Cost**

Sr. No.	Particulars	Total Estimated Amount in ₹	Total Estimated Amount in ₹ Cr.
1	Land Cost		
i.	Acquisition Cost of Land or Development Rights, and Legal Cost.	1,56,47,420.00	1.56
ii.	Rent to Tenants, Lease premium, Lease Rent, interest cost incurred or payable on Land Cost	14,71,11,560.00	14.71
iii.	Amount of Premium payable to obtain development rights, FSI, additional FSI, fungible area, and any other incentive under DCR from Local Authority or State Government or any Statutory Authority.	27,72,60,604.00	27.73
iv.	Acquisition cost of TDR (if any)	-	
2	Cost of Construction		
i.	Estimated construction cost of rehab cum sale building including site development and infrastructure for the same.	57,22,82,410.00	57.23
ii.	On site expenditure for development of entire project excluding cost of construction as per(i) above,		
a.	Architect Fees & Consultant fees	1,14,45,648.00	1.14
b.	Admin Cost includes salaries, site overheads, development works, cost of services (including water, electricity, sewerage, drainage, layout roads etc.), cost of machineries and equipment including its hire and maintenance cost, consumables etc. All costs directly incurred to complete the construction of the entire phase of the project registered.	2,86,14,121.00	2.86
C.	Marketing Cost	2,75,20,165.00	2.75
3	Interest during the Project	8,49,00,000.00	8.49
4.	Contingency Charges	-	
	GRAND TOTAL:	116,47,81,928.00	116.48

# For VASTUKALA CONSULTANTS (I) PVT. LTD. ate. Create

Manoj Chalikwar Digitally signed by Manoj Chalikwar DN: cn=Manoj Chalikwar, o=Vastukala Consultants (I) Pvt. Ltd., ou=Mumbai, email=manoj@vastukala org, c=IN Date: 2023.12.18 14:10:28 +05'30'

Director

Auth. Sign.

Manoj B. Chalikwar

Registered Valuer Chartered Engineer (India)

Reg. No. IBBI / RV / 07/2018/10366

Reg. No. CAT-I-F-1763

SBI Empanelment No.: SME/TCC/2021-22/86/3







Valuation Report Prepared For: SBI / SME Chembur Branch / Sheetal Ekta (5368/2304028) Page 9 of 16 Comments on each element of Cost of Project: -

#### 1. Land Cost:

As per Present Ready Reckoner rate the Project Land Value is ₹ 7.47 Cr. considering Land Rate @ ₹ 68,240.00 per Sq. M. & Net Plot Area of 1,094.33 Sq. M.

As per document purchase cost of land & stamp duty cost is ₹ 1,56,47,420.00 i.e., ₹ 1.56 Cr. which is 1.34% of Total Project Cost.

Sr. No.	Agreement Name	Date	Particulars	Total Cost in ₹	Incurred Cost in ₹
1	Development	-40	Stamp Duty	1,44,97,980.00	1,44,97,980.00
2	Agreement	3/27/2019	Dog Food	30,000.00	30,000.00
3	Agreement		Reg. Fees	2,000.00	2,000.00
4	Rectification Cum	4/29/2022	Stamp Duty	10,86,200.00	10,86,200.00
5	Supplementary Deed	4/29/2022	Reg. Fees	30,000.00	30,000.00
6	Special Power of	3/27/2021	Stamp Duty	500.00	500.00
7	Attorney	3/2//2021	Reg. Fees	740.00	740.00
	\.	TOTAL	a A	1,56,47,420.00	1,56,47,420.00

#### 2. Payment Payable to Rehab Tenants (Rent Cost):

Since it is a having some redevelopment flat from the date of shifting of 61 Tenants till handing over their respective new flats as per the Tenant Agreement. Further the rent keeps on increasing as per agreement. The existing Tenants has to be given total rental of ₹ 14,71,11,560.00 i.e., ₹ 14.71 Cr. Builder has paid ₹ 7.90 Cr. which is 12.63 % of Total Project Cost.

which is 12.63 % of Total Project Cost.

Existing Tenants Carpet Area & Rent per month for Flat are as follows:

Sr. No	Particulars Particulars	Commercial Shops	Commercial Offices	Residential Flat	Total	Units
1	No. of Tenants	4.00	9.00	48.00	61.00	Nos.
2	Rent per tenant per month for April 23 to Feb 24	110,000.00	50,000.00	40,000.00		Rupees
3	Rent per year for April 23 to Feb 24	4,840,000.00	4,950,000.00	21,120,000.00	30,910,000.00	Rupees
4	Rent per tenants per month for March 24 to Jan 25	121,000.00	55,000.00	44,000.00		Rupees
5	Rent per year for March 24 to Jan 25	5,324,000.00	5,445,000.00	23,232,000.00	34,001,000.00	Rupees
6	Rent per tenants per month for Feb 25 to March 25	133,100.00	60,500.00	_		Rupees
7	Rent per year for Feb 25 to March 25	1,064,800.00	1,089,000.00	Special St. Sp	2,153,800.00	Rupees
8	Rent per tenants per month for Feb 25 to Dec 25	-	-	48,400.00		Rupees
9	Rent per year for Feb 25 to Dec 25	Lagaur *		25,555,200.00	25,555,200.00	Rupees
10	Rent per tenants per month for Jan 26 to Mar 26	-	3 22	53,240.00		Rupees
11	Rent per year for Jan 26 to Mar 26	-		7,666,560.00	7,666,560.00	Rupees



Valuation Report Prepared For: SBI / SME Chembur Branch / Sheetal Ekta (5368/2304028) Page 10 of 16

	ALIOTT ROBOTET TODATOUT O			Elita (0000:E00 loE0)		
Sr. No	Particulars	Commercial Shops	Commercial Offices	Residential Flat	Total	Units
12	Corpus Fund per Tenant	800,000.00	700,000.00	700,000.00		Rupees
13	Total Corpus Fund	3,200,000.00	6,300,000.00	33,600,000.00	43,100,000.00	Rupees
14	Shifting Charges per Tenant	15,000.00	15,000.00	15,000.00		Rupees
15	Total Shifting Charges	60,000.00	135,000.00	720,000.00	915,000.00	Rupees
16	Brokerage Cost	440,000.00	450,000.00	1,920,000.00	2,810,000.00	Rupees
17	Total Rent Cost (3 + 5 + 7 + 9 + 11 + 13 + 15 + 16)	1,49,28,800.00	1,83,69,000.00	11,38,13,760.00	14,71,11,560.00	Rupees

#### 3. Building Cost of Construction for Rehab cum Sale Building:

Construction Area of Rehab cum Sale Building = 16,405.79 Sq. M. i.e., 1,76,591.93 Sq. Ft. No. of Stack Car Parking = 111 Nos.

Total estimated cost for construction of Building (includes cost of RCC work, manpower, lift, material, painting, finishing work, site development, etc.) is ₹ 49,21,73,724.00 i.e., ₹ 49.22 Cr. which comes ₹ 30,000.00 per Sq. M. on construction area for building, cost for deep excavation & shore piling is ₹ 2,46,08,686.00 i.e., ₹ 2.46 Cr. which comes 5% of cost of construction of building and cost for stack parking is ₹ 5,55,00,000.00 i.e., ₹ 5.55 Cr. which comes ₹ 5,00,000.00 per stack parking.

Hence, total construction cost (Cost of construction of building + Cost of deep excavation & shore piling + Cost of stack parking) (₹ 49,21,73,724.00 + ₹ 2,46,08,686.00 + ₹ 5,55,00,000.00) = ₹ 57,22,82,410.00 i.e., ₹ 57.23 Cr. The total construction area is 16,405.79 Sq. M. i.e., 1,76,591.93 Sq. Ft., projected cost of ₹ 57.23 Cr is 49.13% of total project cost

VCIPL opinion the construction cost of 30,000/- Per Sq. M. which is in line with Market-Trend.

Particulars	Rate per Sq. Ft.
Excavation Work	1500.00
Total RCC Work	15000.00
Final Finishing Work	7500.00
Other Work	6000.00
Cost of Construction	30000.00
Deep Excavation & Shore Piling Cost	5% of construction cost of building
Stack Car Parking Cost	5,00,000.00 per parking

#### 4. Approval Charges:

The Total Approval Cost (Fungible Cost & Development Cess Premium & TDR Cost) as per architect letter will be ₹ 27,72,60,604.00 i.e., ₹ 27.73 Cr. which is 23.80% of Total Project Cost. Builder has paid ₹ 11.63 Cr.

Sr. No.	Particulars	Total Cost in ₹	Incurred Cost in ₹
1	Water Deposit Charges	100,000.00	100,000.00
2	FSI (1st Installment)	39,709,360.00	39,709,360.00
3	Scrutiny Fees	18,000.00	18,000.00
4	Debris Removal	6,600.00	6,600.00
5	Layout Approval Fees	40,000.00	40,000.00
6	Development Cess	6,679,141.00	6,679,141.00
7	Development Cess	16,697,851.00	16,697,851.00
8	Scrutiny Fees	1,517,200.00	1,517,200.00
9	Deposit	77,800.00	77,800.00





Valuation Report Prepared For: SBI / SME Chembur Branch / Sheetal Ekta (5368/2304028) Page 11 of 16

Sr. No.	Particulars	Total Cost in ₹	Incurred Cost in ₹
10	Debris Deposit	45,000.00	45,000.00
11	Development Charges	25,594,200.00	25,594,200.00
12	Open Space Deficiency charges	678,120.00	678,120.00
13	AVS Deficiency	933,500.00	933,500.00
14	Open Space Deficiency for parkin tower	24,700.00	24,700.00
15	Labour Welfare Cess	2,185,400.00	2,185,400.00
16	Department charges	2,679,500.00	2,679,500.00
17	Misc. Development charges	2,584,234.00	2,584,234.00
18	Infrastructure Charges	16,697,851.00	16,697,851.00
19	FSI Deferment scheme	129,253,966.80	
20	Scrutiny Fees	960,700.00	
21	IOA Deposit	26,000.00	
22	50% Fungible Premium MHADA	-11,915,840.00	1. 1.42/14
23	30% Fungible Premium Dharavi	7,149,504.00	-
24	20% Fungible Premium MSRDC	4,766,336.00	
25	Staircase, Lift, Lobby area, Premium	6,919,800.00	
Total		277,260,603.80	116,268,457.00

As per information & challan provided by developer.

#### 5. Architect Cost, RCC & Other Professional Charges:

The total Architect charges of ₹ 1,14,45,648.00 i.e., ₹ 1.14 Cr. is 2.0% of total construction cost building & it is on lower side because developer have their inhouse team for professional work.

The professional charge consists of Architect & Legal which in lower side than the market trend which is in the range of 2% - 5% of Total Construction cost of the project.

#### 6. Administrative Expenses:

Salaries, site overheads, development works, cost of services (including water, electricity, sewerage, drainage, layout roads etc.), cost of machineries and equipment including its hire and maintenance cost, consumables etc. All costs directly incurred to complete the construction of the entire phase of the project registered is estimated 5% of total construction cost Building which comes to ₹ 2,86,14,121.00 i.e., ₹ 2.86 Cr.

The admin charges which in market is in the range of 3% - 5% of Total Construction cost of the project.

#### 7. Marketing Expenses:

Marketing costs directly incurred to complete the construction of the entire phase of the project registered is estimated at 2% of total Sale income from the project which comes to  $\stackrel{?}{\underset{?}{?}}$  2,75,20,165.00 i.e.,  $\stackrel{?}{\underset{?}{?}}$  2.75 Cr. The marketing charge consists of brokerage & commission which in market is in the range of 1% - 3% of Total Sale income of the property.

#### 8. Interest Costs:

The Interest cost for the term loan is  $\stackrel{?}{\underset{?}{?}}$  8,49,00,000.00 i.e.,  $\stackrel{?}{\underset{?}{?}}$  8.49 Cr., which is 7.29% of total project cost. As per information provided by the client.





Valuation Report Prepared For: SBI / SME Chembur Branch / Sheetal Ekta (5368/2304028) Page 12 of 16

#### Observation and Construction: -

Total estimated cost of project i.e., ₹ 116,47,81,928.00 (Rupees One Hundred Sixteen Crore Forty – Seven Lakh Eighty – One Thousand Nine Hundred Twenty – Eighty Only) i.e., ₹ 116.48 Cr. is fair & reasonable.

The project cost is including land premium payable to concern authorities, Fungible FSI Premium, Cost of Construction of rehab & Sale Building, on site expenses including admin & marketing expenses, premiums / charges to be paid to competent authority and Bank interest, etc. we have not independently verified interest cost hence not consider in cost vetting.

As per present sanctioned building plan, permissible built-up area on the said plot is 7,224.37 Sq. M. The rehab cum sale building is presently approved for Basement + Ground Floor + 1st 18th Upper Floors only. The Developer has submitted the concession drawing plan to the competent authority for utilization of total permissible Built-up area and fungible FSI. The rehab cum sale building is presently sanctioned for Basement + Ground Floor + 1st to 33rd Upper Floors only. Estimated cost of entire project of 33rd upper floors is considered.

Total estimated cost of construction of Rehab cum Sales building is ₹ 49,21,73,724.00 i.e., ₹ 49.22 Cr. which comes ₹ 30,000.00 per Sq. M. on construction area for building, cost for deep excavation & shore piling is ₹ 2,46,08,686.00 i.e., ₹ 2.46 Cr. which comes 5% of cost of construction of building and cost for stack parking is ₹ 5,55,00,000.00 i.e., ₹ 5.55 Cr. which comes ₹ 5,00,000.00 per stack parking. Hence, total construction cost (Cost of construction of building + Cost of deep excavation & shore piling + Cost of stack parking) (₹ 49,21,73,724.00 + ₹ 2,46,08,686.00 + ₹ 5,55,00,000.00) = ₹ 57,22,82,410.00 i.e., ₹ 57.23 Cr., which is fair & reasonable considering the present status of project, type & quality of construction & specification of the building materials to be used, height of the structure, amenities to be provided in proposed building.

#### **Assumptions & Remarks-**

- The adequacy of Engineering / Structural design is beyond the scope of our assignment.
- Estimated project completion date is 31/05/2027. The cost is certified based on the
  assumptions that the project will be completed within time frame. Few assumptions are made
  regarding inflation & cost rise etc. during construction period.

Think.Innovate.Create





Valuation Report Prepared For: SBI / SME Chembur Branch / Sheetal Ekta (5368/2304028) Page 13 of 16

#### Photo copy of following document is provided to us & this report should be read along with it:

- ✓ Copy of Developer Agreement dated 27.03.2021 between M/s. Dindoshi Ekta Co-operative Housing Society Ltd. (The Society) and M/s. DGS Township Pvt. Ltd. (The Developers) through registered agreement vide No. BRL-9-4567-2021 dated 27.03.2021.
- ✓ Copy of Deed of Rectification cum Supplementary Agreement dated 29.04.2022 between M/s. Dindoshi Ekta Co-operative Housing Society Ltd. (The Owner) and M/s. DGS Township Pvt. Ltd. (The Developers) through registered agreement vide No. BLR-9-7335-2022 dated 29.04.2022.
- ✓ Copy of Special Power of Attorney through registered agreement vide No. BLR-9-12120-2021 dated 24.09.2021, M/s. Dindoshi Ekta Co-operative Housing Society Ltd. (The Society/ Executants) appoints Mr. Surajdev D. Shukla director of M/s. DGS Township Pvt. Ltd.
- ✓ Copy of Intimation of Approval (IOA) Letter No. MH / EE / B. P. Cell / GM / MHADA 61 / 1216 / 2022 dated 23.12.2022 issued by Maharashtra Housing and Area Development Authority (MHADA).
- ✓ Copy of Approved Plan No. MHADA 61 / 1216 / 2022 dated 23.12.2022 issued by Maharashtra Housing and Area Development Authority (MHADA).

#### Approved upto: Basement + Ground Floor + 1st to 18th Upper Floors

✓ Copy of Building Concession Plan dated 30.07.2022 issued by Maharashtra Housing and Area Development Authority (MHADA):

#### Sanctioned Upto: Basement + Ground Floor + 1st to 33rd Upper Floors


- ✓ Copy of 1st Commencement Certificate No. MH/EE/(BP)/GM/MHADA-61/1216/2023/CC/1/New dated 22.05.2023 valid upto 21.05.2024 issued by Maharashtra Housing and Area Development Authority (MHADA).
- (This CC is endorsed for the work for Top of Plinth level (i.e., height upto 0.30. mts AGL) as per approved IOA dated 23.12.2022)
- ✓ Copy of 2<sup>nd</sup> Further Commencement Certificate No. MH/EE/(BP)/GM/MHADA-61/1216/2023/FCC/1/New dated 20.09.2023 valid upto 21.05.2024 issued by Maharashtra Housing and Area Development Authority (MHADA).

(This CC is Further extended upto Top of 8th upper floor i.e., for building comprising of Basement for Shops with separate internal staircase from above shops + Ground Floor for Shops and parking tower system for Car – Parks + 1st to 3rd floor Offices (Rehab & Sales) + Service Floor (Between 3rd & 4th Floor and) + 4th Floor to 8th Floor for residential users having BUA adm. 3,585.01 Sq. M. with height 33.25 M. as per last approved IOA plans issued vide / no. MH/EE/(B.P.) Cell/GM/MHADA – 61/1216/2022 dated 23.12.2022)

- ✓ Copy of Fire NOC Certificate No. FB/HR/R-4/81 dated 14.07.2022 issued Municipal Corporation of Greater Mumbai, Mumbai Fire Brigade.
- ✓ Copy of No Objection Certificate for Height Clearance NOC ID No. JUHU/WEST/B/010523/735495 dated 30.01.2023 valid upto 29.01.2031 issued by Airports Authority of India.
- ✓ Copy of Geotechnical Investigation Report dated April 2023 issued by M/s. Geocon International Pvt. Ltd.
- ✓ Copy of CA Certificate dated 17.12.2023 issued by M/s. Rajpurohit & Tiwari Chartered Accountants.
- ✓ Copy of RERA Certificate No. P51800051884 dated 07.07.2023 issued by Maharashtra Real Estate Regulatory Authority (MAHRERA).
- ✓ Copy of Sewerage NOC Certificate No. Dy.CWE/SP/125/P/N dated 08.02.2023 issued by Municipal Corporation of Greater Mumbai, Chief Engineer (Sewerage Project).
- ✓ Copy of Hydraulic NOC Certificate No. HE/744/EEWW (P & R)/NOC dated 27.01.2023 issued by Municipal Corporation of Greater Mumbai, Hydraulic Engineer's Department.



## **Actual Site Photographs**

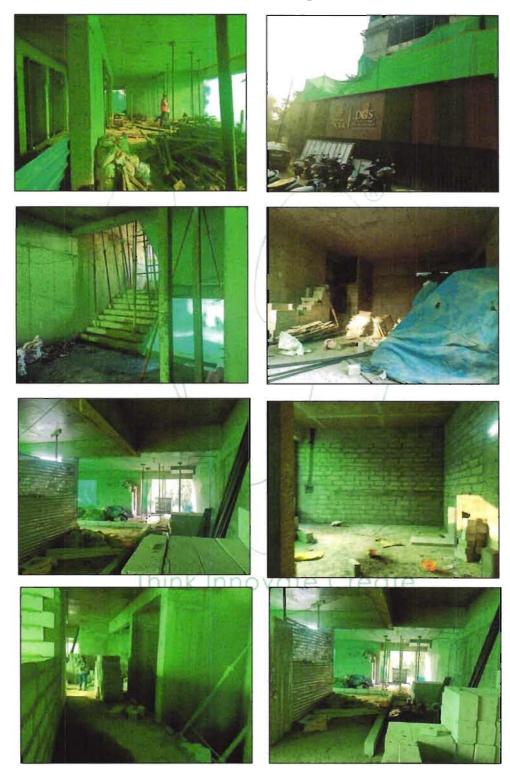




Valuation Report Prepared For: SBI / SME Chembur Branch / Sheetal Ekta (5368/2304028) Page 15 of 16

## **Actual Site Photographs**









Think.Innovate.Create



### Route Map of the property

Site u/r





Latitude Longitude: 19°10'32.1"N 72°51'40.3"E

Note: The Blue line shows the route to site from nearest railway station (Malad – 2.60 Km.)



