



WORK PROGRESS REPORT

Details of the property under consideration:

Name of Project: "Sahil Infra"

"Sahil Infra", Proposed Residential cum Commercial Building bearing on Plot No. 03-R.C., Scheme No. 134, Ward No. 37 (Sai Kripa), Nipania, M.R. 10 Road, Gram Khajrana, Tehsil & District - Indore, Pin Code - 452 010, State - Madhya Pradesh, Country - India

Latitude Longitude: 22°44'48.2"N 75°55'25.9"E

Valuation Done for:

Punjab National Bank MID Corporate Centre

2nd Floor, C 21, Business Park, Opp. Raddison Hotel, Indore,
Pin Code - 452001, State - Madhya Pradesh, Country - India



Indore : 106, 1st Floor, Gold Star Tower, 576, M. G. Road, Opp. TI Mall, Indore - 452 001, (M.P.), INDIA
E-mail : indore@vastukala.org, Tel. : +91 7313510884 +91 9926411111

Our Pan India Presence at :

Mumbai	Aurangabad	Pune	Rajkot
Thane	Nanded	Indore	Raipur
Delhi NCR	Nashik	Ahmedabad	Jaipur

Regd. Office : B1-001, U/B Floor, Boomerang,
Chandivali Farm Road, Andheri (East),
Mumbai - 400 072, (M.S.), INDIA
TeleFax : +91 22 28371325/24
mumbai@vastukala.org

Work Progress Report

The property bearing "Sahil Infra", Proposed Residential cum Commercial Building bearing on Plot No. 03-R.C., Scheme No. 134, Ward No. 37 (Sai Kripa), Nipania, M.R. 10 Road, Gram Khajrana, Tehsil & District - Indore, Pin Code - 452 010, State - Madhya Pradesh, Country - India belongs to **M/s. Sahil Infra**.

Boundaries of the property.

North	20th Road
South	Building
East	Shalimar Apartment
West	Allied Auto Agencies Maurti Authorised Services Station

As per Approved Plan / Sanctioned Letter the construction area as below:

Sr. No.	Floor	FAR Area in Sq. M.	NON - FAR Area in Sq. M.	Total Area in Sq. M.
1	Basement 1	-	2,042.34	2,042.34
2	Basement 2	-	2,042.34	2,042.34
3	Ground Floor	1,247.49	145.16	1,392.65
4	Mezzanine Floor	-	528.51	528.51
5	Parking Floor	-	2,042.34	2,042.34
6	1 st Floor	659.46	341.12	1,000.58
7	2 nd Floor	659.46	315.91	975.37
8	3 rd Floor	659.46	341.12	1,000.58
9	4 th Floor	659.46	315.91	975.37
10	5 th Floor	659.46	341.12	1,000.58
11	6 th Floor	659.46	315.91	975.37
12	7 th Floor	659.46	341.12	1,000.58
13	Terrace	-	91.28	91.28
TOTAL		1,505.04	5,863.71	9,204.18

As per Amended Approved Plan the construction area as below:

Sr. No.	Floor	FAR Area in Sq. M.	NON - FAR Area in Sq. M.	Total Area in Sq. M.
1	Basement 1	-	2,030.20	2,030.20
2	Basement 2	-	2,030.20	2,030.20
3	Ground Floor	1,162.03	64.63	1,226.66
4	Mezzanine Floor	-	1,279.65	1,279.65
5	Parking Floor	-	2,030.20	2,030.20
6	1 st Floor	654.82	471.94	1,126.76
7	2 nd Floor	654.82	471.94	1,126.76
8	3 rd Floor	654.82	471.94	1,126.76
9	4 th Floor	654.82	471.94	1,126.76
10	5 th Floor	654.82	471.94	1,126.76



Indore : 106, 1st Floor, Gold Star Tower, 576, M. G. Road, Opp. TI Mall, Indore - 452 001, (M.P.), INDIA
E-mail : indore@vastukala.org, Tel. : +91 7313510884 +91 9926411111

Our Pan India Presence at :

- | | | | |
|-----------|------------|-----------|--------|
| Mumbai | Aurangabad | Pune | Rajkot |
| Thane | Nanded | Indore | Raipur |
| Delhi NCR | Nashik | Ahmedabad | Jaipur |

Regd. Office : B1-001, U/B Floor, Boomerang, Chandivali Farm Road, Andheri (East), Mumbai - 400 072, (M.S.), INDIA
TeleFax : +91 22 28371325/24
mumbai@vastukala.org

11	6 th Floor	654.82	471.94	1,126.76
12	7 th Floor	654.82	471.94	1,126.76
13	8 th Floor	654.82	471.94	1,126.76
14	9 th Floor	654.82	471.94	1,126.76
15	10 th Floor	654.82	471.94	1,126.76
16	11 th Floor	654.82	471.94	1,126.76
17	12 th Floor	686.51	460.87	1,147.38
18	13 th Floor	428.75	346.64	775.39
19	Terrace	-	194.54	194.54
TOTAL		9,480.31	13,628.27	23,108.58

Hence, for the work progress report, we considered the project upto 7th Residential floor as per sanctioned letter.

The project proposed is under construction, which is considered for project approval. Building consists of proposed 2 Basements + Ground Floor + Mezzanine Floor + Parking Floor + 1st to 7th Upper Residential Floors. The work completion stage is as follows:

Sr. No.	Particulars	Final Percentage	Actual Percentage	Remark
1	RCC Footing/Foundation	5.00	5.00	Completed
2	RCC Plinth	5.00	5.00	Completed
3	Full Building RCC	40.00	40.00	Basement 1 & 2, Ground Floor, Mezzanine Floor, Parking Floor, 1 st to 7 th Upper Floor Slab work is completed
4	Internal Brick work	7.00	7.00	Basement 1 & 2, Ground Floor, Mezzanine Floor, Parking Floor, 1 st to 7 th Upper Floor Brick work is completed
5	External Brickwork	7.00	7.00	
6	Internal plastering	3.50	3.50	Basement 1 & 2, Ground Floor, Mezzanine Floor, Parking Floor, 1 st to 7 th Upper Floor plastering work is completed
7	External plastering	3.50	3.50	
8	Doors & Windows	5.00		
9	Flooring, Tiling, Kitchen Platform	10.00		
10	Internal painting	1.50		
11	External painting	1.50		
12	Electrification, plumbing & Sanitary installation	5.00		
13	Lift Installation	2.00		
14	Passage, Staircase & Lobby development	2.00		
15	External developments / Final finishing work	2.00		
Total		100.00	71.00	

As per Cost Vetting Report Ref. No. Vastu/SBI/Mumbai/08/2022/26145/42374, 27/14-441-PYM Dated 27.08.2022, Estimate Total Cost of Construction of Building was ₹ 30,13,57,800.00.

As per site inspection dated 15.12.2023 work completion percentage is 71.00% and cost of construction as on date is (₹ 30,13,57,800.00 X 71.00%) = ₹ 21,39,64,038.00



The report of the property is based on the site visit dated 15.12.2023 & documents produced by the concern. Construction work going as per approved plan only. Legal aspects have not been taken into considerations while preparing this report.

As per Amend Approved Plan, the project cost of construction will increase and hence, so revised sanctioned of the project will be considered for the further work progress report.

Hence certified

For Vastukala Consultants (I) Pvt. Ltd.

**Manoj
Chalikwar**

Digitally signed by Manoj
Chalikwar
DN: cn=Manoj Chalikwar,
o=Vastukala Consultants (I) Pvt.
Ltd., ou=Mumbai,
email=manoj@vastukala.org, c=IN
Date: 2023.12.22 16:09:26 +05'30'

Manoj B. Chalikwar
Registered Valuer
Chartered Engineer (India)
Reg. No. CAT-I-F-1763
PNB Emp. No. ZO: SAMD:1138

Think.Innovate.Create



Think.Innovate.Create







Vastukala Consultants (I) Pvt. Ltd.

An ISO 9001:2015 Certified Company









www.vastukala.org











Actual Site Photographs

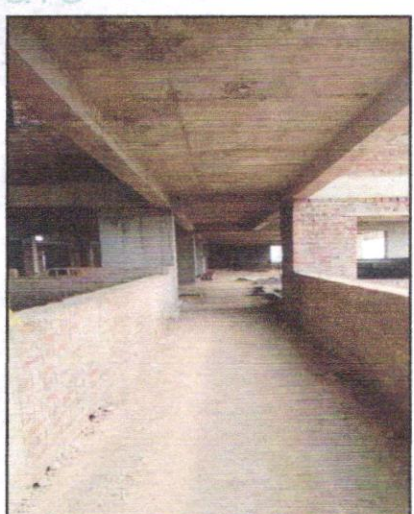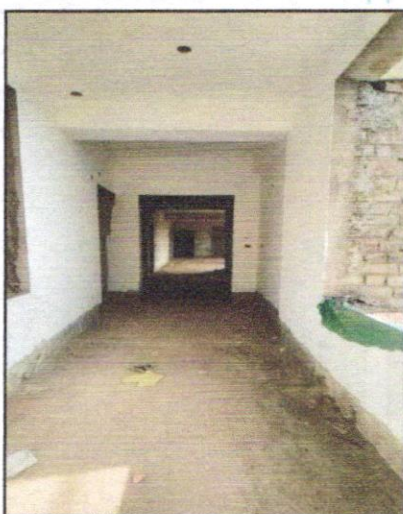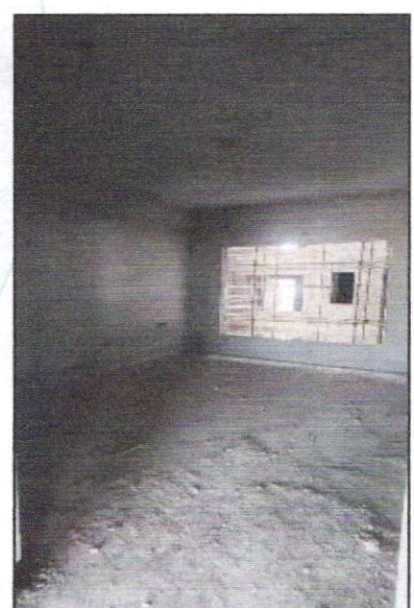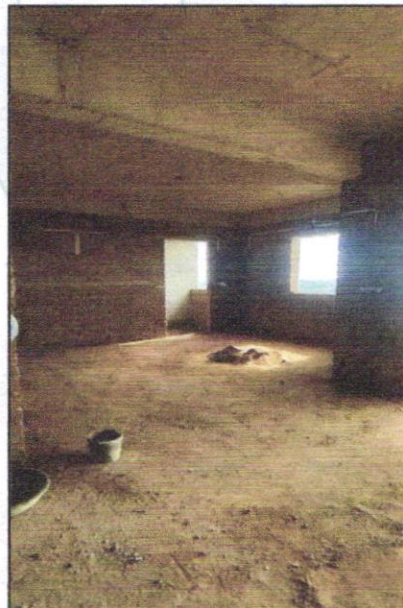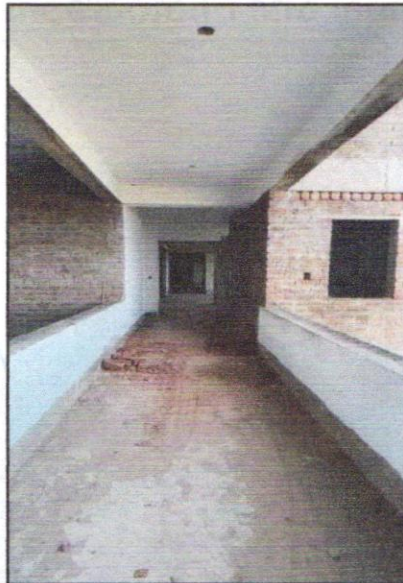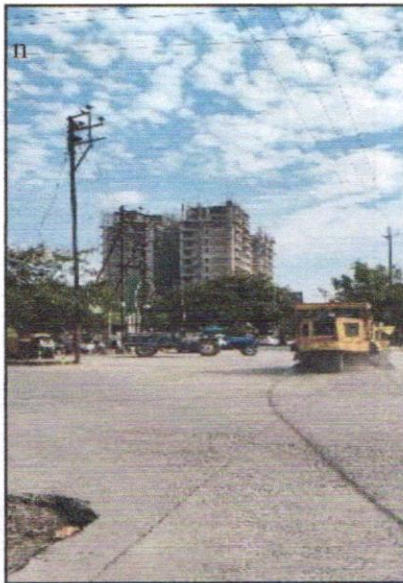

Actual Site Photographs

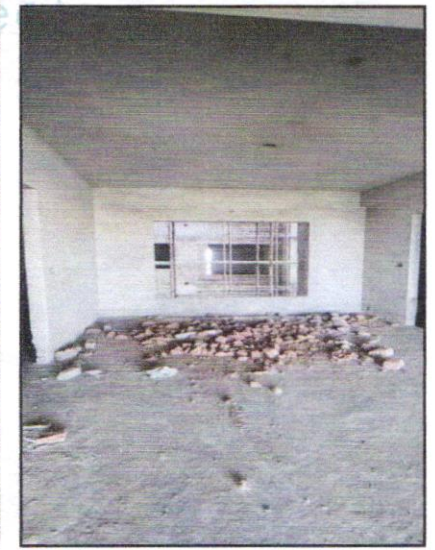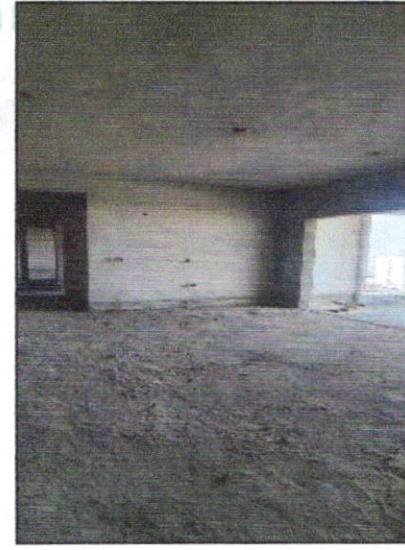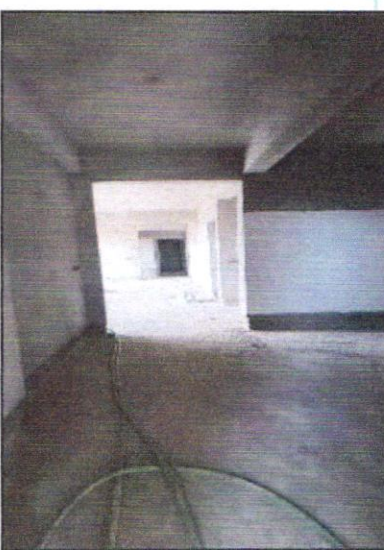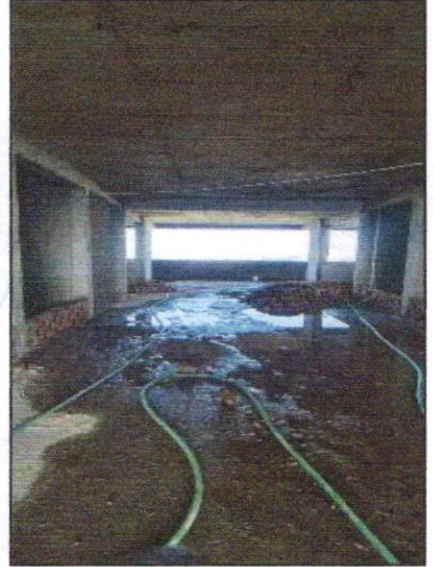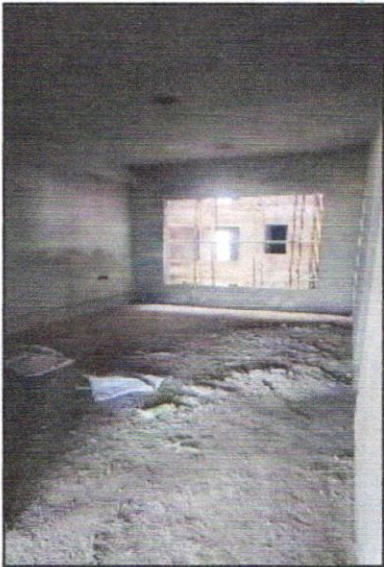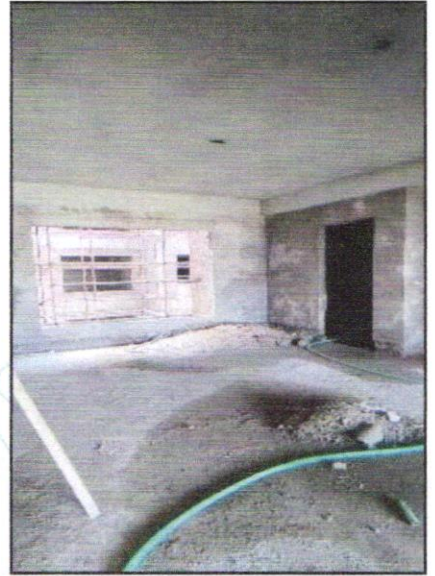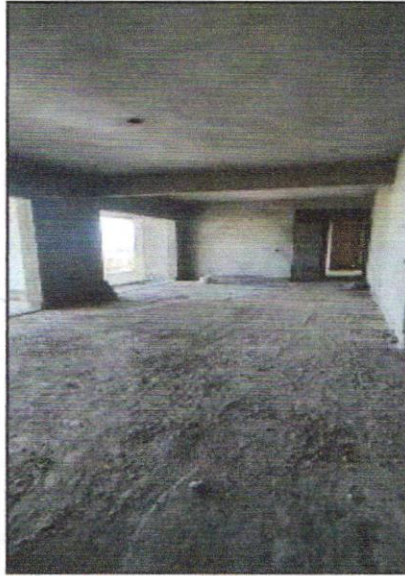
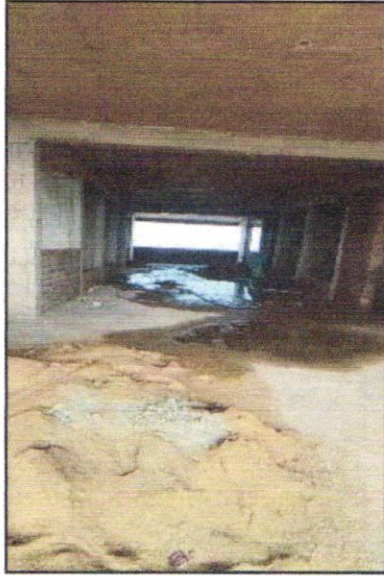


Actual Site Photographs

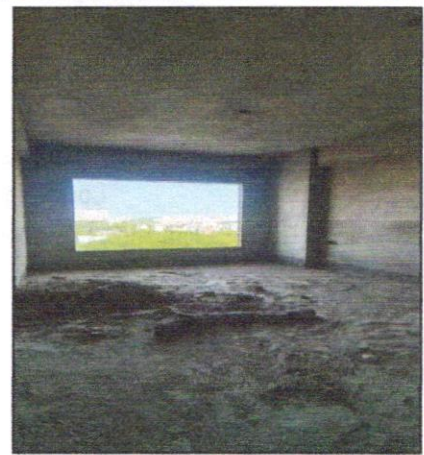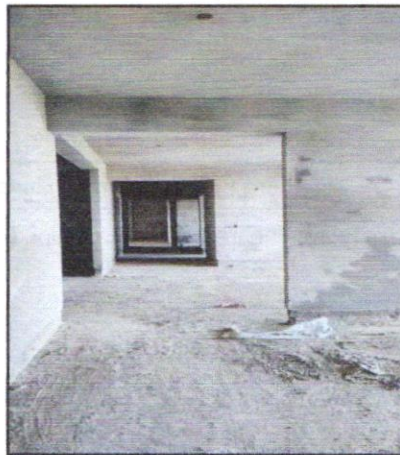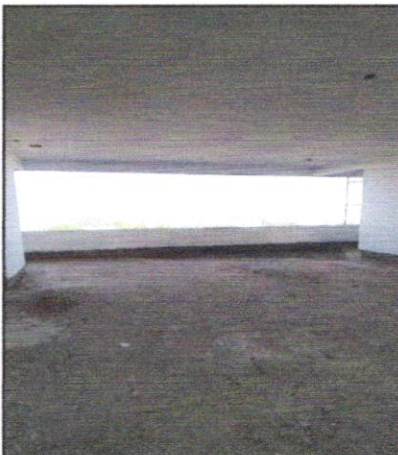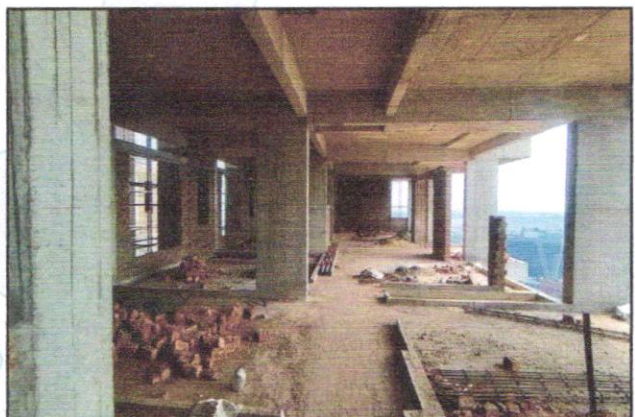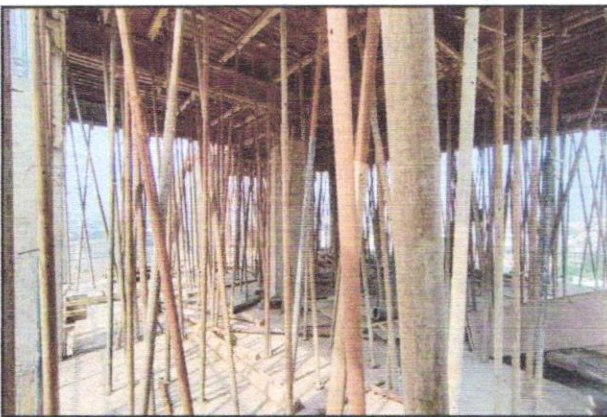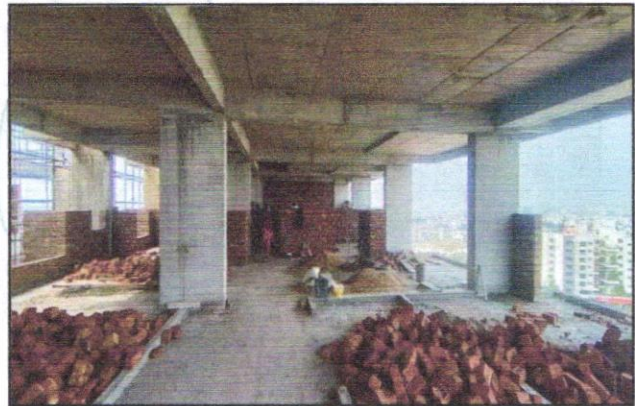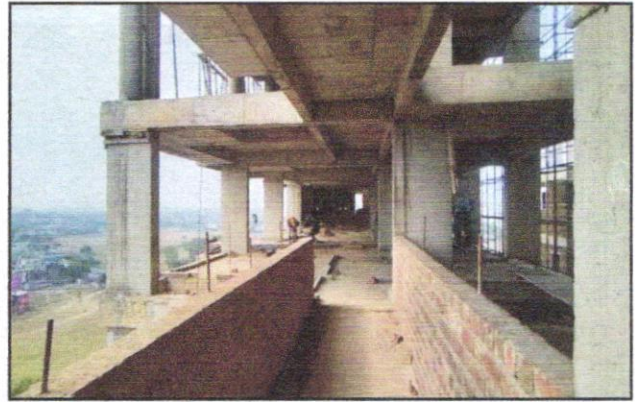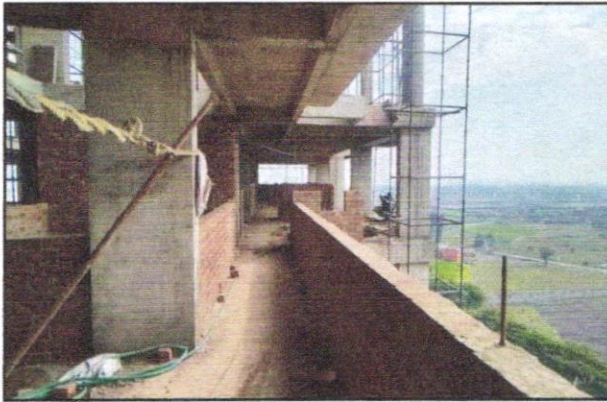

Route Map of the property

Site u/r

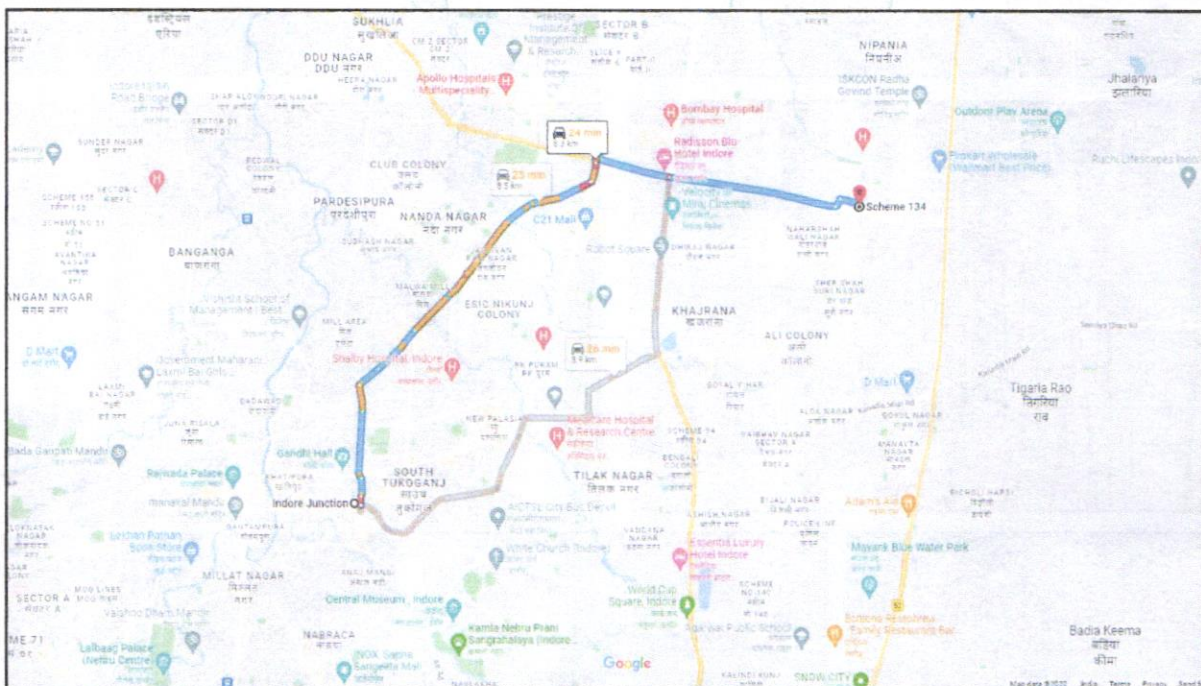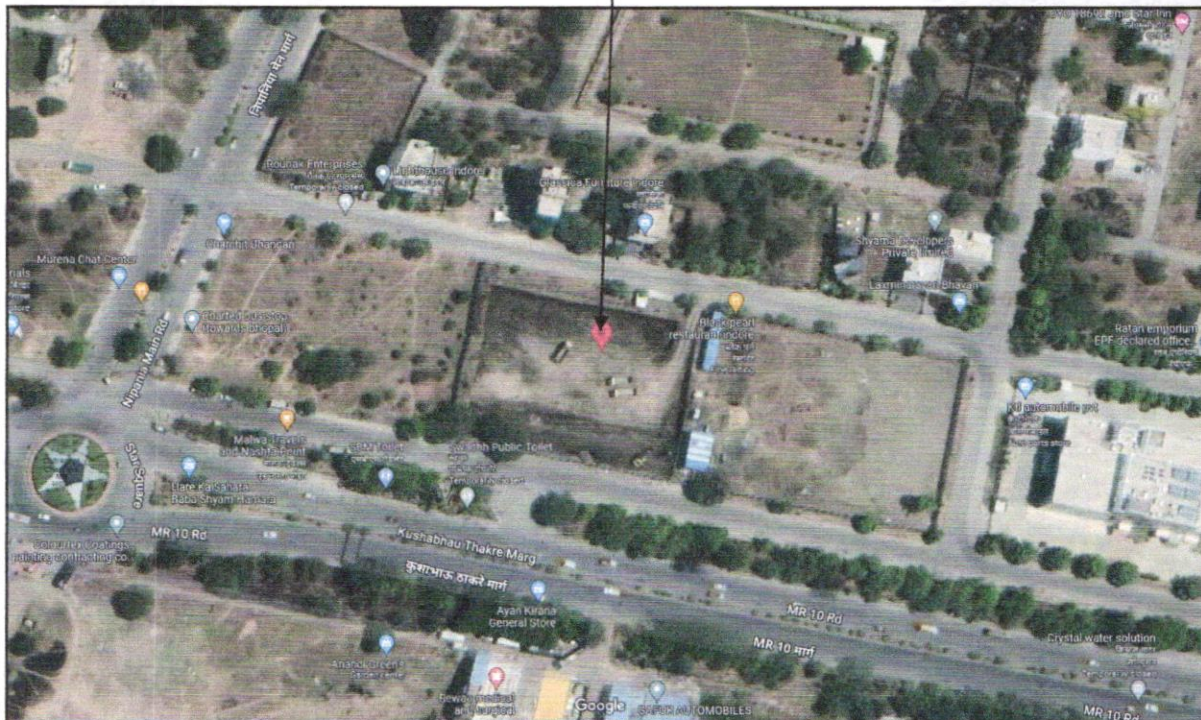

Longitude Latitude - 22°44'48.2"N 75°55'25.9"E

Note: The Blue line shows the route to site from nearest Railway Station (Indore Junction – 8.3 KM.)
