

1st LENDER'S INDEPENDENT ENGINEER REPORT



Details of the property under consideration:

Name of Project: Decent Life Space 2 (Wing B named as Skyrise)

"Decent Life Space 2 (Wing B named as Skyrise)", Proposed Residential Group Housing Scheme on land bearing S. No. 70/A, H. No. 1 & S. No. 51/A, H. No. 5, C. T. S. No. 2163, 16 (Pt) & 192 (Pt), Palghar – Manor Road, Village – Palghar, Taluka & District – Palghar, Pin Code – 401 404, State – Maharashtra, Country – India

Latitude Longitude: 19°42'17.8"N 72°46'15.9"E

Intended User:

State Bank of India




SME Centre Borivali (West) Branch

SME Centre Borivali (15521) 101, 1st Floor, Landmark Building, S. V. Road, Near Petrol Pump,
Borivali (West), Mumbai – 400 092, State – Maharashtra, Country – India.



Our Pan India Presence at :

- | | | | |
|---|--|---|--|
|  Mumbai |  Aurangabad |  Pune |  Rajkot |
|  Thane |  Nanded |  Indore |  Raipur |
|  Delhi NCR |  Nashik |  Ahmedabad |  Jaipur |

-  **Regd. Office :** B1-001, U/B Floor, Boomerang, Chandivali Farm Road, Andheri (East), **Mumbai - 400 072, (M.S.), INDIA**
-  TeleFAX : +91 22 28371325/24
-  mumbai@vastukala.org

LIE Report Prepared for: SBI/ SME Centre Borivali (West) Branch / Decent Life Space 2 (7271/2305804) Page 2 of 19

Vastu/SBI/Mumbai/03/2024/7271/2305804
29/14-552-PYU
Date: - 28.03.2024

FIRST LENDER'S INDEPENDENT ENGINEER REPORT

To,

State Bank of India

SME Centre Borivali (West) Branch,
SME Centre Borivali (15521),
101, 1st Floor, Landmark Building,
S. V. Road, Near Petrol Pump,
Borivali (West), Mumbai – 400 092,
State – Maharashtra, Country – India

Subject: Construction of Proposed Residential Group Housing Scheme on land bearing S. No. 70/A, H. No. 1 & S. No. 51/A, H. No. 5, C. T. S. No. 2163, 16 (Pt) & 192 (Pt), Palghar – Manor Road, Village – Palghar, Taluka & District – Palghar, Pin Code – 401 404, State – Maharashtra, Country – India

Ref: You're Request for Lenders Independent Engineer Report of under Construction Building.

Dear Sir,

1. As per your instruction, we have inspected the under construction residential building situated on plot bearing S. No. 70/A, H. No. 1 & S. No. 51/A, H. No. 5, C. T. S. No. 2163, 16 (Pt) & 192 (Pt), Palghar – Manor Road, Village – Palghar, Taluka & District – Palghar, Pin Code – 401 404, State – Maharashtra, Country – India which is being developed by M/s. Adinath Associates in order to give the physical progress of work completion as on 28/02/2024 as per amended approved plan dated 25.03.2022.
2. While Certifying cost as per plinth area calculation as on 28/02/2024, various important factors such as type & Quality of proposed construction, Specification of building material to be used, grade of the building, height, lead & lift condition, current market price of similar type etc. were given due consideration.
3. As per cost incurred certificate issued by **CA Certificate actual total expenditure occurred as on 31/12/2023 is ₹ 7.53 Cr.**
4. **Overall physical progress of the building construction as on 28/02/2024 is 32.06% as per physical site inspection.**



www.vastukala.org

Our Pan India Presence at :

- | | | | |
|-----------|------------|-----------|--------|
| Mumbai | Aurangabad | Pune | Rajkot |
| Thane | Nanded | Indore | Raipur |
| Delhi NCR | Nashik | Ahmedabad | Jaipur |

- Regd. Office :** B1-001, U/B Floor, Boomerang, Chandivali Farm Road, Andheri (East), Mumbai - 400 072, (M.S.), INDIA
- TeleFax : +91 22 28371325/24
mumbai@vastukala.org



DECLARATION

- a. The information furnished in the report is based on our site visit Dated 28/02/2024 & Document Provided by Client.
- b. Shailesh Wani & Co. Cost Vetting Report of the project Ref. No. SBI / SME Borivali / 314 dated 03.01.2023.
- c. Shailesh Wani & Co. Valuation Report of the project Ref. No. SBI / SME Borivali / 313 dated 03.01.2023.
- d. I have no direct and indirect interest in the property examined for report.
- e. I have not been found guilty of misconduct in my professional capacity.®

For VASTUKALA CONSULTANTS (I) PVT. LTD.

Director

Sharadkumar B. Chalikwar
Govt. Reg. Valuer
Chartered Engineer (India)
Reg. No. (N) CCIT/1-14/52/2008-09

Auth. Sign.

Think.Innovate.Create

1. Purpose & Methodology


- State Bank of India Banks and financial institutions require monitoring & an independent review of the progress of the sanctioned projects

VC IPL undertakes such study to independently review the progress of the project and put forward a comprehensive analysis

1.1. Advantages:

- ✓ Assurance on present practices
- ✓ Identification of risk
- ✓ Analyzing the performance of third parties
- ✓ Recommendations

1.2. The Methodology

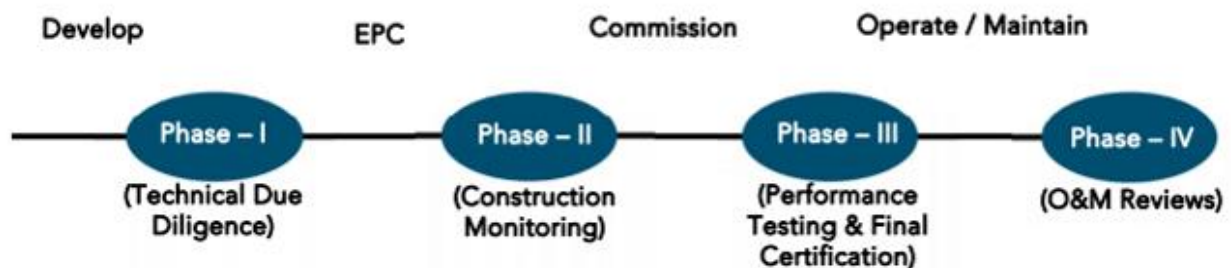

Think.Innovate.Create

FIRST LENDER'S INDEPENDENT ENGINEER REPORT OF

"Decent Life Space 2 (Wing B named as Skyrise)"

"Decent Life Space 2 (Wing B named as Skyrise)", Proposed Residential Group Housing Scheme on land bearing S. No. 70/A, H. No. 1 & S. No. 51/A, H. No. 5, C. T. S. No. 2163, 16 (Pt) & 192 (Pt), Palghar – Manor Road, Village – Palghar, Taluka & District – Palghar, Pin Code – 401 404, State – Maharashtra, Country – India

Latitude Longitude: 19°42'17.8"N 72°46'15.9"E

NAME OF DEVELOPER: M/s. Adinath Associates

Pursuant to instructions from State Bank of India, SME Centre Borivali (West) Branch, Borivali we have duly visited, inspected, surveyed & assessed the above said property on **28th February 2024** to determine the fair & reasonable market value of the said property/project as on Quarter ending **31st December 2023** for LIE purpose.

1. Location Details:

Proposed Residential Group Housing Scheme on land bearing S. No. 70/A, H. No. 1 & S. No. 51/A, H. No. 5, C. T. S. No. 2163, 16 (Pt) & 192 (Pt), Palghar – Manor Road, Village – Palghar, Taluka & District – Palghar, Pin Code – 401 404. It is about 1.60 Km. travelling distance from Palghar Railway station. Surface transport to the property is by buses, taxis & private vehicles. The property is in developed locality. All the amenities like shops, banks, hotels, markets, schools, hospitals, etc. are all available in the surrounding locality. The area is higher middle class & developed.

2. Developer Details:

Name of Developer	M/s. Adinath Associates
Project Rera Registration Number	N. A.
Registered office address	46, Aminabad Building, 7 th Floor, Aga Hall, Nesbit Road, Mazgaon, Mumbai, Pin Code – 400 010, State – Maharashtra, Country – India
Contact details	Contact Person: Mr. Jeet Mehta Mobile No. +91 78781 13580 Mr. Brajalan Yadav (Accountant) Mobile No. +91 83297 74754

E – mail ID and website

3. Boundaries of the Property:

Direction	Particulars
On or towards North	Residential Chawl
On or towards South	Under Construction Building
On or towards East	Open Plot
On or towards West	Internal Road / Western Railway Track



Our Pan India Presence at :

Mumbai Aurangabad Pune Rajkot
Thane Nanded Indore Raipur
Delhi NCR Nashik Ahmedabad Jaipur

Regd. Office : B1-001, U/B Floor, Boomerang, Chandivali Farm Road, Andheri (East), Mumbai - 400 072, (M.S.), INDIA
TeleFax : +91 22 28371325/24
mumbai@vastukala.org

2. Introduction

As per Information on site M/s. Adinath Associates has acquired land by Conveyance Deed dated 17.12.2012 registered vide No. 3340/2013 admeasuring total area is 2405.00 Sq. M. bearing Survey No. 51/A/5 & 70/A/1. For the Proposed Residential Building.

3. Area Statement:

3.1. Land:

Date	Particular	Area in Sq. M.
18.02.2016	Survey No. 51/A/5	32,000.00
	Survey No. 70/A/1	76,000.00
TOTAL		1,08,000.00

- Copy of Legal Title Report dated 07.04.2022 issued by Adv. Avataru R. Gupta.

3.2. Building Area As per Approved Plan:

AREA STATEMENT		
1	Area of plot	
	(Minimum area of a, b, c, to be considered)	
	a) As per ownership [document (7/12, CTS extract)]	10800
	b) as per measurement sheet	9140
	c) as per site	NILL
2	Deductions For	
	(a) Proposed D.P./D.P. Road widening Area/Service Road / Highway Widening	1527.74
	(b) Service Road Area (Reservation Area)	1174.01
	© Not in Possession area	NILL
	(Total a + b + c)	2701.75
3	Balanced area of plot (1-2)	6438.25
4	Amenity Space (if applicable)	NILL
	(a) Required -	
	(b) Adjustment of 2 (b), if any -	
	(c) Balanced Proposed -	NILL
5	Net Plot Area (3-4 (c))	6438.25
6	Recreational Open Space	
	(a) Required -	703.84
	(b) Proposed -	704.02
7	Internal Road area	NILL
8	Plotable Area (if applicable)	
9	Built up area with reference to Basic F.S.I as per front road width	
	(Sr. No. 5 x Basic FSI)	7082.08
10	Addition of FSI on payment of premium	
	(a) Maximum permissible premium FSI - based on road with / TOD Zone. (9140.00 x 0.30)	2742

AREA STATEMENT		
	(b) Proposed FSI on payment of premium	NILL
11	In-situ FSI/TDR Loading	NILL
	(a) In-Situ area against D.P. Road & Reservation (2.0 x Sr. No. 2 (a)), if any	5403.5
	(b) In-situ area against Amenity Space if Handed over [2.00 or 1.85 x Sr. No. 4 (b) and / or (c)]	NILL
	(c) TDR Area	NILL
	(d) Total in-situ / TDR loading proposed (11 (a) + (b) + (c))	5403.5
12	Total Built up area with reference to Basic F.S.I & Proposed FSI on payment of Premium (9 + 10a)	15227.58
13	Total old approval Built up Area	3143.16
14	Total (12-13)	12084.42
15	Additional FSI area under Chapter No. 7	NILL
16	Total entitlement of FSI in the proposal.	
	(a) [9 + 10(a) + 11(d)] or 12 Whichever is applicable	15227.58
	(b) Ancillary Area FSI upto 60% with payment of charges (0.60%) (12084.42 X 0.60)	7250.65
	(c) Total entitlement (a + b)	22478.22
17	Maximum utilization limit of FSI (building potential) Permissible as per Road width {(as per Regulation No. 6.1 or 6.2 or 6.3 or 6.4 as applicable) X 1.6	
18	Total Built-up Area in proposal. (Excluding area at Sr. No. 17b)	2.24
	(a) Existing Built -up area.	3143.16
	(b) Proposed Built-up Area (As per 'P-Line')	16791.62
	(c) Total (a + b)	19934.78
19	F.S.I. Consumed (18/16) (should not be more than Serial no.14 above)	1.589
20	Total proposed Built-up Area in Proposal (For Payment Calculation)	
	(a) Proposed Built-up Area with Reference to Basic F.S.I.	7082.08
	(b) Proposed Built-up Area with Reference To premium F.S.I.	2742
	(c) Proposed Built-up Area with Reference To D.P Road & reservation F.S.I.	5403.5
	(d) Proposed Built-up Area with Reference to Ancillary F.S.I.	4707.2
	Total	19934.78
	TOTAL BALANCE BUILT UP AREA	2543.45

Floor wise Built – Up Area Statement as per amended approved building plan is as below –

Sr.	Floor	Built Up Area in Sq. M.
1	Ground Floor	208.96
2	1st Floor	557.71
3	2nd Floor	589.66
4	3rd Floor	589.66
5	4th Floor	589.66
6	5th Floor	589.66
7	6th Floor	589.66
8	7th Floor	589.66
9	8th Floor	558.03
10	9th Floor	589.66
11	10th Floor	589.66
12	11th Floor	589.66
13	12th Floor	589.66
14	13th Floor	558.03
15	14th Floor	589.66
16	15th Floor	589.66
17	16th Floor	589.66
TOTAL		9,548.31

4. List of Approvals:

1. Copy of Approved Plan No. B. V. 162 dated 08.08.2018 issued by Palghar Nagar Parishad.
Approved upto: Floor + 1st to 7th Upper Floor.
2. Copy of Amend Approved Plan No. NVV 1502 dated 25.03.2022 issued by Palghar Nagar Parishad.
Approved upto: Floor + 1st to 16th Upper Floor.
3. Copy of Commencement Certificate No. PNP/NRV/1502/2021-2022 dated 25.03.2022 issued by Palghar Nagar Parishad.
(This CC is endorsed for the work upto Ground Floor + 1st to 16th Upper Floor)

5. LEVEL OF COMPLETION:

5.1. Construction of Building

Sr. No	Floor No.	Construction Area in Sq. M.	Completed Area in Sq. M.	Percentage of work completed	Work Completion as on 28.02.2024
1	Excavation & Shore Piling			100%	Work is Completed
2	Ground Floor	208.96	208.96	50%	Slab work is completed
3	1st Floor	557.71	557.71	65%	Slab work, Block work, Plaster work & gypsum work is completed
4	2nd Floor	589.66	589.66	65%	Slab work, Block work, Plaster work & gypsum work is completed
5	3rd Floor	589.66	589.66	65%	Slab work, Block work, Plaster work & gypsum work is completed
6	4th Floor	589.66	589.66	60%	Slab work, Block work, Plaster work is completed, Gypsum work is in progress
7	5th Floor	589.66	589.66	50%	Slab work is completed
8	6th Floor	589.66	589.66	50%	Slab work is completed
9	7th Floor	589.66	589.66	50%	Slab work is completed
10	8th Floor	558.03	558.03	50%	Slab work is completed
11	9th Floor	589.66	589.66	50%	Slab work is completed
12	10th Floor	589.66			
13	11th Floor	589.66			
14	12th Floor	589.66			
15	13th Floor	558.03			
16	14th Floor	589.66			
17	15th Floor	589.66			
18	16th Floor	589.66			
19	Terrace Floor & OHT & LMR Area				
Total		9,548.31	5,452.32	32.06%	

5.2. External Development

Particulars	Work Completion as on 28.02.2024
Meter Room	
Sewage Treatment Plant	
24 X 7 Water Supply	
Landscaping & Tree Planting	
Water Conversation, rain water harvesting	
Open Parking	
Storm Water Drains	
Closed Car Parking	
Fire Sprinklers	

6. Details of the Project as Financed By SBI:

6.1. Estimate of the project

Project expenses	Cost as per CA Certificate & Cost Vetting Report in ₹ Cr.
Land Cost	0.78
Construction Cost of Building & external development cost	28.44
Approval Cost	0.79
Professional, Admin & Marketing Cost	1.58
Contingency Cost	1.70
Interest Cost	3.85
Total Cost	64.54

Note: -

6.1. Project Cost: (as per C.A. Certificate)

Particulars	Incurred Cost (In ₹ Cr.) till 31.12.2023 dated 07.01.2024 by M/s. Zenith M Jain & Co.
Land Cost	0.78
Construction Cost of Building & external development cost	5.95
Approval Cost	0.64
Professional, Admin & Marketing Cost	0.16
Contingency Cost	-
Interest Cost	-
Total	7.53

6.2. Cost of Construction as on 28th February 2024:**6.2.1. Construction Cost of Building:**

Sr.	Floor	Built Up Area in Sq. M.	Completed Area in Sq. M.	Rate per Sq. M.	Full Value after completion	% of work completed	Actual Expenditure till date in ₹
1	Ground Floor	208.96	208.96	30,000.00	62,68,800.00	50%	31,34,400.00
2	1st Floor	557.71	557.71	30,000.00	1,67,31,300.00	65%	1,08,75,345.00
3	2nd Floor	589.66	589.66	30,000.00	1,76,89,800.00	65%	1,14,98,370.00
4	3rd Floor	589.66	589.66	30,000.00	1,76,89,800.00	65%	1,14,98,370.00
5	4th Floor	589.66	589.66	30,000.00	1,76,89,800.00	60%	1,06,13,880.00
6	5th Floor	589.66	589.66	30,000.00	1,76,89,800.00	50%	88,44,900.00
7	6th Floor	589.66	589.66	30,000.00	1,76,89,800.00	50%	88,44,900.00
8	7th Floor	589.66	589.66	30,000.00	1,76,89,800.00	50%	88,44,900.00
9	8th Floor	558.03	558.03	30,000.00	1,33,92,720.00	50%	66,96,360.00
10	9th Floor	589.66	589.66	30,000.00	1,76,89,800.00	50%	88,44,900.00
11	10th Floor	589.66		30,000.00	1,76,89,800.00		
12	11th Floor	589.66		30,000.00	1,76,89,800.00		
13	12th Floor	589.66		30,000.00	1,76,89,800.00		
14	13th Floor	558.03		30,000.00	1,33,92,720.00		
15	14th Floor	589.66		30,000.00	1,76,89,800.00		
16	15th Floor	589.66		30,000.00	1,76,89,800.00		
17	16th Floor	589.66		30,000.00	1,76,89,800.00		
TOTAL		9,548.31	5,452.32		27,97,52,940.00	32.06%	8,96,96,325.00

6.2.2. External Development:

Particulars	Cost as per Cost vetting Report dated 03.01.2023	Percentage of work completed	Actual Expenditure till date in ₹
Meter Room	2,00,000.00		
Sewage Treatment Plant	12,00,000.00		
24 X 7 Water Supply	10,00,000.00		
Landscaping & Tree Planting	6,00,000.00		
Water Conversation, rain water harvesting	5,00,000.00		
Open Parking	3,00,000.00		
Storm Water Drains	4,00,000.00		
Closed Car Parking	2,00,000.00		
Fire Sprinklers	2,00,000.00		
TOTAL	46,00,000.00		

Note: Details of work completed is as per site visit dated 28.02.2024 but LIE report is prepared for quarter ending on 31st December 2023.

7. Means of Finance:

Sr. No.	Particulars	Exp. Cumulative (Cr.)
1.	Equity share capital / Quassi Loan from Promoter	1.50
2.	Unsecured Loan	1.30
3.	Bank Loan Amount	1.86
4.	Sales (Advance from customer)	3.47
	Total	8.14

The Details of the Means of Finance are provided by Client as on 31.12.2023.

8. Mandatory Arrangements:

Sr. No.	Particulars	Status
a.	Rainwater Harvesting	To be executed after RCC Structure
b.	Firefighting System	To be executed after RCC Structure
c.	Solid Waste Management	To be executed after RCC Structure

9. Quality of Construction:

Sr. No.	Particulars	Status
a.	Soundness of Structures	Executing as per approved Structural Design
b.	Look of Structures	Good
c.	Quality of Material Used	Good
d.	Safety Measures for Construction/labour	Taken Care by Contractor

10. Schedule V/s. Actual Progress:

Activity	Date of Implementation	Date of Completion	Status
Land			Completed
Development of Land			Completed
Foundation Work			Completed
Ground Floor Slab			Slab work is Completed
1st Floor Slab			Slab work is Completed
2nd Floor Slab			Slab work is Completed
3rd Floor Slab			Slab work is Completed
4th Floor Slab			Slab work is Completed
5th Floor Slab			Slab work is Completed
6th Floor Slab			Slab work is Completed
7th Floor Slab			Slab work is Completed
8th Floor Slab			Slab work is Completed
9th Floor Slab			Slab work is Completed
10th Floor Slab			
11th Floor Slab			
12th Floor Slab			
13th Floor Slab			
14th Floor Slab			
15th Floor Slab			
16th Floor Slab			
Block work / Internal Plaster work			1st to 4th floor blockwork is completed

Activity	Date of Implementation	Date of Completion	Status
Terrace Parapet wall / Overhead water tank / Lift Machine room / compound wall / External Plaster work			
Electric Work			Work is in progress
Water Proofing			Work is in progress
Plumbing Work			Work is in progress
Tiling / Marble Flooring			
Door Frames			
Window Installation			
Staircase Flooring			
Staircase Railing			
Refuge Area Flooring			
Internal Painting			
External Painting			
Lift Work			
Fire Fighting Installation			
Stack Parking			
CP Fitting & Sanitary Work			
Final Finishing & Fitting			

11. Action initiated to complete the project in time:

For Sale Building: Till 9th Slab work is completed & 10th floor slab work is in progress.

12. Comments related to cost overrun if any:

The cost of Sales Building is ₹ 37.12 Cr.

13. Balance investment required for completion of project:

We opinion amount of ₹ 29.60 Cr. Will be required to complete the Project.

14. Mandatory Approval Status:

Sr. No.	Particulars	Name of Department	Status	Order Details
1	IOD of Building	Palghar Nagar Parishad	Obtained and available at site	No. B. V. 162 dated 08.08.2018 Approved upto: Floor + 1 st to 7 th Upper Floor.
1A	1 st Amended	Palghar Nagar Parishad	Obtained and available at site	No. NVV 1502 dated 25.03.2022 Approved upto: Floor + 1 st to 16 th Upper Floor.
2A	First C.C.	Palghar Nagar Parishad	Obtained and available at site	No. PNP/NRV/1502/2021-2022 dated 25.03.2022 (This CC is endorsed for the work upto Ground Floor + 1st to 16th Upper Floor)
3	Occupancy	Palghar Nagar Parishad	Pending (Project is not completed)	

15. Status Insurance Coverage:

Information not provided

16. Assumptions & Remarks:

- The adequacy of Engineering / Structural design is beyond the scope of our assignment.
- Estimated project completion date is 31/12/2026. The cost is certified based on the assumptions that the project will be completed within period. Few assumptions were made regarding inflation & cost rise etc. during construction period.

For VASTUKALA CONSULTANTS (I) PVT. LTD.

Director

Sharadkumar B. Chalikwar

Govt. Reg. Valuer

Chartered Engineer (India)

Reg. No. (N) CCIT/1-14/52/2008-09

Auth. Sign.

Think.Innovate.Create

About the Project:

1. Introduction	
a) Project Name (With Address & Phone Nos.)	"Decent Life Space 2 (Wing B named as Skyrise)", Proposed Residential Group Housing Scheme on land bearing S. No. 70/A, H. No. 1 & S. No. 51/A, H. No. 5, C. T. S. No. 2163, 16 (Pt) & 192 (Pt), Palghar – Manor Road, Village – Palghar, Taluka & District – Palghar, Pin Code – 401 404, State – Maharashtra, Country – India <u>Contact Person:</u> Mr. Jeet Mehta Mobile No. +91 78781 13580 Mr. Brajlan Yadav (Accountant) Mobile No. +91 83297 74754
b) Purpose of Valuation	As per request from State Bank of India, SME Centre Borivali (West) Branch, Borivali to assess cost of the Project for LIE purpose.
c) Date of Inspection of Property	28.02.2024
d) Date of LIE Report	28.03.2024
e) Name of the Developer of Property (in case of developer built properties)	M/s. Gillani Hospitality Pvt. Ltd. 46, Aminabad Building, 7 th Floor, Aga Hall, Nesbit Road, Mazgaon, Mumbai, Pin Code – 400 010, State – Maharashtra, Country – India
2. Physical Characteristics of the Property	
a) Location of the Property	"Decent Life Space 2 (Wing B named as Skyrise)", Proposed Residential Group Housing Scheme on land bearing S. No. 70/A, H. No. 1 & S. No. 51/A, H. No. 5, C. T. S. No. 2163, 16 (Pt) & 192 (Pt), Palghar – Manor Road, Village – Palghar, Taluka & District – Palghar, Pin Code – 401 404, State – Maharashtra, Country – India
Brief description of the property	
TYPE OF THE BUILDING	
1. Residential Building	
No. of Floors	Ground Floor + 1st to 16th Upper Floor.
Building type	Residential building
Residential Building work is given on contract based for RCC contract. Developer has grant to the contractor do the work of construction and completion includes Concrete work, Reinforcement work, Masonry, Internal Plaster, External Plaster and other miscellaneous work such as repairing, joints b/w concrete and masonry surface, etc. Bill must be paid on measurement of construction area exclusive of Steel, Cement & other construction material. Lift & lift installation contract is not finalized till now. Firefighting work contract is not finalized.	
PROPOSED DATE OF COMPLETION & FUTURE LIFE:	
Expected completion date as per developer is 31 st December 2026	
Nearby landmark	-
Postal Address of the Property	"Decent Life Space 2 (Wing B named as Skyrise)", Proposed Residential Group Housing Scheme on land bearing S. No. 70/A, H. No. 1 & S. No. 51/A, H. No. 5, C. T. S. No. 2163, 16 (Pt) & 192 (Pt), Palghar – Manor Road, Village – Palghar, Taluka & District – Palghar, Pin Code – 401 404,

	State – Maharashtra, Country – India	
Area of the plot/land (Supported by a plan)	Plot Area: 1,08,000.00 Sq. M.	
Type of Land: Solid, Rocky, Marsh land, reclaimed land, Water-logged, Land locked.	Solid land	
Independent access/approach to the property etc.	Yes	
Google Map Location of the Property with a neighborhood layout map	Provided	
Details of roads abutting the property		
Description of adjoining property	Located in Middle-class locality	
Plot No. Survey No.	S. No. 70/A, H. No. 1 & S. No. 51/A, H. No. 5, C. T. S. No. 2163, 16 (Pt) & 192 (Pt)	
Ward/Village/Taluka	Village – Palghar, Taluka – Palghar	
Sub-Registry/Block	Palghar	
District	District – Palghar	
b) Boundaries of the Plot		
	As per Agreement	Actual
North	Information not available	Residential Chawl
South	Information not available	Under Construction Building
East	Information not available	Open Plot
West	Information not available	Internal Road / Western Railway Track

4. Document Details and Legal Aspects of Property:	
a)	Ownership Documents (Building Permission, Commencement Certificate & Status of Plan)
	Sale Deed, Gift Deed, Lease Deed
	1. Copy of Legal Title Report dated 07.04.2022 issued by Adv. Avataru R. Gupta
	2. Copy of Approved Plan No. B. V. 162 dated 08.08.2018 issued by Palghar Nagar Parishad. Approved upto: Floor + 1st to 7th Upper Floor.
	3. Copy of Amend Approved Plan No. NVV 1502 dated 25.03.2022 issued by Palghar Nagar Parishad. Approved upto: Floor + 1st to 16th Upper Floor.
	4. Copy of Commencement Certificate No. PNP/NRV/1502/2021-2022 dated 25.03.2022 issued by Palghar Nagar Parishad. (This CC is endorsed for the work upto Ground Floor + 1st to 16th Upper Floor)
	5. Copy of RERA Certificate No. P99000045487 dated 24.05.2022 issued by Maharashtra Real Estate Regulatory Authority.
	6. Copy of Valuation Report Ref. No. SBI/Borivali/312 dated 03.01.2023 issued by Shailesh Wani & Co.
	7. Copy of Cost Vetting Report Ref. No. SBI/Borivali/314 dated 03.01.2023 issued by Shailesh Wani & Co.
	8. Copy of CA Certificate dated 07.01.2024 issued by M/s. Zenith M Jain & Co.
	9. Copy of Engineer Certificate dated 01.01.2024 issued by Darsh Consult.

Actual Site Photographs as on 28.02.2024



Actual Site Photographs as on 28.02.2024





Actual Site Photographs as on 28.02.2024



Route Map of the property

Site u/r

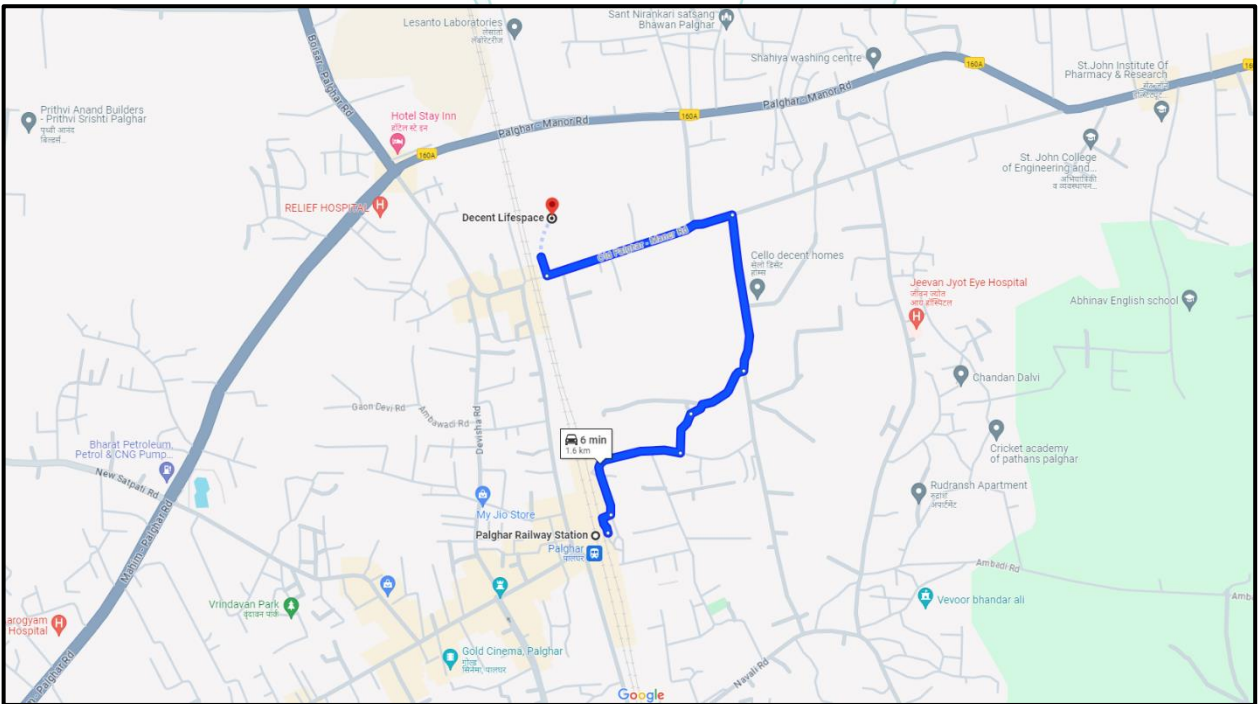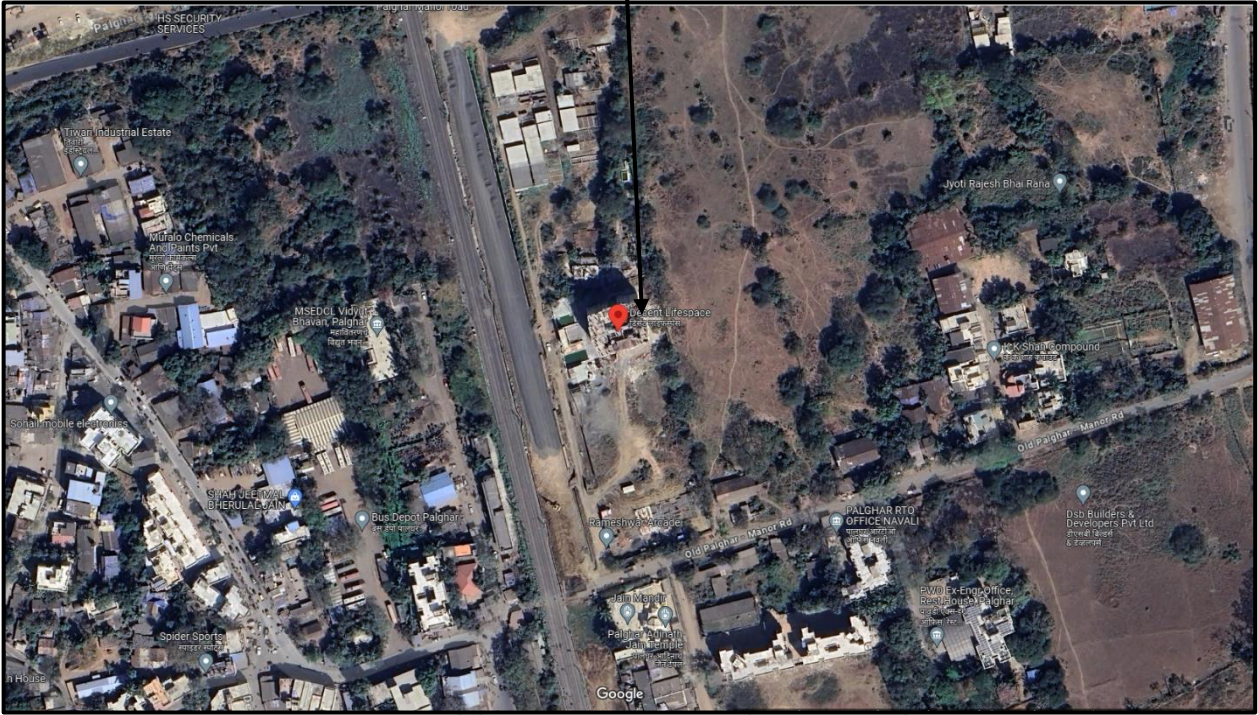

Latitude Longitude: 19°42'17.8"N 72°46'15.9"E

Note: The Blue line shows the route to site from nearest railway station (Palghar – 1.60 Km.)
