



VASTUKALA
Unlocking Excellence

www.vastukala.co.in

MSME Reg No: UDYAM-MH-18-0083617

An ISO 9001 : 2015 Certified Company

CIN: U74120MH2010PTC207869

Vastukala Consultants (I) Pvt. Ltd.

COST VETTING REPORT



Details of the property under consideration:

Name of Project: "Aventus Heights – Phase 2"

"Aventus Heights – Phase 2", Proposed Slum Redevelopment Scheme on Plot Bearing C.T.S. No. 1A (Part), Survey No. 93 (Part) Plot No. 49, Road No. 5/6, Village Deonar, Shivaji Nagar, Govandi (East), Mumbai – 400 043, State – Maharashtra, Country – India

Latitude Longitude: 19°03'44.3"N 72°55'20.7"E

Valuation Done for:
State Bank of India
SME Chembur Branch

Unit No. 11, Building No. 11, Ground Floor, Corporate Park, Sion Trombay Road,
Chembur, Mumbai, Pin Code – 400 071, State - Maharashtra, Country – India.

Our Pan India Presence at :

- | | | | |
|--------------|----------|-------------|-------------|
| 📍 Nanded | 📍 Thane | 📍 Ahmedabad | 📍 Delhi NCR |
| 📍 Mumbai | 📍 Nashik | 📍 Rajkot | 📍 Raipur |
| 📍 Aurangabad | 📍 Pune | 📍 Indore | 📍 Jaipur |

Regd. Office

BI-001, U/B Floor, BOOMERANG, Chandivali Farm Road,
Powai, Andheri East, Mumbai: 400072, (M.S), India

📞 +91 2247495919

✉️ mumbai@vastukala.co.in

🌐 www.vastukala.co.in



www.vastukala.co.in

MSME Reg No: UDYAM-MH-18-0083617

An ISO 9001 : 2015 Certified Company

CIN: U74120MH2010PTC207869

Vastukala Consultants (I) Pvt. Ltd.

Vastu/SBI/Mumbai/04/2024/8367/2306061

24/02-200-PY

Date: 24.04.2024

To,
The Branch Manager,
State Bank of India
SME Chembur Branch
Unit No. 11, Building No. 11,
Ground Floor, Corporate Park,
Sion Trombay Road, Chembur,
Mumbai, Pin Code – 400 071,
State - Maharashtra, Country – India.

Sub: Cost Vetting Report for "**Aventus Heights – Phase 2**" at Govandi (East) Mumbai, Pin Code – 400 043.

Dear Sir,

In accordance with your letter of engagement as stated above, we enclose our Report on Cost Vetting for "**Aventus Heights – Phase 2**", Proposed Slum Redevelopment Scheme on Plot Bearing C.T.S. No. 1A (Part), Survey No. 93 (Part) Plot No. 49, Road No. 5/6, Shivaji Nagar, Village Deonar, Govandi (East), Mumbai – 400 043, State – Maharashtra, Country – India.

M/s. Ratnaakar Shelters LLP is proposing Slum redevelopment Scheme on Plot Bearing C.T.S. No. 1A (Part), Survey No. 93 (Part) Plot No. 49, Road No. 5/6, Shivaji Nagar, Village Deonar, Govandi (East), Mumbai – 400 043, State – Maharashtra, Country – India. Project is comprising Sale Building.

Residential of Sale Building is proposed of Basement + Stilt + 1st to 3rd Podium + 4th to 35th Upper Floors with total RERA carpet area of 66,932.00 Sq. Ft. which consists 2 BHK, with 116 nos. of Sell flats providing with Fitness Centre, Society Office, & Other Amenities.

In this regard, SBI, SME Chembur Branch, Unit No. 11, Building No. 11, Ground Floor, Corporate Park, Sion Trombay Road, Chembur, Mumbai, Pin Code – 400 071, has approached Vastukala Consultants (I) Pvt. Ltd. (VCIPL) to conduct a Cost Vetting of the said project.

Our analysis of the cost vetting is enclosed in this report. This Report forms an integral whole and cannot be split in parts. The outcome of the report/ study can only lead to proper conclusions if the Report as a whole is taken into account.



Our Pan India Presence at :

- | | | | |
|--------------|----------|-------------|-------------|
| 📍 Nanded | 📍 Thane | 📍 Ahmedabad | 📍 Delhi NCR |
| 📍 Mumbai | 📍 Nashik | 📍 Rajkot | 📍 Raipur |
| 📍 Aurangabad | 📍 Pune | 📍 Indore | 📍 Jaipur |

Regd. Office

B1-001, U/B Floor, BOOMERANG, Chandivali Farm Road, Powai, Andheri East, **Mumbai:** 400072, (M.S), India

📞 +91 2247495919

✉️ mumbai@vastukala.co.in

🌐 www.vastukala.co.in

The information used by Vastukala Consultants (I) Pvt. Ltd. (VCIPL) in preparing this report has been obtained from a variety of sources and other relevant documents provided by the client & bank. As agreed, we have performed our cost vetting exercise with the data available related to the business, considering the market prospects and projections. Our results are dependent on documents provided by client & bank, the underlying assumptions, which has been analyzed at a broader level by VCIPL while assessing their reasonableness.

Total Project Cost for the completion of Project will be ₹ 58.10 Cr.

For VASTUKALA CONSULTANTS (I) PVT. LTD.

Manoj
Chalikwar

Director

Manoj B. Chalikwar

Registered Valuer

Chartered Engineer (India)

Reg. No. IBBI / RV / 07/2018/10366

Reg. No. CAT-I-F-1763

SBI Empanelment No.: SME/TCC/2021-22/86/3

Digitally signed by Manoj Chalikwar
DN: cn=Manoj Chalikwar, o=Vastukala
Consultants (I) Pvt. Ltd., ou=Mumbai,
email=manoj@vastukala.org, c=IN
Date: 2024.04.24 11:15:01 +05'30'

Auth. Sign.



Since 1989

Vastukala Consultants (I) Pvt. Ltd.

An ISO 9001 : 2015 Certified Company



About the Project:

Proposed Slum Redevelopment Scheme on Plot Bearing C.T.S. No. 1A (Part), Survey No. 93 (Part) Plot No. 49, Road No. 5/6, Village Deonar, Shivaji Nagar, Govandi (East), Mumbai – 400 043. It is about 2.70 Km. travelling distance from Govandi (East) Railway station

Area Statement as per Approved Plan

A	AREA STATEMENT	
1	Area of the plot	4423.95
2	Deduction for	
a	Set back area	88.95
b	Proposed Road	-
c	Any reservation	-
	Total (a + b + c)	88.95
3	Net Area of Plot (1 – 2)	4335.00
4	Deduction for	-
a	Recreation Ground	
5	Balance Area of Plot (3 – 4)	4310.00
6	Additions for FSI	88.95
	2a. Set Back Area	
7	Total Area (5 + 6)	4423.95
8	FSI Permissible	4.00
9	Proposed Rehab BUA	9432.85
10	Proposed Rehab Component Area	14083.09
11	Additional 1.15% Component	2112.46
12	Total Permissible Sale BUA (10+11)	16195.55
13	Proposed Sale BUA	16065.94
14	Total Proposed BUA (9+13)	25498.79
15	F.S.I. Consumed 14/1	5.76
16	Permissible Rehab Fungible Compensatory FSI Rehab BUA 9432.85 X 35% = 3301.50 sq.mt.	3301.50
17	Proposed Rehab Fungible Compensatory FSI	1193.57
18	Permissible Sale Fungible Compensatory FSI Sale BUA 16065.94 X 35% = 5623.08 sq.mt	5623.08
19	Proposed Sale Fungible Compensatory FSI	-----



Since 1989

Vastukala Consultants (I) Pvt. Ltd.

An ISO 9001 : 2015 Certified Company



Construction Area as per Approved Plan for Sale Building

Sr. No.	Floor	Built Up Area in Sq. M.	Staircase Area in Sq. M.	Other Area in Sq. M.	Total Construction Area in Sq. M.
1	Basement	-	117.97	-	117.97
2	Ground Floor	-	117.97	3.32	121.29
3	1st Floor	-	117.97	3.32	121.29
4	2nd Floor	-	117.97	3.32	121.29
5	3rd Floor	-	117.97	245.03	363.00
6	4th Floor	-	117.97	245.03	363.00
7	5th Floor	241.71	117.97	3.32	363.00
8	6th Floor	241.71	117.97	3.32	363.00
9	7th Floor	241.71	117.97	3.32	363.00
10	8th Floor	178.74	117.97	68.87	365.58
11	9th Floor	241.71	117.97	3.32	363.00
12	10th Floor	241.71	117.97	3.32	363.00
13	11th Floor	241.71	117.97	3.32	363.00
14	12th Floor	241.71	117.97	3.32	363.00
15	13th Floor	241.71	117.97	3.32	363.00
16	14th Floor	241.71	117.97	3.32	363.00
17	15th Floor	178.74	117.97	68.87	365.58
18	16th Floor	241.71	117.97	3.32	363.00
19	17th Floor	241.71	117.97	3.32	363.00
20	18th Floor	241.71	117.97	3.32	363.00
21	19th Floor	241.71	117.97	3.32	363.00
22	20th Floor	241.71	117.97	3.32	363.00
23	21st Floor	241.71	117.97	3.32	363.00
24	22nd Floor	178.74	117.97	68.87	365.58
25	23rd Floor	241.71	117.97	3.32	363.00
26	24th Floor	-	117.97	245.03	363.00
27	25th Floor	241.71	117.97	3.32	363.00
28	26th Floor	241.71	117.97	3.32	363.00
29	27th Floor	241.71	117.97	3.32	363.00
30	28th Floor	241.71	117.97	3.32	363.00
31	29th Floor	178.74	117.97	68.87	365.58
32	30th Floor	241.71	117.97	3.32	363.00
33	31st Floor	241.71	117.97	3.32	363.00
34	32nd Floor	241.71	117.97	3.32	363.00
35	33rd Floor	241.71	117.97	3.32	363.00
36	34th Floor	241.71	117.97	3.32	363.00
37	35th Floor	241.71	117.97	3.32	363.00
38	Terrace / OHT	-	117.97	-	117.97
TOTAL		6,999.42	4,482.86	1,106.85	12,589.13
No. of Stack Parking					96 Nos.

Project Cost

Sr. No.	Particulars	Total Estimated Amount in ₹	Total Estimated Amount in ₹ Cr.
1	Land Cost		
i.	Acquisition Cost of Land or Development Rights, and Legal Cost.	-	-
ii.	Rent to Tenants, Lease premium, Lease Rent, interest cost incurred or payable on Land Cost	-	-
iii.	Amount of Premium payable to obtain development rights, FSI, additional FSI, fungible area, and any other incentive under DCR from Local Authority or State Government or any Statutory Authority.	10,00,00,000.00	10.00
iv.	Acquisition cost of TDR (if any)	-	-
2	Cost of Construction		
i.	Estimated construction cost of rehab cum sale building including site development and infrastructure for the same.	37,35,06,510.00	37.35
ii.	On site expenditure for development of entire project excluding cost of construction as per(i) above,		
a.	Architect Fees & Consultant fees	1,86,75,326.00	1.87
b.	Admin Cost includes salaries, site overheads, development works, cost of services (including water, electricity, sewerage, drainage, layout roads etc.), cost of machineries and equipment including its hire and maintenance cost, consumables etc. All costs directly incurred to complete the construction of the entire phase of the project registered.	2,24,10,391.00	2.24
c.	Marketing Cost	1,52,29,130.00	1.52
3	Interest during the Project	4,00,00,000.00	4.00
4.	Contingency Charges	1,12,05,195.00	1.12
	GRAND TOTAL:	58,10,26,552.00	58.10

For VASTUKALA CONSULTANTS (I) PVT. LTD.

**Manoj
Chalikwar**
Director

Digitally signed by Manoj Chalikwar
DN: cn=Manoj Chalikwar, o=Vastukala
Consultants (I) Pvt. Ltd., ou=Mumbai,
email=manoj@vastukala.org, c=IN
Date: 2024.04.24 11:15:25 +05'30'

Auth. Sign.

Manoj B. Chalikwar

Registered Valuer

Chartered Engineer (India)

Reg. No. IBBI / RV / 07/2018/10366

Reg. No. CAT-I-F-1763

SBI Empanelment No.: SME/TCC/2021-22/86/3



Since 1989

Vastukala Consultants (I) Pvt. Ltd.

An ISO 9001 : 2015 Certified Company



Comments on each element of Cost of Project: -

1. Land Cost:

As per Present Ready Reckoner rate the Project Land Value is ₹ 39.69 Cr. considering Land Rate @ ₹ 92,080.00 per Sq. M. & Net Plot Area of 4,310 Sq. M.

As per document purchase cost of land & stamp duty cost is ₹ 0.00 i.e., ₹ 0.0 Cr. which is 0% of Total Project Cost.

2. Building Cost of Construction for Sale Building:

Construction Area of Sale Building = 12,589.13 Sq. M. i.e., 1,35,509.40 Sq. Ft.

No. of Stack Car Parking = 96 Nos.

Total estimated cost for construction of Building (includes cost of RCC work, manpower, lift, material, painting, finishing work, site development, etc.) is ₹ 33,99,06,510.00 i.e., ₹ 33.99 Cr. which comes ₹ 27,000.00 per Sq. M. on construction area for building, and cost for stack parking is ₹ 3,36,00,000.00 i.e., ₹ 3.36 Cr. which comes ₹ 3,50,000.00 per stack parking.

Hence, total construction cost (Cost of construction of building + Cost of stack parking) (₹ 33,99,06,510.00 + ₹ 3,36,00,000.00) = ₹ 37,35,06,510.00 i.e., ₹ 37.35 Cr.

The total construction area is 12,589.13 Sq. M. i.e., 1,35,509.40 Sq. Ft., projected cost of ₹ 37.35 Cr is 64.28% of total project cost

VC IPL opinion the construction cost of 27,000/- Per Sq. M. which is in line with Market-Trend.

Particulars	Rate per Sq. Ft.
Excavation Work	1500.00
Total RCC Work	12000.00
Final Finishing Work	7500.00
Other Work	6000.00
Cost of Construction	27000.00
Stack Car Parking Cost	3,50,000.00 per parking

3. Approval Charges:

The Total Approval Cost (Fungible Cost & Development Cess Premium & TDR Cost) as per architect letter will be ₹ 10,00,00,000.00 i.e., ₹ 10.00 Cr. which is 17.21% of Total Project Cost.

As per information provided by developer.

4. Architect Cost, RCC & Other Professional Charges:

The total Architect charges of ₹ 1,86,75,326.00 i.e., ₹ 1.87 Cr. is 5.0% of total construction cost building & it is line up with Market trend.

The professional charge consists of Architect & Legal which in market is in the range of 2% - 5% of Total Construction cost of the project.

5. Administrative Expenses:

Salaries, site overheads, development works, cost of services (including water, electricity, sewerage, drainage, layout roads etc.), cost of machineries and equipment including its hire and maintenance cost, consumables etc. All costs directly incurred to complete the construction of the entire phase of the project registered is estimated 6% of total construction cost Building which comes to ₹ 2,24,10,391.00 i.e., ₹ 2.24Cr.

The admin charges which in market is in the range of 4% - 6% of Total Construction cost of the project.

6. Marketing Expenses:

Marketing costs directly incurred to complete the construction of the entire phase of the project registered is estimated at 2% of total Sale income from the project which comes to ₹ 1,52,29,130.00 i.e., ₹ 1.52 Cr.

The marketing charge consists of brokerage & commission which in market is in the range of 1% - 3% of Total Sale income of the property.



Since 1989

Vastukala Consultants (I) Pvt. Ltd.

An ISO 9001 : 2015 Certified Company



Photo copy of following document is provided to us & this report should be read along with it:

- ✓ Copy of Developer Agreement dated 15.03.2015 between M/s. Devkrupa Co-operative Housing Society Ltd. (The Society) and M/s. Ratnaakar Shelters LLP (The Developers) through registered agreement Notary R No. 001/2015
- ✓ Copy of Legal Title Report dated 20.10.2022 issued by Anant Narayan Advocate High Court.
- ✓ Copy of Intimation of Approval (IOA) Letter No. SRA/ENG/3834/ME/MCGM/AP dated 03.11.2021 issued by Slum Rehabilitation Authority (SRA).
- ✓ Copy of Approved Plan No. SRA/ENG/3834/ME/MCGM/AP dated 03.11.2021 issued by Slum Rehabilitation Authority (SRA).

Approved upto: Basement + Stilt Floor + 1st to 3rd Podium floor + 4th to 16th Upper Floors

- ✓ Copy of Commencement Certificate No. SRA/ENG/3834/ME/MCGM/AP dated 03.11.2021 issued by Slum Rehabilitation Authority (SRA).

(This CC is endorsed for the work for up to 5 floors as per approved plan dated 03.11.2021)

- ✓ Copy of Architect Drawing Plan issued by M/s. Consultants Combined Architects.

Approval upto: Basement + Stilt Floor + 1st to 3rd Podium + 4th to 35th Upper Floors

- ✓ Copy of Fire NOC Certificate No. FB / HRC / R – V / 67 dated 25.10.2019 issued Municipal Corporation of Greater Mumbai, Mumbai Fire Brigade.
- ✓ Copy of Engineer's Certificate dated 11.10.2023 issued by optimal Consultancy Services Pvt. Ltd.
- ✓ Copy of CA Certificate dated 01.10.2022 issued by M/s. Vinod Sukhraj Mehta.
- ✓ Copy of RERA Certificate No. P51800047961 dated 02.12.2022 issued by Maharashtra Real Estate Regulatory Authority (MAHRERA).
- ✓ Copy of Architect's Certificate dated 20.04.2023 issued by Consultants Combined Architects.



Since 1989

Vastukala Consultants (I) Pvt. Ltd.

An ISO 9001 : 2015 Certified Company





Actual Site Photographs



Route Map of the property

Site u/r

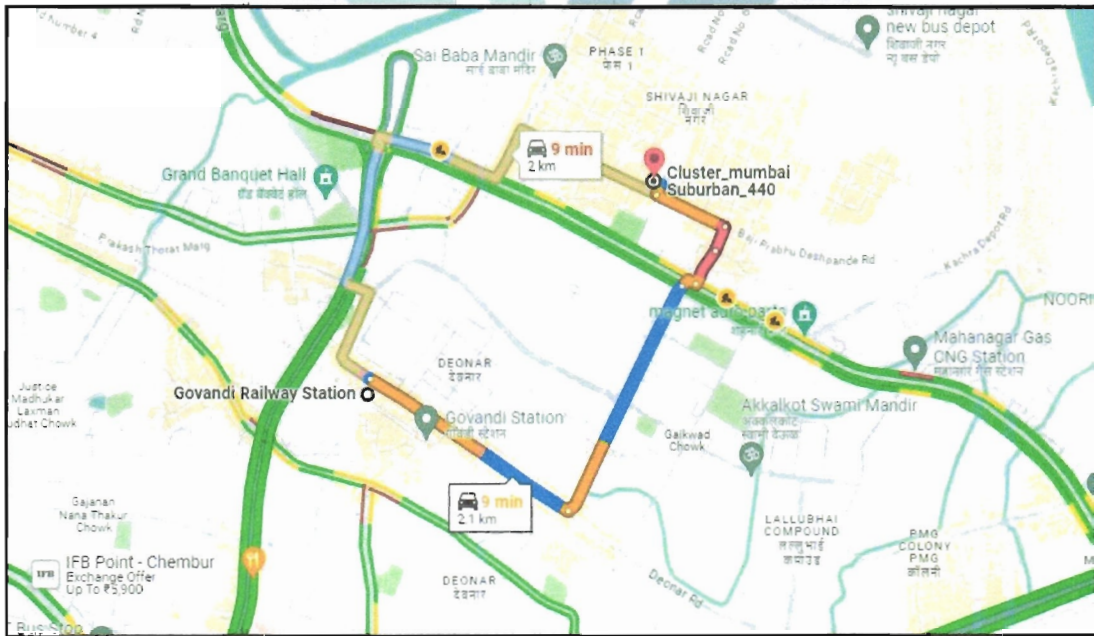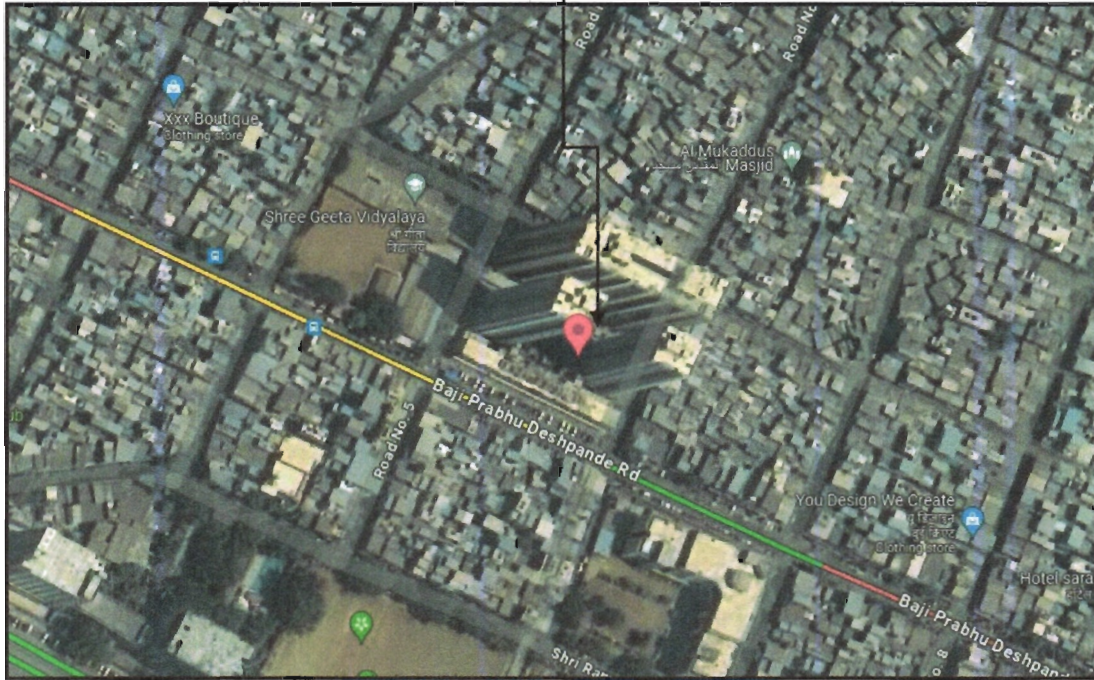

Latitude Longitude: 19°03'44.3"N 72°55'20.7"E

Note: The Blue line shows the route to site from nearest railway station (Govandi – 2.1 Km.)
