MSME Reg No: UDYAM-MH-18-0083617 An ISO 9001 : 2015 Certified Company CIN: U74120MH2010PTC207869



Vastukala Consultants (I) Pvt. Ltd.

WORK PROGRESS REPORT

Details of the property under consideration:

Name of Owner: M/s. Matrukrupa Stone Crusher LLP

Industrial Land bearing New Gat No. 83/4/A & 83/4/B (Old Gat No. 83/4), Near Indian Oil Petrol Pump, Village - Pandhurli, Taluka – Sinnar, District – Nashik, State – Maharashtra, Country - India

Latitude Longitude: 19°50'03.8"N 73°53'12.5"E

Valuation Done for: Bank of India Zonal Office, Nashik

1st Floor, Plot No G-1, MIDC, Satpur Colony, Main Trimbaak Road, Nashik – 422007, State – Maharashtra, Country - India



Nashik: 4, 1st Floor, Madhusha Elite, Vrundavan Nagar, Jatra Nandu Naka Link Road, Adgaon, Nashik-422003 (M.S.), INDIA Email: nashik@vastukala..co.in| Tel : +91 253 4068262/98903 80564

Our Pan India Presence at :

ur ran mu	la l'icoci	icc at .	
Nanded	Q Thane	Ahmedabad	O Delhi NCR
Mumbai	Nashik	Rajkot	Raipur
Aurangabad	♀ Pune	♀Indore	💡 Jaipur

Regd. Office

B1-001, U/B Floor, BOOMERANG, Chandivali Farm Road, Powai, Andheri East, **Mumbai** :400072, (M.S), India

+91 22 47495919
mumbai@vastukala.co.in

www.vastukala.co.in



MSME Reg No: UDYAM-MH-18-0083617 An ISO 9001 : 2015 Certified Company CIN: U74120MH2010PTC207869

Vastukala Consultants (I) Pvt. Ltd.

Vastu/BOI/Nashik/05/2024/8535/2306222 08/03-82-PY Date: 08.05.2024

Work Progress Report

Farm

Farm

Farm Farm

The property bearing Industrial Land bearing New Gat No. 83/4/A & 83/4/B (Old Gat No. 83/4), Near Indian Oil Petrol Pump, Village - Pandhurli, Taluka - Sinnar, District - Nashik, State - Maharashtra, Country - India belongs to M/s. Matrukrupa Stone Crusher LLP.

Boundaries of the property. North South East West

The project proposed is under construction, which is considered for project approval. As per Cost Vetting Report Ref. No. Vastu/Nashik/12/2022/28176/44512, 29/05-586-VBVS Dated 29.12.2022, Estimate Total Cost of Construction of Building was ₹ 79,44,925.00 and the work completion stage of following items described in cost vetting report is as follows:

Sr. No.	Particulars	Estimate Amount as per Cost Vetting Report	Actual Percentage work completed as on 21.11.2023	Actual Amount to be incurred as on 21.11.2023	Remark
1	RCC Construction of Staff Quarters followed by brickwork, plastering, windows and doors	23,36,400.00	0.00%	0.00	Work not started yet
2	RCC Construction of Office Room followed by brickwork, plastering, windows and doors	3,76,420.00	0.00%	0.00	Work not started yet
3	Plinth levelling and Backfilling	25,48,800.00	100.00%	25,48,800.00	Footing work is completed
4	Retaining Wall	14,11,575.00	0.00%	0.00	Work is in progress
5	RCC Construction of Electrical Room followed by brickwork, plastering, windows and doors	5,31,000.00	0.00%	0.00	Work not started yet
6	RCC Construction of Toilet Blocks followed by brickwork, plastering, windows and doors, Tiling work upto 9 ft.	3,77,600.00	0.00%	0.00	Work not started yet
7	Attached Toilets	89,680.00	0.00%	0.00	Work not started yet
8	Solar Panel	1,29,800.00	0.00%	0.00	Work not started yet
9	Electrical Work	1,43,650.00	0.00%	0.00	Work not started yet
	Total	79,44,925.00		25,48,800.00	



Nashik: 4, 1st Floor, Madhusha Elite, Vrundavan Nagar, Jatra Nandu Naka Link Road, Adgaon, Nashik-422003 (M.S.), INDIA Email: nashik@vastukala..co.in| Tel : +91 253 4068262/98903 80564

Our Pan India Presence at :

Nanded	Q Thane	Ahmedabad	Q Delhi NCR
Mumbai	P Nashik	Rajkot	Raipur
Q Aurangabad	♀ Pune	♀ Indore	💡 Jaipur

Regd. Office

BI-001, U/B Floor, BOOMERANG, Chandivali Farm Road, Powai, Andheri East, Mumbai :400072, (M.S), India

+91 22 47495919 📉 mumbai@vastukala.co.in

🛞 www.vastukala.co.in



MSME Reg No: UDYAM-MH-18-0083617 An ISO 9001 : 2015 Certified Company CIN: U74120MH2010PTC207869

Vastukala Consultants (I) Pvt. Ltd.

Vastu/BOI/Nashik/05/2024/8535/2306222 08/03-82-PY Date: 08.05.2024

Work Progress Report

Farm

Farm Farm

The property bearing Industrial Land bearing New Gat No. 83/4/A & 83/4/B (Old Gat No. 83/4), Near Indian Oil Petrol Pump, Village - Pandhurli, Taluka - Sinnar, District - Nashik, State - Maharashtra, Country - India belongs to M/s. Matrukrupa Stone Crusher LLP.

Boundaries of the property. Farm North South East West

The project proposed is under construction, which is considered for project approval. As per Cost Vetting Report Ref. No. Vastu/Nashik/12/2022/28176/44512, 29/05-586-VBVS Dated 29.12.2022, Estimate Total Cost of Construction of Building was ₹ 79,44,925.00 and the work completion stage of following items described in cost vetting report is as follows:

Sr. No.	Particulars	Estimate Amount as per Cost Vetting Report	Actual Percentage work completed as on 21.11.2023	Actual Amount to be incurred as on 21.11.2023	Remark
1	RCC Construction of Staff Quarters followed by brickwork, plastering, windows and doors	23,36,400.00	0.00%	0.00	Work not started yet
2	RCC Construction of Office Room followed by brickwork, plastering, windows and doors	3,76,420.00	0.00%	0.00	Work not started yet
3	Plinth levelling and Backfilling	25,48,800.00	100.00%	25,48,800.00	Footing work is completed
4	Retaining Wall	14,11,575.00	0.00%	0.00	Work is in progress
5	RCC Construction of Electrical Room followed by brickwork, plastering, windows and doors	5,31,000.00	0.00%	0.00	Work not started yet
6	RCC Construction of Toilet Blocks followed by brickwork, plastering, windows and doors, Tiling work upto 9 ft.	3,77,600.00	0.00%	0.00	Work not started yet
7	Attached Toilets	89,680.00	0.00%	0.00	Work not started yet
8	Solar Panel	1,29,800.00	0.00%	0.00	Work not started yet
9	Electrical Work	1,43,650.00	0.00%	0.00	Work not started yet
	Total	79,44,925.00		25,48,800.00	



Nashik: 4, 1st Floor, Madhusha Elite, Vrundavan Nagar, Jatra Nandu Naka Link Road, Adgaon, Nashik-422003 (M.S.), INDIA Email: nashik@vastukala..co.in| Tel : +91 253 4068262/98903 80564

Our Pan India Presence at :

Nanded	O Thane	Q Ahmedabad	Oelhi NCR
Mumbai	Vashik	Rajkot	🖓 Raipur
💡 Aurangabad	♀ Pune	♀Indore	♀ Jaipur

Regd. Office

B1-001, U/B Floor, BOOMERANG, Chandivali Farm Road, Powai, Andheri East, Mumbai :400072, (M.S), India

***** +91 22 47495919

🞽 mumbai@vastukala.co.in

🛞 www.vastukala.co.in

Valuation Report Prepared For: BOI/ Zonal Office / M/s. Matrukrupa Stone Crusher LLP (8535/2306222) Page 3 of 5

As per site inspection dated 21.11.2023 cost of construction must incur will be ₹ 25,48,800.00

The report of the property is based on the site visit dated 21.11.2023 & documents produced by the concern. Construction work going as per approved plan only. Legal aspects have not been taken into considerations while preparing this report.

Hence certified

For VASTUKALA CONSULTANTS (I) PVT. LTD.

Manoj Chalikwar Digitally signed by Manoj Chalikwar DN: cn=Manoj Chalikwar, o=Vastukala Consultants (II) Pvt. Ltd., ou=Mumbai, email=manoj@vastukala.org, c=IN Date: 2024.05.08 10:52:13 +05'30'

Director

Auth. Sign.

Manoj B. Chalikwar Registered Valuer Chartered Engineer (India) Reg. No. IBBI / RV / 07/2018/10366 Reg. No. CAT-I-F-1763 BOI Empanelment No.: MNZ:C&IC:VAL19-20



Since 1989




An ISO 9001 : 2015 Certified Company

Vastukala Consultants (I) Pvt. Ltd.

Valuation Report Prepared For: BOI/ Zonal Office / M/s. Matrukrupa Stone Crusher LLP (8535/2306222) Page 4 of 5

Actual Site Photographs

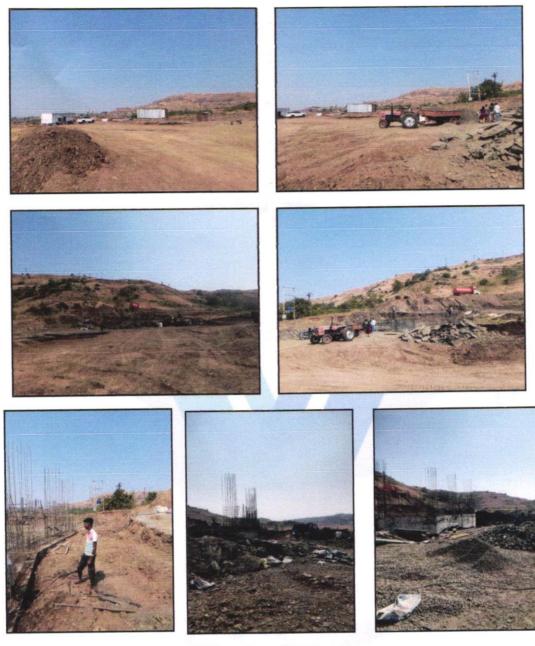



Since 1989



An ISO 9001 : 2015 Certified Company

Vastukala Consultants (I) Pvt. Ltd.

Valuation Report Prepared For: BOI/ Zonal Office / M/s. Matrukrupa Stone Crusher LLP (8535/2306222) Page 5 of 5



Latitude Longitude: 19°50'03.8"N 73°53'12.5"E Note: The Blue line shows the route to site from nearest railway station (Deolali – 15.3 Km.)

Vastukala Consultants (I) Pvt. Ltd.

An ISO 9001 : 2015 Certified Company



Since 1989

