CIN: U74120MH2010PTC207869 MSME Reg. No.: UDYAM-MH-18-0083617 An ISO 9001:2015 Certified Company





WORK PROGRESS REPORT



Details of the property under consideration:

Name of Project: "Sahil Infra"

"Sahil Infra", Proposed Residential cum Commercial Building bearing on Plot No. 03-R.C., Scheme No. 134, Ward No. 37 (Sai Kripa), Nipania, M.R. 10 Road, Gram Khajrana, Tehsil & District - Indore, Pin Code - 452 010, State - Madhya Pradesh, Country - India

Latitude Longitude: 22°44'48.2"N 75°55'25.9"E

Valuation Done for: ThPunjab National Bank Create **MID Corporate Centre**

2nd Floor, C 21, Business Park, Opp. Raddison Hotel, Indore, Pin Code - 452001, State - Madhya Pradesh, Country - India




Indore: 106, 1st Floor, Gold Star Tower, 576, M. G. Road, Opp. TI Mall, Indore - 452 001, (M.P.), INDIA E-mail: indore@vastukala.org, Tel.: +91 7313510884 +91 9926411111

Our Pan India Presence at:

Aurangabad Pune Mumbai **♀** Nanded Thane

P Delhi NCR P Nashik

🦞 Rajkot **♀** Raipur Ahmedabad 💡 Jaipur



TeleFax: +91 22 28371325/24

CIN: U74120MH2010PTC207869 MSME Reg. No.: UDYAM-MH-18-0083617 An ISO 9001:2015 Certified Company





Valuation Report Prepared For: PNB / MCC Branch / M/s. Sahil Infra (30606/2301440)

Page 2 of 8

Vastu/PNB/Indore/07/2023/2364/2301440

06/11-65-PY Date: 06.07.2023

Work Progress Report

The property bearing "Sahil Infra", Proposed Residential cum Commercial Building bearing on Plot No. 03-R.C., Scheme No. 134, Ward No. 37 (Sai Kripa), Nipania, M.R. 10 Road, Gram Khajrana, Tehsil & District -Indore, Pin Code – 452 010, State – Madhya Pradesh, Country – India belongs to M/s. Sahil Infra.

Boundaries of the property.

North 20th Road South Building

East Shalimar Apartment

West Allied Auto Agencies Maurti Authorised Services Station

The project proposed is under construction, which is considered for project approval. Building consists of proposed 2 Basements + Ground Floor + Mezzanine Floor + Parking Floor + 1st to 7th Upper Residential Floors. The work completion stage is as follows:

Sr. No.	Particulars	Final Percentage	Actual Percentage	Remark
1	RCC Footing/Foundation	5.00	5.00	Completed
2	RCC Plinth	5.00	5.00	Completed
3	Full Building RCC	40.00	36.50	Basement 1 & 2, Ground Floor, Mezzanine Floor, Parking Floor, 1 st to 6 th Upper Floor Slab work is completed
4	Internal Brick work	7.00	5.25	Basement 1 & 2, Ground Floor,
5	External Brickwork	7.00	5.25	Mezzanine Floor, Parking Floor & 1st to 4th floor Brick work is completed and on 5th floor work is in progress.
6	Internal plastering	3.50	2.00	Basement 1 & 2, Ground Floor,
7	External plastering	3.50	2.00	Mezzanine Floor, Parking Floor & 1st to 3rd floor plastering work is completed and on 4th floor work is in progress
8	Doors & Windows Th	ink 5.00 nov	rate Crec	nte
9	Flooring, Tiling, Kitchen Platform	10.00	010.0100	
10	Internal painting	1.50		
11	External painting	1.50		
12	Electrification, plumbing & Sanitary installation	5.00		
13	Lift Installation	2.00		
14	Passage, Staircase & Lobby development	2.00		CONSULTANTO DE CONSUL
15	External developments / Final finishing work	2.00		valuers a appraisers A Valuers a Appraisers Interior Designers Chartered Engineers (I) TEV Consultants Landor's Engineers
Total		100.00	61.00	730 MH2010 PTC281

Indore: 106, 1st Floor, Gold Star Tower, 576, M. G. Road, Opp. TI Mall, Indore - 452 001, (M.P.), INDIA E-mail: indore@vastukala.org, Tel.: +91 7313510884 +91 9926411111



Mumbai Thane

Delhi NCR

Aurangabad Nanded **?** Nashik

Pune 🕈 Ahmedabad 💡 Jaipur

🦞 Rajkot **♀** Raipur



TeleFax: +91 22 28371325/24



As per Cost Vetting Report Ref. No. Vastu/SBI/Mumbai/08/2022/26145/42374, 27/14-441-PYM Dated 27.08.2022, Estimate Total Cost of Construction of Building was ₹ 30,13,57,800.00.

As per site inspection dated 30.06.2023 work completion percentage is 61.00% and cost of construction as on date is (₹ 30,13,57,800.00 X 61.00%) = ₹ 18,38,28,258.00

The report of the property is based on the site visit dated 30.06.2023 & documents produced by the concern. Construction work going as per approved plan only. Legal aspects have not been taken into considerations while preparing this report.

Hence certified

For Vastukala Consultants (I) Pvt. Ltd.

Manoj B. Chalikwar Registered Valuer Chartered Engineer (India) Reg. No. CAT-I-F-1763 PNB Emp. No. ZO: SAMD:1138

Think.Innovate.Create








































































Route Map of the property

Site u/r



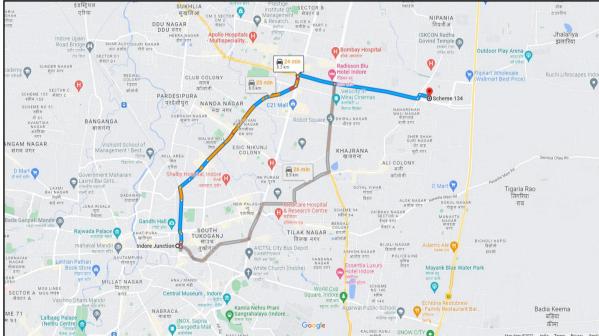

Longitude Latitude - 22°44'48.2"N 75°55'25.9"E

Note: The Blue line shows the route to site from nearest Railway Station (Indore Junction – 8.3 KM.)



