



## PROJECT VALUATION REPORT



**Details of the property under consideration:** 

Name of Project: "Elite Vivanta"

"Elite Vivanta", Proposed Residential cum Commercial building on Plot bearing Plot No. 38C, Sector No. 15, Near Millennium Empire, D – Mart Road, Village – Kharghar, Navi Mumbai, Taluka – Panvel, District – Raigad, Pin Code – 410 210, State – Maharashtra, Country – India

Think.Innovate.Create

Latitude Longitude: 19°02'34.0"N 73°04'41.6"E

# Valuation Done for: State Bank of India SME - Vashi Turbhe Branch

Sector 19, Ground Floor, Central Facility Building, Phase – II, Vashi, Navi Mumbai – 400 705, State - Maharashtra, Country – India





Regd. Office: B1-001, U/B Floor, Boomerang, Chandivali Farm Road, Andheri (East), Mumbai - 400 072, (M.S.), INDIA

TeleFax: +91 22 28371325/24

mumbai@vastukala.org

CIN: U74120MH2010PTC207869 MSME Reg. No.: UDYAM-MH-18-0083617 An ISO 9001:2015 Certified Company





Vastu/SBI/Mumbai/02/2024/7213/2305241 29/20-463-PY

Date: 22.02.2024

To,
The Branch Manager,
State Bank of India
SME - Vashi Turbhe Branch
Sector 19, Ground Floor,
Central Facility Building, Phase – II,
Vashi, Navi Mumbai – 400 705,
State - Maharashtra, Country – India

Sub: Project Valuation for "Elite Vivanta" at Kharghar, Navi Mumbai, Pin Code – 410 210.

Dear Sir.

In accordance with your letter of engagement as stated above, we enclose our Report on Project Valuation for **"Elite Vivanta"**, Proposed Residential cum Commercial building on Plot bearing Plot No. 38C, Sector No. 15, Near Millennium Empire, D – Mart Road, Village – Kharghar, Navi Mumbai, Taluka – Panvel, District – Raigad, Pin Code – 410 210, State – Maharashtra, Country – India.

M/s. Nathdwara Developers Pvt. Ltd., is a private limited company. The firm is in operation for over the last 20 years, M/s Nathdwara Developers Pvt. Ltd., a Builders & Developers has created a history of success by building a robust portfolio for itself by delivering dream homes to affordable homes in and around Navi Mumbai area.

M/s. Nathdwara Developers Pvt. Ltd., is developing a Residential cum Commercial building on Plot bearing Plot No. 38C, Sector No. 15, Near Millennium Empire, D – Mart Road, Village – Kharghar, Navi Mumbai, Taluka – Panvel, District + Raigad, Pin Code + 410 210, State – Maharashtra, Country – India. Project is comprising of Residential Building.

Residential Building is proposed of Ground Floor + 1st to 3rd Podium Floors + 4th to 24th Upper Residential Floors with total RERA carpet area of 79,282.60 Sq. Ft. which consists 2 BHK, 3 BHK and Shops units with 81 nos. of Sell flats and 14 nos. of Sell Shops providing with Fitness Centre, Society Office, & Other Amenities.





Regd. Office: B1-001, U/B Floor, Boomerang, Chandivali Farm Road, Andheri (East), Mumbai - 400 072, (M.S.), INDIA

TeleFax: +91 22 28371325/24

mumbai@vastukala.org

In this regard, SBI, SME - Vashi Turbhe Branch, Sector 19, Ground Floor, Central Facility Building, Phase - II, Vashi, Navi Mumbai - 400 705, has approached Vastukala Consultants (I) Pvt. Ltd. (VCIPL) to conduct a Project Valuation of the said project.

Our analysis of the project valuation is enclosed in this report. This Report forms an integral whole and cannot be split in parts. The outcome of the report/ study can only lead to proper conclusions if the Report as a whole is taken into account.

The information used by Vastukala Consultants (I) Pvt. Ltd. (VCIPL) in preparing this report has been obtained from a variety of sources and other relevant documents provided by the client & bank. As agreed, we have performed our project valuation exercise with the data available related to the business, considering the market prospects and projections. Our results are dependent on documents provided by client & bank, the underlying assumptions, which has been analyzed at a broader level by VCIPL while assessing their reasonableness.

Sale Realisation from the Project is ₹ 153.15 Cr. and Net Present Value of the project as on date is ₹ 71.15 Cr.

For VASTUKALA CONSULTANTS (I) PVT. LTD.

Director

Auth. Sign.

Manoj B. Chalikwar

Registered Valuer Chartered Engineer (India) Reg. No. IBBI / RV / 07/2018/10366

Reg. No. CAT-I-F-1763

SBI Empanelment No.: SME/TCC/2021-22/86/3 NOVate. Create









Page 4 of 42

# PROJECT VALUATION REPORT OF

"Elite Vivanta"

"Elite Vivanta", Proposed Residential cum Commercial building on Plot bearing Plot No. 38C, Sector No. 15, Near Millennium Empire, D – Mart Road, Village – Kharghar, Navi Mumbai, Taluka – Panvel, District – Raigad, Pin Code – 410 210, State – Maharashtra, Country – India

Latitude Longitude: 19°02'34.0"N 73°04'41.6"E

#### NAME OF DEVELOPER: M/s. Nathdwara Developers Pvt. Ltd.

Pursuant to instructions from State Bank of India, SME – Vashi Turbhe Branch, we have duly visited, inspected, surveyed & assessed the above said property to determine the fair & reasonable market value of the said property as on 31st December 2024 for approval of project finance purpose.

#### 1. Location Details:

Proposed Residential cum Commercial building on Plot bearing Plot No. 38C, Sector No. 15, Near Millennium Empire, D – Mart Road, Village – Kharghar, Navi Mumbai, Taluka – Panvel, District – Raigad, Pin Code – 410 210. It is about 1.30 Km. travelling distance from Kharghar Village Metro Station & 2.90 Km. travelling distance from Kharghar Railway station. Surface transport to the property is by buses, taxis & private vehicles. The property is in developed locality. All the amenities like shops, banks, hotels, markets, schools, hospitals, etc. are all available in the surrounding locality. The area is higher middle class & developed.

2. Developer Details:

Name of builder	M/s. Nathdwara Developers Pvt. Ltd.
Project Registration Number	P52000054784
Register office address	M/s. Nathdwara Developers Pvt. Ltd.
	309, Arenja Corner, Sector – 17, Vashi, Navi Mumbai, Taluka & District – Thane, Pin Code – 400 703, State – Maharashtra, Country – India.
Contact Numbers	Contact Person:  Mr. Vijesh Jain (Consultant)
	Mobile No. 9929977362
	Mr. Ramchandra Chauhan (Site Engineer)
	Mobile No. 9321256337
E – mail ID and Website	

3. Boundaries of the Property:

Direction	Sale Building
On or towards North	Ayyappa Mandir Road & Millennium Empire
On or towards South	Under Construction Building
On or towards East	Ayyappa Mandir Road
On or towards West	Tricity Eros Building
{	Tel Consultants Lender's Engineer



Our Pan India Presence at:

Mumbai
Thane
Nanded
Delhi NCR
Nashik

Regd. Office: B1-001, U/B Floor, Boomerang, Chandivali Farm Road, Andheri (East), Mumbai - 400 072, (M.S.), INDIA

TeleFax: +91 22 28371325/24

mumbai@vastukala.org

#### Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 5 of 42 **Vastukala Consultants (I) Pvt. Ltd.**

B1-001, U/B Floor, Boomerang, Chandivali Farm Road, Powai, Andheri (East), Mumbai – 400 072

To,
The Branch Manager,
State Bank of India
SME - Vashi Turbhe Branch
Sector 19, Ground Floor,
Central Facility Building, Phase – II,
Vashi, Navi Mumbai – 400 705,
State - Maharashtra, Country – India

### VALUATION REPORT (IN RESPECT OF PROJECT FINANCE)

Ι	General							
1.	Purpose for which the valuation is made :	As per request from State Bank of India, SME – Vashi						
		Turbhe Branch, to assess Fair Market value of the						
		Project for bank loan purpose.						
2.	a) Date of inspection :	31.01.2024						
	b) Date on which the valuation is made :	22.02.2024						
3.	List of documents produced for perusal							
	Corporation of Maharashtra Limited (CIDCO (*) Ltd. (The Licensee) through registered agreeme							
		al Plot Letter Reference No. 1960/1000082/221 dated pment Corporation of Maharashtra Limited (CIDCO).						
	3. Copy of Approved Plan No. CIDCO/BP-17102/	TPO (NM & K)/2019/10852 dated 06.06.2023 issued by						
	City and Industrial Development Corporation of I  Approved upto: Ground Floor + 1st to 3rd Podiur							
		CIDCO/BP-17102/TPO (NM & K)/2019/10852 dated						
		pment Corporation of Maharashtra Ltd. (CIDCO).						
		loor + 1st to 3rd Podium Floors + 4th to 24th Upper						
	Residential Floors remain valid for period of 1 ye							
	1	HQ/2023/E-208345 dated 10.05.2023 issued by City and						
	Industrial Development Corporation of Maharashtra Limited (CIDCO).							
	6. Copy of No Objection Certificate for Height Clearance NOC ID No. NAVI/WEST/B/072419/418097 dated 20.08.2019 valid upto 19.08.2027 issued by Airports Authority of India.							
	7. Copy of Grant of NOC for avail additional FSI Certificate No. CIDCO/MTS-III/UDCPR/800197105/2023/2311 dated 27.03.2023 issued by City and Industrial Development Corporation of Maharashtra Limited (CIDCO).							
	8. Copy of RERA Certificate RERA No. P52000 Estate Regulatory Authority (MAHRERA).	54784 dated 12.02.2024 issued by Maharashtra Real						
	9. Copy of CA Certificate (Form 3) dated 27.11.202	23 issued by M/s. H. M. Shah & Associates.						
	10. Copy of Architect Certificate dated 01.09.2023 is							
	Project Name :	"Elite Vivanta", Proposed Residential cum						
	(with address & phone nos.)	Commercial building on Plot bearing Plot No. 38C, Sector No. 15, Near Millennium Empire, D – Mart Road, Village – Kharghar, Navi Mumbai, Taluka – Panvel, District – Raigad, Pin Code – 410 210, State – Maharashtra, Country – India						



atior	n Report Prepare					
			is / their address		M/s. Nathdwara Develop	
		` '	of share of each			
	` '	•			309, Arenja Corner, Secto	r – 17, Vashi, Navi Mumba
	owner in case of joint ownership)				Taluka & District - Thane,	Pin Code - 400 703, Stat
					<ul><li>– Maharashtra, Country –</li></ul>	India.
					Comboot Domonius	
					Contact Person: Mr. Vijesh Jain (Consultan	4\
					Mobile No. 9929977362	11)
					Mr. Ramchandra Chauhar	(Site Engineer)
					Mobile No. 9321256337	. (=
	Brief description	of the propert	y (Including Leaseho	old /	freehold etc.): Leasehold I	and
	TYPE OF THE B	BUILDING:				
	Building			_/	lumber of Floors	
	"Elite					odium Floors + 4th to 24th
	Vivanta"	Upper Resid	ential Floors as per	appr	oved plan and information	from developer.
	1 EVEL OF OOL	IDI ETEION				
	LEVEL OF CON	IPLETEION:				% of construction cost
	Building	\	Present stage of		Percentage of work	incurred certificate
	Danaing		Construction		completion	dated 27.11.2023
		Plinth	Work is in comple	ted:	10.000	
				10 000/	5.00%	
	PROPOSED DA Expected compl	TE OF COMP etion date as i	tructure is 60 years	<u>E LIF</u> s <b>31</b> .	.12.2027 (As per RERA C	ertificate)
	PROPOSED DA Expected compl Future estimate maintenance & S PROPOSED PR Vitrified floori	ATE OF COMP etion date as i d life of the S Structural repa	PLETION & FUTURE informed by builder is tructure is 60 years irs.  NITIES: rooms	E LIF s 31 s (aff	FE: .12.2027 (As per RERA Coter completion) Subject to	ertificate)
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche	TE OF COMF etion date as i d life of the S Structural repa COJECT AMEI ng tiles in all en platform w	PLETION & FUTURE informed by builder is itructure is 60 years irs.  NITIES: rooms ith Stainless Steel	E LIF s 31 s (aft	E: .12.2027 (As per RERA C ter completion) Subject to	ertificate)
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche Powder coate	TE OF COMF etion date as i d life of the S Structural repa COJECT AME ng tiles in all en platform w	PLETION & FUTURE informed by builder is itructure is 60 years irs.  NITIES: rooms ith Stainless Steel sliding windows wit	E LIF s 31 s (aft Sink	E: .12.2027 (As per RERA C ter completion) Subject to	ertificate)
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche Powder coate Laminated wo	etion date as it defined by the Structural repartition of the Stru	PLETION & FUTURE informed by builder is itructure is 60 years irs.  NITIES: rooms ith Stainless Steel	E LIF s 31 s (aft Sink	E: .12.2027 (As per RERA C ter completion) Subject to	ertificate)
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche Powder coate Laminated wo Concealed wi	TE OF COMF etion date as i d life of the S Structural repa COJECT AMEI ng tiles in all en platform w d aluminum s oden flush d	PLETION & FUTURE informed by builder is itructure is 60 years irs.  NITIES: rooms ith Stainless Steel sliding windows wit	E LIF s 31 s (aft Sink	E: .12.2027 (As per RERA C ter completion) Subject to	ertificate)
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche Powder coate Laminated wo Concealed with	etion date as id life of the Structural reparents in all the platform with daluminum strong tiles in all the platform with aluminum strong tiles in all the platform with all the plat	PLETION & FUTURE informed by builder is itructure is 60 years irs.  NITIES: rooms ith Stainless Steel sliding windows wit	E LIF s 31 s (aft Sink	E: .12.2027 (As per RERA C ter completion) Subject to	ertificate)
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche Powder coate Laminated wo Concealed wi Concealed plu Fire Fighting S	etion date as id life of the Structural reparents in all the platform with daluminum strong tiles in all the platform with aluminum strong tiles in all the platform with all the plat	PLETION & FUTURE informed by builder is itructure is 60 years irs.  NITIES: rooms ith Stainless Steel sliding windows wit	E LIF s 31 s (aft Sink	E: .12.2027 (As per RERA C ter completion) Subject to	ertificate)
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche Powder coate Laminated wo Concealed wi Concealed plu Fire Fighting S Car Parking	TE OF COMF etion date as i d life of the S Structural reparations COJECT AMEI and tiles in all en platform we d aluminum seconden flush dering umbing System	PLETION & FUTURE informed by builder is itructure is 60 years irs.  NITIES: rooms ith Stainless Steel sliding windows wit	E LIF s 31 s (aft Sink	E: .12.2027 (As per RERA C ter completion) Subject to	ertificate)
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche Powder coate Laminated wo Concealed wi Concealed plu Fire Fighting S Car Parking Fitness Cente	etion date as i d life of the S Structural repa COJECT AME Ing tiles in all en platform w d aluminum s oden flush d ring umbing System	PLETION & FUTURE informed by builder is itructure is 60 years irs.  NITIES: rooms ith Stainless Steel sliding windows wit	E LIFE S 31 S (afft	E: .12.2027 (As per RERA C ter completion) Subject to	ertificate)
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche Powder coate Laminated wo Concealed wi Concealed plu Fire Fighting S Car Parking Fitness Cente Location of prop	atte of competion date as in different date as in different date.  Coject American different date in all en platform with date and aluminum strong date.  Coject American different date in all en platform with date date in all en platform with date date.  Coject American date in all en platform with date i	PLETION & FUTURE informed by builder is itructure is 60 years irs.  NITIES: rooms ith Stainless Steel sliding windows wit	E LIFE S 31.	EE: .12.2027 (As per RERA Coter completion) Subject to  Completion Subject to	ertificate) proper, preventive period
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche Powder coate Laminated wo Concealed with Concealed plut Fire Fighting S Car Parking Fitness Cente Location of prop a) Plot No. / S	column  ATE OF COMF  etion date as i  d life of the S  Structural repa  COJECT AME  ng tiles in all  en platform w  d aluminum s  coden flush d  ring  umbing  System  r  erty	PLETION & FUTURE informed by builder is itructure is 60 years irs.  NITIES: rooms ith Stainless Steel sliding windows wit	Sink Mooor	TE:  .12.2027 (As per RERA Coter completion) Subject to  S. S. Grills  Plot No. 38C, Sector No. 1	ertificate) proper, preventive period
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche Powder coate Laminated wo Concealed plu Fire Fighting S Car Parking Fitness Cente Location of prop a) Plot No. / S b) Door No.	etion date as i d life of the S Structural repa  COJECT AMEI ng tiles in all en platform w d aluminum s oden flush d ring umbing System  r erty Survey No.	PLETION & FUTURE informed by builder is itructure is 60 years irs.  NITIES: rooms ith Stainless Steel sliding windows wit	E LIFF S 31. S (aft	FE: .12.2027 (As per RERA Coter completion) Subject to  Completion Subject to	ertificate) proper, preventive period
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche Powder coate Laminated wo Concealed wi Concealed plu Fire Fighting S Car Parking Fitness Cente Location of prop a) Plot No. / S b) Door No. c) C. T.S. No	ATE OF COMF etion date as i d life of the S Structural reparations in all eng tiles in all en platform we d aluminum second flush dering umbing System erty Survey No.	PLETION & FUTURE informed by builder is itructure is 60 years irs.  NITIES: rooms ith Stainless Steel sliding windows wit	E LIFE S 31.	E: .12.2027 (As per RERA Coter completion) Subject to  S. S. Grills  Plot No. 38C, Sector No. 1 Not applicable Village – Kharghar	ertificate) proper, preventive period
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche Powder coate Laminated wo Concealed wi Concealed plu Fire Fighting S Car Parking Fitness Cente Location of prop a) Plot No. / S b) Door No. c) C. T.S. No d) Ward / Tali	etion date as i d life of the S Structural repa COJECT AMEI ng tiles in all en platform w d aluminum s oden flush d ring umbing System  r erty Survey No.	PLETION & FUTURE informed by builder is itructure is 60 years irs.  NITIES: rooms ith Stainless Steel sliding windows wit	Sink Moor	Plot No. 38C, Sector No. 1 Not applicable Village – Kharghar Taluka – Panvel	ertificate) proper, preventive period
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche Powder coate Laminated wo Concealed wi Concealed plu Fire Fighting S Car Parking Fitness Cente Location of prop a) Plot No. / S b) Door No. c) C. T.S. No d) Ward / Tali e) Mandal / D	ATE OF COMF etion date as i d life of the S Structural repa COJECT AMEI ng tiles in all en platform w d aluminum s oden flush d ring umbing System erty Survey No.	PLETION & FUTURE Informed by builder is structure is 60 years irs.  NITIES: rooms ith Stainless Steel sliding windows with oors with Safety do	E LIFF S 31.	Plot No. 38C, Sector No. 1 Not applicable Village – Kharghar Taluka – Panvel District – Raigad	ertificate) proper, preventive period
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche Powder coate Laminated wo Concealed wi Concealed plu Fire Fighting S Car Parking Fitness Cente Location of prop a) Plot No. / S b) Door No. c) C. T.S. No d) Ward / Tali	ATE OF COMF etion date as i d life of the S Structural repa COJECT AMEI ng tiles in all en platform w d aluminum s oden flush d ring umbing System erty Survey No.	PLETION & FUTURE Informed by builder is structure is 60 years irs.  NITIES: rooms ith Stainless Steel sliding windows with oors with Safety do	Sink Moor	Plot No. 38C, Sector No. 1 Not applicable Village – Kharghar Taluka – Panvel District – Raigad "Elite Vivanta", Pro	ertificate) proper, preventive period
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche Powder coate Laminated wo Concealed wi Concealed plu Fire Fighting S Car Parking Fitness Cente Location of prop a) Plot No. / S b) Door No. c) C. T.S. No d) Ward / Tali e) Mandal / D	ATE OF COMF etion date as i d life of the S Structural repa COJECT AMEI ng tiles in all en platform w d aluminum s oden flush d ring umbing System erty Survey No.	PLETION & FUTURE Informed by builder is structure is 60 years irs.  NITIES: rooms ith Stainless Steel sliding windows with oors with Safety do	E LIFE S 31.	Plot No. 38C, Sector No. 1 Not applicable Village – Kharghar Taluka – Panvel District – Raigad "Elite Vivanta", Pro Commercial building on	ertificate) proper, preventive period  5  posed Residential cu Plot bearing Plot No. 386
	PROPOSED DA Expected compl Future estimate maintenance & S  PROPOSED PR Vitrified floori Granite Kitche Powder coate Laminated wo Concealed wi Concealed plu Fire Fighting S Car Parking Fitness Cente Location of prop a) Plot No. / S b) Door No. c) C. T.S. No d) Ward / Tali e) Mandal / D	ATE OF COMF etion date as i d life of the S Structural repa COJECT AMEI ng tiles in all en platform w d aluminum s oden flush d ring umbing System erty Survey No.	PLETION & FUTURE Informed by builder is structure is 60 years irs.  NITIES: rooms ith Stainless Steel sliding windows with oors with Safety do	Sink Mooor	Plot No. 38C, Sector No. 1 Not applicable Village – Kharghar Taluka – Panvel District – Raigad "Elite Vivanta", Pro	ertificate) proper, preventive period  5  posed Residential cu Plot bearing Plot No. 38 Jennium Empire, D – Ma





Panvel, District - Raigad, Pin Code - 410 210, State

Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 7 of 42

F	City / Town			– Maharashtra, Country – Iı	ndia			
F	City / Town			- Maharashtra, Country - India				
	,			Kharghar, Navi Mumbai				
	Residential area		:	Yes				
	Commercial area			Yes				
	Industrial area			No				
	Classification of the		:					
,	) High / Middle / Po		:	Higher Middle Class				
	i) Urban / Semi Ur		:	Urban				
	Coming under (		:	Kharghar, Navi Mumbai				
F	Panchayat / Munic	ipality		City and Industrial Dev	•			
44				Maharashtra Limited (CIDC	SO)			
		under any State / Central	:/	No				
		(e.g., Urban Land Ceiling Act)						
		gency area/ scheduled area /						
	cantonment area	Uk val land any annuaring to	ļ _	NI A				
I I	•	ultural land, any conversion to	:	N.A.				
	house site plots is  Boundaries of	contemplated						
13.	the property	As per Agreement		As per RERA Certificate	As per Site			
N	North	15 Meters Wide Road		15 Meters Wide Road	Ayyappa Mandir Road &			
					Millennium Empire			
S	South	Plot No - 38		Plot No - 38	Under Construction			
-	East	Plot No – 38A		Plot No – 38A	Building Ayyappa Mandir Road			
	West	15 Meters Wide Road		15 Meters Wide Road Tricity Eros Bui				
	Dimensions of the		l	N. A. as the land is irregular in shape				
14.1 L	Dimensions of the	Site	/	A (As per the Deed) B (Actu				
	North			- (A3 per trie beed)	D (Actuals)			
	South							
ļ	East		· ·		-			
				-	-			
	West	0.0	•	-	-			
		e & Co-ordinates of property	VC	19°02'34.0"N 73°04'41.6"E				
14. E	Extent of the site		:	Net Plot area = 2,050.70 Sc	•			
15. E	Extent of the site of	onsidered for Valuation (least		Structure - As per table atta Net Plot area = 2,050.70 So	•			
	Extent of the site of of 14A& 14B)	onsidered for valuation (least	•	INGL FIOL AIRA - 2,000.70 50	4. IVI.			
		hy the owner / tenant? If		N.A. Building Construction	work is in progress			
	Whether occupied by the owner / tenant? If occupied by tenant since how long? Rent			11.71. Dunding Constitution	work to in progress			
I I	received per month.							
	CHARACTERSTICS OF THE SITE							
	Classification of lo		:	Higher Middle class				
	Development of su	-	:	Very Good				
		ent flooding/ sub-merging	:	No				
	<u> </u>	Civic amenities like School,	:	All available near by				
	Hospital, Bus Stop			,				
	<u> </u>	opographical conditions	:	Plain				





Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 8 of 42

	on Report Prepared For: SBI / SME Vashi Turbhe Brai	nch	/ Elite Vivanta (7213/2305241) Page 8 of 42
6.	Shape of land	:	Irregular
7.	Type of use to which it can be put	:	For residential cum commercial purpose
8.	Any usage restriction		Residential cim Commercial
9.	Is plot in town planning approved layout?		11. Copy of Approved Plan No. CIDCO/BP-17102/TPO (NM & K)/2019/10852 dated 06.06.2023 issued by City and Industrial Development Corporation of Maharashtra Limited (CIDCO).  Approved upto: Ground Floor + 1st to 3rd Podium Floors + 4th to 24th Upper Residential Floors  12. Copy of Commencement Certificate No. CIDCO/BP-17102/TPO (NM & K)/2019/10852 dated 06.06.2023 issued by City and Industrial Development Corporation of Maharashtra Ltd. (CIDCO).  (This CC is endorsed for the work for Ground Floor + 1st to 3rd Podium Floors + 4th to 24th Upper Residential Floors remain valid for period
			of 1 years commencing from the date of its issue)
10.	Corner plot or intermittent plot?	:	Corner Plot
11.	Road facilities	•	Yes
12.	Type of road available at present	:	Bituminous Road
13.	Width of road – is it below 20 ft. or more than 20	:	15 M wide road
	ft.		
14.	Is it a Land – Locked land?	:	No
15.	Water potentiality	:	Municipal Water supply
16.	Underground sewerage system	:	Connected to Municipal sewer
17.	Is Power supply is available in the site	/	Yes
18.	Advantages of the site		Located in developed area
19.	Special remarks, if any like threat of acquisition of land for publics service purposes, road widening or applicability of CRZ provisions etc. (Distance from sea-cost / tidal level must be incorporated)		No Crosto
Part -	A (Valuation of land)	/ (	HE.CIECIE
1	Size of plot	:	Net Plot area = 2,050.70 Sq. M.
	North & South	:	-
	East & West	:	-
2	Total extent of the plot	:	As per table attached to the report
3	Prevailing market rate (Along With details /	:	As per table attached to the report
	reference of at least two latest deals /		Details of recent transactions/online listings are
	transactions with respect to adjacent properties		attached with the report.
	in the areas)		r · ·
4	Guideline rate obtained from the Register's	:	₹ 42,400.00 per Sq. M. for Land
	Office (evidence thereof to be enclosed)		₹ 86,800.00 per Sq. M. for Residential Flat
	,		₹ 1,27,600.00 per Sq. M. for Commercial Office
5	Assessed / adopted rate of valuation	:	As per table attached to the report
6	Estimated value of land	:	As per table attached to the report
			- b





Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 9 of 42

				urbhe Brar	ncn	/ Elite Vivanta (7213/2305241) Page 9 of 42
Part -	B (V	aluation of E	Building)			
1	Tec	hnical details	of the building		:	
	a) Type of Building (Residential / Commercial			mmercial		Residential
		/ Industrial)				
	b)	Type of con	struction (Load bearing	/ RCC /	:	R.C.C. Framed structure
		Steel Frame	d)			
	c)	Year of cons	struction			Building Construction work is in progress
	d)	Number of	floors and height of ea	ach floor		
		including ba	sement, if any			
		Building				Number of Floors
		"Elite	Proposed Residential	Building o	of G	round Floor + 1st to 3rd Podium Floors + 4th to 24th
	1	Vivanta"	Upper Residential Flo	ors as per	app	proved plan and information from developer.
	e)	Plinth area f	loor-wise		/	As per table attached to the report
	f)	Condition of	the building	1	/	
	i)	Exterior – E	Excellent, Good, Norma	ıl, Poor /		N.A. Building Construction work is in progress
	ii)	Interior – E	xcellent, Good, Normal	, Poor	:	N.A. Building Construction work is in progress
	g)	Date of iss approved ma	sue and validity of la	ayout of		<ol> <li>Copy of Approved Plan No. CIDCO/BP-17102/TPO (NM &amp; K)/2019/10852 dated 06.06.2023 issued by City and Industrial Development Corporation of Maharashtra Limited (CIDCO).</li> <li>Approved upto: Ground Floor + 1st to 3rd Podium Floors + 4th to 24th Upper Residential Floors</li> <li>Copy of Commencement Certificate No. CIDCO/BP-17102/TPO (NM &amp; K)/2019/10852 dated 06.06.2023 issued by City and Industrial Development Corporation of Maharashtra Ltd. (CIDCO).</li> <li>(This CC is endorsed for the work for Ground Floor + 1st to 3rd Podium Floors + 4th to 24th Upper Residential Floors remain valid for period of 1 years commencing from the date of its issue)</li> </ol>
	h)	Approved m	ap / plan issuing author	rity	-	City and Industrial Development Corporation of
	:\	\//la a tla a .a	Think t	മക്ക ക്ര	1.0	Maharashtra Limited (CIDCO)
	i)	_	enuineness or auther	iticity of	1	Verified TE OTE
	'\		ap / plan is verified	., ,		N. A.
	j)	•	comments by our em		:	N.A.
		valuers on a	uthentic of approved pl	an		

Specifications of construction (floor-wise) in respect of

Sr. No.	Description		
1.	Foundation	:	Proposed R.C.C. Footing
2.	Basement	:	N. A.
3.	Superstructure	:	Proposed as per IS Code requirements
4.	Joinery / Doors & Windows (Please furnish		Proposed
	details about size of frames, shutters, glazing, fitting etc. and specify the species of timber		
5.	RCC Works	:	N.A. Building Construction work is in progress
6.	Plastering	:	N.A. Building Construction work is in progress
7.	Flooring, Skirting, dado		N.A. Building Construction work is in progress





Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 10 of 42

paneling, grills etc.  Roofing including weather proof course		
Roofing including weather proof course		
	:	N.A. Building Construction work is in progress
Drainage	•	Proposed
Compound Wall	:	
Height	:	N.A. Building Construction work is in progress
Length	•	
Type of construction	:	
Electrical installation	:	N.A. Building Construction work is in progress
Type of wiring	:	
Class of fittings (superior / ordinary / poor)	:	
Number of light points	:	N.A. Building Construction work is in progress
Fan points	:	$\mathbb{R}$
Spare plug points	:,	
Any other item	/	-
a) No. of water closets and their type	:	
b) No. of wash basins	:	
c) No. of urinals	:	N.A. Building Construction work is in progress
d) No. of bath tubs	:	N.A. Dulluling Constituction work is in progress
e) Water meters, taps etc.	)	
f) Any other fixtures		
	Height Length Type of construction Electrical installation Type of wiring Class of fittings (superior / ordinary / poor) Number of light points Fan points Spare plug points Any other item Plumbing installation a) No. of water closets and their type b) No. of wash basins c) No. of urinals d) No. of bath tubs e) Water meters, taps etc.	Height : Length : Type of construction : Electrical installation : Type of wiring : Class of fittings (superior / ordinary / poor) : Number of light points : Fan points : Spare plug points : Any other item : Plumbing installation : a) No. of water closets and their type : b) No. of wash basins : c) No. of urinals : d) No. of bath tubs : e) Water meters, taps etc. : f) Any other fixtures :

Part - C (Extra Items) : Amount in ₹  1. Portico : 2. Ornamental front door : 3. Sit out / Verandah with steel grills : 4. Overhead water tank : 5. Extra steel / collapsible gates : 5. Total : 7. Wardrobes : 2. Glazed tiles : 5. Extra sinks and bath tub : 5. Interior decorations : 7. Paneling works : 7. Paneling works : 8. Aluminum works : 9. Aluminum works : 9. Aluminum hand rails : 10. False ceiling				
2. Ornamental front door 3. Sit out / Verandah with steel grills 4. Overhead water tank 5. Extra steel / collapsible gates Total Part – D (Amenities) 1. Wardrobes 2. Glazed tiles 3. Extra sinks and bath tub 4. Marble / ceramic tiles flooring 5. Interior decorations 6. Architectural elevation works 7. Paneling works 8. Aluminum works 9. Aluminum hand rails 10. False ceiling Total Part – E (Miscellaneous) 1. Separate toilet room 2. Separate lumber room 3. Separate water tank / sump Total Part – F (Services) 2. Amount in ₹	Part -	- C (Extra Items)	:	Amount in ₹
3. Sit out / Verandah with steel grills 4. Overhead water tank 5. Extra steel / collapsible gates Total  Part - D (Amenities) 1. Wardrobes 2. Glazed tiles 3. Extra sinks and bath tub 4. Marble / ceramic tiles flooring 5. Interior decorations 6. Architectural elevation works 7. Paneling works 8. Aluminum works 9. Aluminum hand rails 10. False ceiling Total  Part - E (Miscellaneous) 1. Separate toilet room 2. Separate lumber room 3. Separate water tank / sump 4. Trees, gardening Total  Part - F (Services)  N.A. Building Construction work is in progress  N.A. Building Construction work is in progress  N.A. Building Construction work is in progress	1.	Portico	:	
4. Overhead water tank :  5. Extra steel / collapsible gates :  Total :  Part – D (Amenities) : Amount in ₹  1. Wardrobes :  2. Glazed tiles :  3. Extra sinks and bath tub :  4. Marble / ceramic tiles flooring INC INC :  5. Interior decorations : N.A. Building Construction work is in progress :  6. Architectural elevation works :  7. Paneling works :  8. Aluminum works :  9. Aluminum hand rails :  10. False ceiling : Total :  Part – E (Miscellaneous) : Amount in ₹  1. Separate toilet room :  2. Separate lumber room :  3. Separate water tank / sump :  4. Trees, gardening :  Total :  Part – F (Services) : Amount in ₹	2.	Ornamental front door	:	
5. Extra steel / collapsible gates  Total  Part - D (Amenities)  1. Wardrobes  2. Glazed tiles  3. Extra sinks and bath tub  4. Marble / ceramic tiles flooring  5. Interior decorations  6. Architectural elevation works  7. Paneling works  8. Aluminum works  9. Aluminum hand rails  10. False ceiling  Total  Part - E (Miscellaneous)  1. Separate toilet room  2. Separate lumber room  3. Separate water tank / sump  4. Trees, gardening  Total  Part - F (Services)  1. Amount in ₹  N.A. Building Construction work is in progress  N.A. Building Construction work is in progress  1. Amount in ₹  Amount in ₹	3.	Sit out / Verandah with steel grills	•	N.A. Building Construction work is in progress
Total  Part - D (Amenities) : Amount in ₹  1. Wardrobes :	4.	Overhead water tank	:	
Part - D (Amenities) : Amount in ₹  1. Wardrobes : : 2. Glazed tiles : : 3. Extra sinks and bath tub : : 4. Marble / ceramic tiles flooring   N.	5.	Extra steel / collapsible gates	.)	
1. Wardrobes : 2. Glazed tiles : 3. Extra sinks and bath tub : 4. Marble / ceramic tiles flooring IN C C C C C C C C C C C C C C C C C C		Total		
2. Glazed tiles : 3. Extra sinks and bath tub : 4. Marble / ceramic tiles flooring IN . In	Part -	– D (Amenities)	• •	Amount in ₹
3. Extra sinks and bath tub  4. Marble / ceramic tiles flooring In Construction work is in progress  5. Interior decorations  6. Architectural elevation works  7. Paneling works  8. Aluminum works  9. Aluminum hand rails  10. False ceiling  Total  Part - E (Miscellaneous)  1. Separate toilet room  2. Separate lumber room  3. Separate water tank / sump  4. Trees, gardening  Total  Part - F (Services)  1. Amount in ₹  N.A. Building Construction work is in progress  N.A. Building Construction work is in progress	1.	Wardrobes		
4. Marble / ceramic tiles flooring IN	2.	Glazed tiles	/	
5. Interior decorations :   6. Architectural elevation works :   7. Paneling works :   8. Aluminum works :   9. Aluminum hand rails :   10. False ceiling :   Total :   Part - E (Miscellaneous) :   1. Separate toilet room :   2. Separate lumber room :   3. Separate water tank / sump :   4. Trees, gardening :   Total   Part - F (Services) :   Amount in ₹    Amount in ₹	3.	Extra sinks and bath tub	٠.	
6. Architectural elevation works 7. Paneling works 8. Aluminum works 9. Aluminum hand rails 10. False ceiling Total  Part - E (Miscellaneous) 1. Separate toilet room 2. Separate lumber room 3. Separate water tank / sump 4. Trees, gardening Total  Part - F (Services)  N.A. Building Construction work is in progress  Amount in ₹  Amount in ₹	4.	Marble / ceramic tiles flooring	9	vate.Create
7. Paneling works 8. Aluminum works 9. Aluminum hand rails 10. False ceiling     Total  Part - E (Miscellaneous) : Amount in ₹  1. Separate toilet room : Separate lumber room : N.A. Building Construction work is in progress  4. Trees, gardening : Total  Part - F (Services) : Amount in ₹	5.	Interior decorations	٠.	N.A. Building Construction work is in progress
8. Aluminum works 9. Aluminum hand rails 10. False ceiling Total  Part – E (Miscellaneous) 1. Separate toilet room 2. Separate lumber room 3. Separate water tank / sump 4. Trees, gardening Total  Part – F (Services)  Separate water tank / sump  Amount in ₹  Amount in ₹	6.	Architectural elevation works		N.A. Building Constituction work is in progress
9. Aluminum hand rails  10. False ceiling  Total  Part – E (Miscellaneous)  1. Separate toilet room 2. Separate lumber room 3. Separate water tank / sump 4. Trees, gardening Total  Part – F (Services)  Separate water tank / sump  Amount in ₹	7.	Paneling works		
10. False ceiling Total  Part – E (Miscellaneous)  1. Separate toilet room 2. Separate lumber room 3. Separate water tank / sump 4. Trees, gardening Total  Part – F (Services)  Separate water tank / sump  Amount in ₹  Amount in ₹				
Total  Part – E (Miscellaneous) : Amount in ₹  1. Separate toilet room : 2. Separate lumber room : 3. Separate water tank / sump : 4. Trees, gardening : Total  Part – F (Services) : Amount in ₹	9.	Aluminum hand rails		
Part – E (Miscellaneous) : Amount in ₹  1. Separate toilet room : 2. Separate lumber room : 3. Separate water tank / sump : 4. Trees, gardening : Total  Part – F (Services) : Amount in ₹	10.	False ceiling		
1. Separate toilet room : 2. Separate lumber room : 3. Separate water tank / sump : 4. Trees, gardening : Total				
2. Separate lumber room       :         3. Separate water tank / sump       :         4. Trees, gardening       :         Total       :         Part - F (Services)       :         Amount in ₹	Part -	- E (Miscellaneous)	:	Amount in ₹
3. Separate water tank / sump : N.A. Building Construction work is in progress  4. Trees, gardening : Total  Part – F (Services) : Amount in ₹	1.	Separate toilet room	٠.	
3. Separate water tank / sump : 4. Trees, gardening : Total  Part – F (Services) : Amount in ₹	2.	Separate lumber room	:	N.A. Building Construction work is in progress
Total  Part – F (Services) : Amount in ₹	3.	Separate water tank / sump	:	N.A. building Construction work is in progress
Part – F (Services) : Amount in ₹	4.	Trees, gardening	:	
		Total		
Water supply arrangements : N.A. Building Construction work is in progress	Part -	- F (Services)	:	Amount in ₹
	1.	Water supply arrangements		N.A. Building Construction work is in progress





Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 11 of 42

2.	Drainage arrangements	:		
3.	Compound wall	:		
4.	C.B. deposits, fittings etc.	:		
5.	Pavement			
	Total			

#### Total abstract of the entire property

Part – A	Land	:	
Part – B	Building	:	
	Land development	:	
Part – C	Compound wall	:	As per below table attached in the report
Part - D	Amenities	:	$\bigcirc$ $\bigcirc$ $\bigcirc$
Part – E	Pavement /	:	
Part – F	Services	:	





Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 12 of 42

CA Certificate dated 27.11.2023 by M/s. H. M. Shah & Associates

	CA Certificate dated 27.11.2023 by M/s. H. M. Shan & Assoc								
Sr. No.	Particulars Particulars	Estimated	Incurred						
1	Land Cost								
а	Value of Land as ascertained from Annual Statements of Rates (ASR)	28,36,84,917.00	28,36,84,917.00						
b	Amount of Premium payable to obtain development rights, FSI, additional FSI, fungible area, and any other incentive under DCR from Local Authority or State Government or any Statutory Authority	6,15,63,719.00	6,15,63,719.00						
С	Acquisition cost of TDR (if any)	-	-						
d	Amounts payable to State Government or competent authority or any other statutory authority of the State or Central Government, towards stamp duty, transfer charges, registration fees etc. (Stamp Duty Paid on account of Development agreement and Municipal Charges paid)	1,30,51,900.00	1,30,51,900.00						
е	Land Premium payable as per annual statement of rates (ASR) for redevelopment of land owned by public authorities.	-	-						
f	Under Rehabilitation Scheme								
g	Estimated construction cost of rehab building including site development and infrastructure IBR the same as certified by Engineer	-	-						
h	Actual Cost of construction of rehab building incurred as per the books of accounts as verified by the CA <b>Note:</b> (for total cost of construction incurred, Minimum of (i) or (ii) is to be considered).	-	-						
i	Cost towards clearance of land of all or any encumbrances including cost of removal of legal/illegal occupants, cost for providing temporary transit accommodation or rent in lieu of Transit Accommodation, overhead cost	-	-						
j	Cost of ASR linked premium, fees, charges and security deposits or maintenance deposit, or any amount whatsoever payable to any authorities towards and in project of rehabilitation	-	-						
2	Development Cost / Cost of Construction								
а	Estimated Cost of Construction as certified by Engineer	35,30,00,000.00	97,54,317.00						
b	Actual Cost of construction incurred as per the books of accounts as verified by the CA	eate -	1,37,55,000.00						
С	Onsite expenditure for development of entire project excluding cost (iii) of construction as per (i) or (ii) above, i.e., salaries, consultants' fees, site overheads, development works, cost of services (including water, electricity, sewerage, drainage, layout roads etc.), cost of machineries and equipment including its hire and maintenance costs, consumables etc. All costs directly incurred to complete the construction of the entire phase of the project registered	4,50,00,000.00	45,08,968.00						
i	Payment of Taxes, cess, fees, charges, premiums, interest etc. to any statutory Authority Including all Charges paid to Municipality	4,50,00,000.00	1,62,35,806.00						
ii	Principal sum and interest payable to financial institutions, scheduled banks, non-banking financial institution (NBFC) or money lenders on construction funding or money borrowed for construction	-	-						
	TOTAL	80,13,00,536.00	39,93,49,626.00						
	-	, , , ,	, , -,						



Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 13 of 42

**Construction Area as per Approved Plan** 

	Construction Area as per Approved Flair											
Sr. No.	Floor	Built Up Area in Sq. M.	Other Area in Sq. M.	Total Construction Area in Sq. M.								
1	Ground Floor	612.86	612.10	1,224.97								
2	1st Floor	-	1,232.77	1,232.77								
3	2nd Floor	•	1,232.77	1,232.77								
4	3rd Floor	ı	1,232.77	1,232.77								
5	4th Floor	442.90	35.76	478.66								
6	5th Floor	441.55	35.76	477.31								
7	6th Floor	441.55	35.76	477.31								
8	7th Floor	441.55	35.76	477.31								
9	8th Floor	441.55	35.76	477.31								
10	9th Floor	441.55	35.76	477.31								
11	10th Floor	441.55	35.76	477.31								
12	11th Floor	441.55	35.76	477.31								
13	12th Floor	441.55	35.76	477.31								
14	13th Floor	441.55	35.76	477.31								
15	14th Floor	441.55	35.76	477.31								
16	15th Floor	441.55	35.76	477.31								
17	16th Floor	441.55	35.76	477.31								
18	17th Floor	441.55	35.76	477.31								
19	18th Floor	441.55	35.76	477.31								
20	19th Floor	441.55	35.76	477.31								
21	20th Floor	441.55	35.76	477.31								
22	21st Floor	441.55	35.76	477.31								
23	22nd Floor	441.55	35.76	477.31								
24	23rd Floor	441.55	35.76	477.31								
25	24th Floor	441.55	35.76	477.31								
26	OHT / LMR	-	35.76	35.76								
Tota	l Area in Sq. M.	9,886.83	5,097.12	14,983.94								

Think.Innovate.Create



S. No.	Floor No.	Shop No / Flat No.	Comp.	RERA Carpet Area in Sq. M.	RERA Carpet Area in Sq. Ft.	Balcony Area in Sq. M.	Balcony Area in Sq. Ft.	Total Carpet Area in Sq. Ft.	Built Up Area in Sq. Ft.	Sold / Unsold Inventory
1	Ground Floor	1	Shop	58.18	626.00	1	-	626.00	689.00	Unsold
2	Ground Floor	2	Shop	39.21	422.00	-	-	422.00	464.00	Unsold
3	Ground Floor	3	Shop	44.59	480.00	-	-	480.00	528.00	Unsold
4	Ground Floor	4	Shop	43.16	465.00	-	R	465.00	512.00	Unsold
5	Ground Floor	5	Shop	91.90	989.00	i	1	989.00	1,088.00	Unsold
6	Ground Floor	6	Shop	20.34	219.00	ı	-	219.00	241.00	Unsold
7	Ground Floor	7	Shop	30.31	326.00	-	-	326.00	359.00	Unsold
8	Ground Floor	8	Shop	34.87	375.00		-	375.00	413.00	Unsold
9	Ground Floor	9	Shop	25.05	270.00	-	-	270.00	297.00	Unsold
10	Ground Floor	10	Shop	29.96	322.00	/-	-/	322.00	354.00	Unsold
11	Ground Floor	11	Shop	29.96	322.00	-	-	322.00	354.00	Unsold
12	Ground Floor	12	Shop	25.05	270.00	-	-	270.00	297.00	Unsold
13	Ground Floor	13	Shop	32.91	354.00	1	-	354.00	389.00	Unsold
14	Ground Floor	14	Shop	33.40	360.00	<u> </u>	-	360.00	396.00	Unsold
15	1st Floor		Podium	ı	•	,	-	•	•	Podium
16	2nd Floor		Podium	mmk.	.IIIIO\	rare.	Clec	<u>.</u>	-	Podium
17	3rd Floor		Podium	-	-	-	-	-	-	Podium
18	4th Floor	401	3 BHK	93.88	1,010.52	-	-	1,010.52	1,112.00	Unsold
19	4th Floor	402	3 BHK	95.05	1,023.12	ı	1	1,023.12	1,125.00	Unsold
20	4th Floor	403	Society Office	-	1	1	-	-	-	Society Office
21	4th Floor	404	Fitness Center	-	-	ı	-	-	-	Fitness Center
22	5th Floor	501	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold
23	5th Floor	502	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold
24	5th	503	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold





Valua	Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 15 of 42											
S. No.	Floor No.	Shop No / Flat No.	Comp.	RERA Carpet Area in Sq. M.	RERA Carpet Area in Sq. Ft.	Balcony Area in Sq. M.	Balcony Area in Sq. Ft.	Total Carpet Area in Sq. Ft.	Built Up Area in Sq. Ft.	Sold / Unsold Inventory		
	Floor											
25	5th Floor	504	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
26	6th Floor	601	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
27	6th Floor	602	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
28	6th Floor	603	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		
29	6th Floor	604	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
30	7th Floor	701	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
31	7th Floor	702	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
32	7th Floor	703	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		
33	7th Floor	704	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
34	8th Floor	801	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
35	8th Floor	802	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
36	8th Floor	803	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		
37	8th Floor	804	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
38	9th Floor	901	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
39	9th Floor	902	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
40	9th Floor	903	2 BHK	64,92	698.80	/af.01.	65.00	11 263.80	840.00	Unsold		
41	9th Floor	904	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
42	10th Floor	1001	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
43	10th Floor	1002	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
44	10th Floor	1003	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		
45	10th Floor	1004	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
46	11th Floor	1101	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
47	11th Floor	1102	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
48	11th Floor	1103	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		





Valua	Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 16 of 42											
S. No.	Floor No.	Shop No / Flat No.	Comp.	RERA Carpet Area in Sq. M.	RERA Carpet Area in Sq. Ft.	Balcony Area in Sq. M.	Balcony Area in Sq. Ft.	Total Carpet Area in Sq. Ft.	Built Up Area in Sq. Ft.	Sold / Unsold Inventory		
49	11th Floor	1104	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
50	12th Floor	1201	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
51	12th Floor	1202	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
52	12th Floor	1203	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		
53	12th Floor	1204	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
54	13th Floor	1301	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
55	13th Floor	1302	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
56	13th Floor	1303	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		
57	13th Floor	1304	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
58	14th Floor	1401	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
59	14th Floor	1402	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
60	14th Floor	1403	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		
61	14th Floor	1404	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
62	15th Floor	1501	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
63	15th Floor	1502	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
64	15th Floor	1503	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		
65	15th Floor	1504	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
66	16th Floor	1601	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
67	16th Floor	1602	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
68	16th Floor	1603	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		
69	16th Floor	1604	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
70	17th Floor	1701	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
71	17th Floor	1702	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
72	17th Floor	1703	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		
73	17th	1704	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		





Valua	Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 17 of 42											
S. No.	Floor No.	Shop No / Flat No.	Comp.	RERA Carpet Area in Sq. M.	RERA Carpet Area in Sq. Ft.	Balcony Area in Sq. M.	Balcony Area in Sq. Ft.	Total Carpet Area in Sq. Ft.	Built Up Area in Sq. Ft.	Sold / Unsold Inventory		
	Floor											
74	18th Floor	1801	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
75	18th Floor	1802	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
76	18th Floor	1803	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		
77	18th Floor	1804	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
78	19th Floor	1901	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
79	19th Floor	1902	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
80	19th Floor	1903	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		
81	19th Floor	1904	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
82	20th Floor	2001	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
83	20th Floor	2002	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
84	20th Floor	2003	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		
85	20th Floor	2004	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
86	21st Floor	2101	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
87	21st Floor	2102	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
88	21st Floor	2103	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		
89	21st Floor	2104	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
90	22nd Floor	2201	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
91	22nd Floor	2202	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
92	22nd Floor	2203	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		
93	22nd Floor	2204	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		
94	23rd Floor	2301	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold		
95	23rd Floor	2302	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold		
96	23rd Floor	2303	2 BHK	64.92	698.80	6.01	65.00	763.80	840.00	Unsold		
97	23rd Floor	2304	2 BHK	65.61	706.23	6.01	65.00	771.23	848.00	Unsold		





Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 18 of 42

S. No.	Floor No.	Shop No / Flat No.	Comp.	RERA Carpet Area in Sq. M.	RERA Carpet Area in Sq. Ft.	Balcony Area in Sq. M.	Balcony Area in Sq. Ft.	Total Carpet Area in Sq. Ft.	Built Up Area in Sq. Ft.	Sold / Unsold Inventory
98	24th Floor	2401	3 BHK	86.99	936.36	7.50	81.00	1,017.36	1,119.00	Unsold
99	24th Floor	2402	3 BHK	88.15	948.85	6.60	71.00	1,019.85	1,122.00	Unsold
100	24th Floor	2403	4 BHK	131.01	1,410.19	12.03	129.00	1,539.19	1,693.00	Unsold
	Total				73,643.60	522.41	5,639.00	79,282.60	87,203.00	

Unsold Flats Inventory R

S. No.	Floor	Flat No.	Comp.	RERA Carpet Area in Sq. Ft.	Balcony Area in Sq. Ft.	Total Carpet Area in Sq. Ft.	Built Up Area in Sq. Ft.	Rate per Sq. Ft. on Carpet Area	Value in ₹
1	4th Floor	401	3 BHK	1,010.52	-	1,010.52	1,112.00	18,000.00	1,81,89,360.00
2	4th Floor	402	3 BHK	1,023.12	-	1,023.12	1,125.00	18,000.00	1,84,16,160.00
3	5th Floor	501	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00
4	5th Floor	502	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00
5	5th Floor	503	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00
6	5th Floor	504	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00
7	6th Floor	601	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00
8	6th Floor	602	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00
9	6th Floor	603	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00
10	6th Floor	604	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00
11	7th Floor	701	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00
12	7th Floor	702	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00
13	7th Floor	703	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00
14	7th Floor	704	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00
15	8th Floor	801	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00
16	8th Floor	802	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00
17	8th Floor	803	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00



Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 19 of 42

value	aluation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 19 of 42									
S. No.	Floor	Flat No.	Comp.	RERA Carpet Area in Sq. Ft.	Balcony Area in Sq. Ft.	Total Carpet Area in Sq. Ft.	Built Up Area in Sq. Ft.	Rate per Sq. Ft. on Carpet Area	Value in ₹	
18	8th Floor	804	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00	
19	9th Floor	901	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00	
20	9th Floor	902	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00	
21	9th Floor	903	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00	
22	9th Floor	904	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00	
23	10th Floor	1001	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00	
24	10th Floor	1002	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00	
25	10th Floor	1003	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00	
26	10th Floor	1004	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00	
27	11th Floor	1101	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00	
28	11th Floor	1102	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00	
29	11th Floor	1103	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00	
30	11th Floor	1104	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00	
31	12th Floor	1201	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00	
32	12th Floor	1202	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00	
33	12th Floor	1203	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00	
34	12th Floor	1204	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00	
35	13th Floor	1301	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00	
36	13th Floor	1302	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00	
37	13th Floor	1303	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00	
38	13th Floor	1304	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00	
39	14th Floor	1401	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00	
40	14th Floor	1402	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00	
41	14th Floor	1403	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00	





Valua	Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 20 of 42											
S. No.	Floor	Flat No.	Comp.	RERA Carpet Area in Sq. Ft.	Balcony Area in Sq. Ft.	Total Carpet Area in Sq. Ft.	Built Up Area in Sq. Ft.	Rate per Sq. Ft. on Carpet Area	Value in ₹			
42	14th Floor	1404	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00			
43	15th Floor	1501	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00			
44	15th Floor	1502	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00			
45	15th Floor	1503	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00			
46	15th Floor	1504	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00			
47	16th Floor	1601	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00			
48	16th Floor	1602	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00			
49	16th Floor	1603	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00			
50	16th Floor	1604	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00			
51	17th Floor	1701	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00			
52	17th Floor	1702	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00			
53	17th Floor	1703	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00			
54	17th Floor	1704	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00			
55	18th Floor	1801	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00			
56	18th Floor	1802	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00			
57	18th Floor	1803	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00			
58	18th Floor	1804	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00			
59	19th Floor	1901	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00			
60	19th Floor	1902	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00			
61	19th Floor	1903	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00			
62	19th Floor	1904	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00			
63	20th Floor	2001	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00			
64	20th Floor	2002	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00			
65	20th Floor	2003	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00			





Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 21 of 42

Valua	шоп кер	on Piep	areu For.	vivania (721)	3/2305241) Pa	age 21 01 42			
S. No.	Floor	Flat No.	Comp.	RERA Carpet Area in Sq. Ft.	Balcony Area in Sq. Ft.	Total Carpet Area in Sq. Ft.	Built Up Area in Sq. Ft.	Rate per Sq. Ft. on Carpet Area	Value in ₹
66	20th Floor	2004	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00
67	21st Floor	2101	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00
68	21st Floor	2102	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00
69	21st Floor	2103	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00
70	21st Floor	2104	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00
71	22nd Floor	2201	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00
72	22nd Floor	2202	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00
73	22nd Floor	2203	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00
74	22nd Floor	2204	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00
75	23rd Floor	2301	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00
76	23rd Floor	2302	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00
77	23rd Floor	2303	2 BHK	698.80	65.00	763.80	840.00	18,000.00	1,37,48,400.00
78	23rd Floor	2304	2 BHK	706.23	65.00	771.23	848.00	18,000.00	1,38,82,140.00
79	24th Floor	2401	3 BHK	936.36	81.00	1,017.36	1,119.00	18,000.00	1,83,12,480.00
80	24th Floor	2402	3 BHK	948.85	71.00	1,019.85	1,122.00	18,000.00	1,83,57,300.00
81	24th Floor	2403	4 BHK	1,410.19	129.00	1,539.19	1,693.00	18,000.00	2,77,05,420.00
	Total			67,843.60	5,639.00	73,482.60	80,822.00		1,32,26,86,800.00



Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 22 of 42

**Unsold Flats Inventory** 

S. No.	Floor	Shop No.	Comp.	RERA Carpet Area in Sq. Ft.	Built UP Area in Sq. Ft.	Rate per Sq. Ft. on Carpet Area	Value in ₹
1	Ground Floor	1	Shop	626.00	689.00	36,000.00	2,25,36,000.00
2	Ground Floor	2	Shop	422.00	464.00	36,000.00	1,51,92,000.00
3	Ground Floor	3	Shop	480.00	528.00	36,000.00	1,72,80,000.00
4	Ground Floor	4	Shop	465.00	512.00	36,000.00	1,67,40,000.00
5	Ground Floor	5	Shop	989.00	1,088.00	36,000.00	3,56,04,000.00
6	Ground Floor	6	Shop	219.00	241.00	36,000.00	78,84,000.00
7	Ground Floor	7	Shop	326.00	359.00	36,000.00	1,17,36,000.00
8	Ground Floor	8 /	Shop	375.00	413.00	36,000.00	1,35,00,000.00
9	Ground Floor	9	Shop	270.00	297.00	36,000.00	97,20,000.00
10	Ground Floor	/10	Shop	322.00	354.00	36,000.00	1,15,92,000.00
11	Ground Floor	11	Shop	322.00	354.00	36,000.00	1,15,92,000.00
12	Ground Floor	12	Shop	270.00	297.00	36,000.00	97,20,000.00
13	Ground Floor	13	Shop	354.00	389.00	36,000.00	1,27,44,000.00
14	Ground Floor	14	Shop	360.00	396.00	36,000.00	1,29,60,000.00
	Tota			5,800.00	6,381.00		20,88,00,000.00

## **TOTAL SUMMARY**

Particulars	No. of Units	Total Carpet Area in Sq. Ft.	Rate in ₹	Market Value in ₹
Unsold Flats	81.00	73,482.60	18,000.00	132,26,86,800.00
Unsold Shops	14.00	5,800.00	36,000.00	20,88,00,000.00
Total	95.00	79,282.60		153,14,86,800.00
Total Income from Sale in Cr. 153.15				

## **COST OF PROJECT**

OOT OF TROOPER				
Project expenses	Incurred	To be Incurred	Total	
T Tojout expenses	Cost in ₹ Cr.	Cost in ₹ Cr.	(₹ in Cr.)	
Land & Stamp Duty Cost	27.35	-	27.35	
Construction Cost of Building	2.04	35.42	37.46	
Approval Cost of Fungible Cost & Development charges	7.78	-	7.78	
Architect Cost, RCC & other Professional fees			1.87	
Administrative Expenses	1 + 0.045	OTE 6.73	2.25	
Marketing Expenses			3.06	
Interest Cost	-	7.08	7.08	
Contiguous Cost	-	1.12	1.12	
TOTAL COST	37.62	50.36	87.98	



Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 23 of 42

#### Land Cost:

As per Present Ready Reckoner rate the Project Land Value is ₹ 8.69 Cr. considering Land Rate @ ₹42,400.00 per Sq. M. & Net Plot Area of 2,050.70 Sq. M.

As per document purchase cost of land & stamp duty cost is ₹ 27,34,89,550.00 i.e., ₹ 27.35 Cr. which is 31.09% of Total Project Cost.

Sr.	Agreement Name	Date	Particulars	Total Cost in ₹	Incurred Cost in ₹		
1			Purchase	26,04,36,850.00	26,04,36,850.00		
2	I a a a a A a wa a ma mb	t 11.07.2019	Stamp Duty	1,30,22,000.00	1,30,22,000.00		
3	Lease Agreement		11.07.2019	11.07.2019	11.07.2019		30,000.00
4			Reg. Fees	700.00	700.00		
	TOTAL			27,34,89,550.00	27,34,89,550.00		

#### > Building Cost of Construction for Building:

Construction Area of Building = 14,983.94 Sq. M. i.e., 1,61,287.16 Sq. Ft.

Total estimated cost for construction of Building (includes cost of RCC work, manpower, lift, material, painting, finishing work, site development, etc.) is ₹37,45,98,575.00 i.e., ₹37.46 Cr. which comes ₹25,000.00 per Sq. M. on construction area for building.

The total construction area is 14,983.94 Sq. M., projected cost of ₹37.46 Cr is 42.58% of total project cost VCIPL opinion the construction cost of 25,000/- Per Sq. M. which is in line with Market-Trend.

Particulars Particulars	Rate per Sq. M.
Excavation Work	1,500.00
RCC Work	15,000.00
Final Finishing Work	5,000.00
Other Work	3,500.00
Cost of Construction	25,000.00

#### > Approval Charges:

The Total Approval Cost (Fungible Cost & Development Cess Premium & TDR Cost) as per architect letter will be ₹7,77,99,525.00 i.e., ₹7.78Cr. which is 8.84% of Total Project Cost. Builder has paid ₹7.78 Cr.

Sr. No.	Particulars	Total Cost in ₹	Incurred Cost in ₹
1	Development Charges	6,15,63,719.00	6,15,63,719.00
2	Labour Cess	1,62,35,806.00	1,62,35,806.00
Total		7,77,99,525.00	7,77,99,525.00

As per information provided by developer. Innovate. Create

#### Architect Cost, RCC & Other Professional Charges:

The total Architect charges of ₹1,87,29,929.00 i.e., ₹1.87 Cr. is 5% of construction cost of building & it is line up with Market trend.

The professional charge consists of Architect & Legal which in market is in the range of 2% - 5% of Total Construction cost of the project.

#### Administrative Expenses:

Salaries, site overheads, development works, cost of services (including water, electricity, sewerage, drainage, layout roads etc.), cost of machineries and equipment including its hire and maintenance cost, consumables etc. All costs directly incurred to complete the construction of the entire phase of the project registered is estimated 6% of construction cost of building which comes to ₹2,24,75,915.00 i.e., ₹2.25 Cr.

The admin charges which in market is in the range of 4% - 6% of Total Construction cost of the project.





Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 24 of 42

#### > Marketing Expenses:

Marketing costs directly incurred to complete the construction of the entire phase of the project registered is estimated at 2% of total Sale income from the project which comes to ₹3,06,29,736.00 i.e., ₹3.06 Cr. The marketing charge consists of brokerage & commission which in market is in the range of 1% - 3% of Total Sale income of the property.

#### > Interest Costs:

The Interest cost for the term loan is ₹7,08,00,000.00 i.e., ₹7.08 Cr., which is 8.05% of total project cost. As per information provided by the client.

#### > Contingency Costs:

The contingency charges estimated at 3% construction cost of building which comes to ₹1,12,37,957.00 i.e., ₹1.12 Cr.

#### PROFIT FROM THE PROJECT:

TROTTI ROM THE TROCEST.			
Particulars Particulars	Amount (₹ in Cr.)		
Gross Estimated Revenue	153.15		
Less: Total projected Expenses	87.98		
Estimated Surplus	65.17		
Project Cost and Developer Profit			
Developer Profit @ 30% of estimated surplus	19.55		
Net Surplus (3-4)	45.62		
PV (discounted @ 8% for 2 years)	Rs. 33.53		
Add:			
Expenses already incurred as on date	37.62		
(As per the certified Trial Balance Sheet of the project)			
Less:	-		
Present Value of the project potential/ Land Value as on Date	Rs. 71.15		
The realizable value of the property	Rs. 64.04		
Distress value of the property	Rs. 56.92		

Think.Innovate.Create



## **Actual Site Photographs**

















# Route Map of the property $\frac{\text{Site } \mu/r}{}$





#### Latitude Longitude: 19°02'34.0"N 73°04'41.6"E


Note: The Blue line shows the route to site from nearest metro station (Kharghar Village – 1.30 Km.)





Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 27 of 42

## Ready Reckoner 2023 - 2024

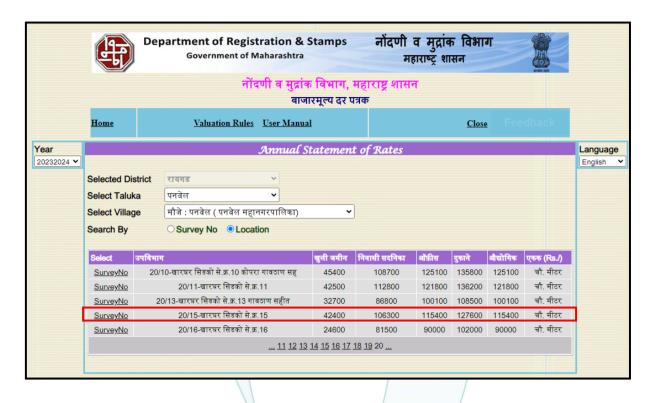





## **Registered Sales Instances**

1068529	सूची क्र.2	दुय्यम निबंधक : सह दु.नि.पनवेल 5
29-02-2024	X41 N.2	दस्त क्रमांक : 1068/2024
Note:-Generated Through eSearch		नोदंणी :
Module, For original report please contact concern SRO office.		Regn:63m
	गावाचे नाव: खारघर	
(1)विलेखाचा प्रकार	करारनामा	
(2)मोबदला	9525000	
(3) बाजारभाव(भाडेपटटयाच्या बाबतितपटटाकार आकारणी देतो की पटटेदार ते नमुद करावे)		
(4) भू-मापन,पोटहिस्सा व घरक्रमांक(असल्यास)	1) पालिकेचे नाव:पनवेल म.न.पा.इतर वर्णन :, इतर माहिती: विभाग क्र-20/34,दर-98900/-प्रती चौ.मी.सदिनका नं.802,आठवा मजला,निहारिका रेसिडेन्सी को-ऑपरेटिव्ह हौिसंग सोसायटी लिमिटेड,प्लॉट नं.15,17,18,18ए,19 आणि 20,सेक्टर 34बी,ओवे-खारघर नवी मुंबई.ता.पनवेल,जि,रायगड,क्षेत्र-49.91 चौ.मी.कारपेट एरिया,8.626 चौ.मी पॉकेट टेरेस +3.64 चौ.मी फ्लॉवर बेड .(( Plot Number : १५,१७,१८,१८ए, १९;))	
(5) क्षेत्रफळ 49.911 चौ.मीटर		
(6)आकारणी किंवा जुडी देण्यात असेल तेव्हा.	ारणी किंवा जुडी देण्यात असेल	
(७) दस्तऐवज करुन देणा-या/लिहून ठेवणा-या पक्षकाराचे नाव किंवा दिवाणी न्यायालयाचा हुकुमनामा किंवा आदेश असल्यास,प्रतिवादिचे नाव व पत्ता.		
(8)दस्तऐवज करुन घेणा-या पक्षकाराचे व किंवा दिवाणी न्यायालयाचा हुकुमनामा किंवा आदेश असल्यास,प्रतिवादिचे नाव व पत्ता	मा पॉइंट, प्लॉट क्र. 58,59 आणि 60, सेक्टर 18, खारघर, नवी मुंबई, ब्लॉक नं: -, रोड नं: -, महाराष्ट्र,	
(9) दस्तऐवज करुन दिल्याचा दिनांक	चा दिनांक 20/01/2024	
(10)दस्त नोंदणी केल्याचा दिनांक	20/01/2024	
(11)अनुक्रमांक,खंड व पृष्ठ	1068/2024	
(12)बाजारभावाप्रमाणे मुद्रांक शुल्क 666800		
(13)बाजारभावाप्रमाणे नोंदणी शुल्क 30000		





### **Registered Sales Instances**

104086	सूची क्र.2	दुय्यम निबंधक : दु.नि. पनवेल 1
29-02-2024	(Z41 Nr.2	दुस्यम । नवयक : पु.1न. पनपर। 1 दस्त क्रमांक : 1040/2024
Note:-Generated Through eSearch		नोदंणी :
Module,For original report please contact concern SRO office.		
Contact concern SNO office.		Regn:63m
	गावाचे नाव: खारघर	
(1)विलेखाचा प्रकार	करारनामा	
(2)मोबदला	11800000	
(3) बाजारभाव(भाडेपटटयाच्या	9476550.27	
बाबतितपटटाकार आकारणी देतो की पटटेदार ते नमुद करावे)		
(4) भू-मापन,पोटहिस्सा व घरक्रमांक(असल्यास)	<ol> <li>पालिकेचे नावःरायगडइतर वर्णन :, इ</li> </ol>	
धरक्रमाक(असल्यास)		ोरया हाईट्स को. ऑप. हौसिंग सोसायटी
	लि.,प्लॉट नं. 15,16 आणि 17,सेक्टर नं.	
	पनवेल,जिल्हा - रायगड,क्षेत्रफळ ७७२.२०	0 चा. फूट कारपट एरिया + 50 चा. फूट AND 17 ; SECTOR NUMBER : 18 ;
	))	AND 17; SECTOR NUMBER: 18;
(5) क्षेत्रफळ	772.20	
(6)आकारणी किंवा जुडी देण्यात असेल तेव्हा.		
(७) दस्तऐवज करुन देणा-या/लिहून	1): नाव:-विनोद कुमार खिलनानी वय:-63 पत्त	
ठेवणा-या पक्षकाराचे नाव किंवा दिवाणी न्यायालयाचा हुकुमनामा किंवा आदेश	वनश्री सीएचएसएल, सेक्टर नं. ५८ए, एनआरआय	
न्यायालयाचा हुकुमनामा किंवा आदेश असल्यास,प्रतिवादिचे नाव व पत्ता. ब्लॉक नं: -, रोड नं: -, महाराष्ट्र, THANE. पिन कोड:-400706 पॅन नं:-AIRPK6342E		75:-400/00 41 1:-AIRFR0342E
(8)दस्तऐवज करुन घेणा-या पक्षकाराचे	1): नाव:-नानाजी क्षीरसागर वय:-49; पत्ता:-प	लॉट नं: -, माळा नं: -, इमारतीचे नाव: ए-३, ४०२-
व किंवा दिवाणी न्यायालयाचा हुकुमनामा		ट नं. ५५, सेक्टर नं. २०, खारघर, नवी मुंबई, ब्लॉक
किंवा आदेश असल्यास,प्रतिवादिचे नाव व पत्ता	नं: -, रोड नं: -, महाराष्ट्र, राईग़ार्:(ं:).     पिन कोड	:-410210  पैन ने:-AMJPK2697L . पत्ता:-प्लॉट ने: -, माळा ने: -, इमारतीचे नाव: ए-३,
व पत्ता		, पत्ता:-प्लाट न: -, माळा न: -, इमारताच नाव: ए-३, इ, प्लॉट नं. ५५, सेक्टर नं. २०, खारघर, नवी मुंबई,
	ब्लॉक नं: -, रोड नं: -, महाराष्ट्र, राईग़ारू:(ं:). पि	न कोड:-410210  पॅन नं:-AOVPB1326B
(9) दस्तऐवज करुन दिल्याचा दिनांक	13/02/2024	
(10)दस्त नोंदणी केल्याचा दिनांक	13/02/2024	
(11)अनुक्रमांक,खंड व पृष्ठ	1040/2024	
(12)बाजारभावाप्रमाणे मुद्रांक शुल्क	826000	
(13)बाजारभावाप्रमाणे नोंदणी शुल्क 30000		



# Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 30 of 42 **Price Indicators for Flats**




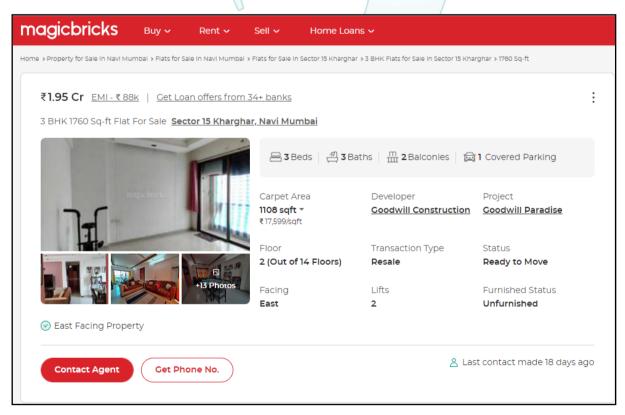






# Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 31 of 42 **Price Indicators for Flats**

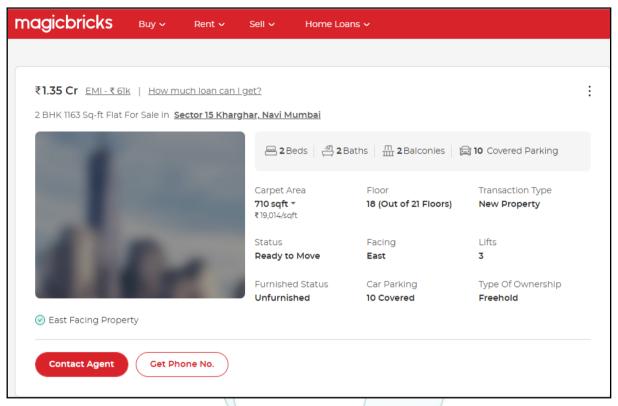

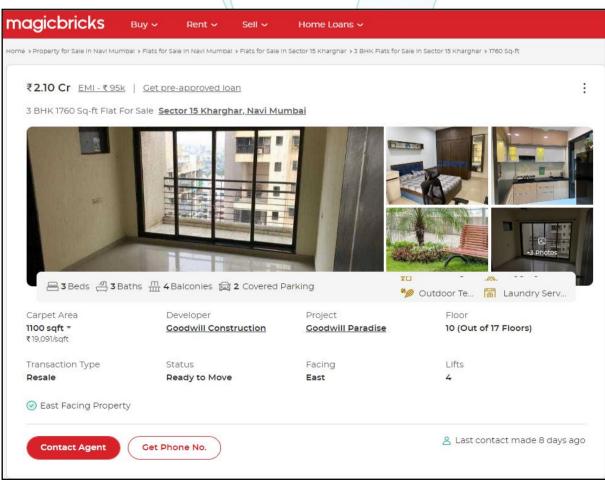





Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 32 of 42

## Justification for price /rate

The Market Value of the property is based on facts of markets discovered by us during our enquiries, however the government rate value in this case is less than the market value arrived by us. We are of the opinion that the value arrive by us will prove to be correct if an Auction of the subject property is carried out. As far as Market Value in Index II is concerned, it is not possible to comment on same, may be government rates are fixed by sampling during same point of time in part and whereas, Market values change every month.

In most of the cases the actual deal amount or Transaction value is not reflected in Index II because of various Market practices. As Valuer, we always try to give a value which is correct reflection of actual transaction value irrespective of any factors in market.

We hope this will satisfy your requirements.

Think.Innovate.Create



Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 33 of 42 As a result of my appraisal and analysis, it is my considered opinion that the realizable Value of the above property in the prevailing condition with aforesaid specification is **(As per table attached to the report)** 

Place: Mumbai Date: 22.02.2024

For VASTUKALA CONSULTANTS (I) PVT. LTD.

Director

Manoj B. Chalikwar

Registered Valuer

Chartered Engineer (India) Reg. No. IBBI / RV / 07/2018/10366

Reg. No. CAT-I-F-1763

SBI Empanelment No.: SME/TCC/2021-22/86/3

Auth. Sign.

Enc	losures			
	Declaration-cum-undertaking from the valuer	r (Annexure- I)	Attached	
	Model code of conduct for valuer - (Annexure	e - II)	Attached	
		/	/	

Think.Innovate.Create



(Annexure-I)

#### **DECLARATION-CUM-UNDERTAKING**

- I, Manoj Chalikwar son of Shri. Baburao Chalikwar do hereby solemnly affirm and state that:
- a. I am a citizen of India.
- b. I will not undertake valuation of any assets in which I have a direct or indirect interest or become so interested at any time during a period of three years prior to my appointment as valuer or three years after the valuation of assets was conducted by me.
- c. The information furnished in my valuation report dated 22.02.2024 is true and correct to the best of my knowledge and belief and I have made an impartial and true valuation of the property.
- d. I/ my authorized representative have personally inspected the property on 31.01.2024. The work is not sub contracted to any other valuer and carried out by myself.
- e. Valuation report is submitted in the format as prescribed by the bank.
- f. I have not been depanelled / delisted by any other bank and in case any such depanelment by other banks during my empanelment with you, I will inform you within 3 days of such depanelment.
- g. I have not been removed / dismissed from service / employment earlier.
- h. I have not been convicted of any offence and sentenced to a term of imprisonment
- i. I have not been found guilty of misconduct in my professional capacity.
- i. I have not been declared to be unsound mind
- k. I am not an undischarged bankrupt, or has not applied to be adjudicated as a bankrupt;
- I. I am not an undischarged insolvent.
- m. I have not been levied a penalty under section 271J of Income-tax Act, 1961 (43 of 1961) and time limit for filing appeal before Commissioner of Income-tax (Appeals) or Income-tax Appellate Tribunal, as the case may be has expired, or such penalty has been confirmed by Income-tax Appellate Tribunal, and five years have not elapsed after levy of such penalty
- n. I have not been convicted of an offence connected with any proceeding under the Income Tax Act 1961, Wealth Tax Act 1957 or Gift Tax Act 1958 and
- o. My PAN Card number as applicable is AERPC9086P
- p. I undertake to keep you informed of any events or happenings which would make me ineligible for empanelment as a valuer
- q. I have not concealed or suppressed any material information, facts and records and I have made a complete and full disclosure



Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 35 of 42

- r. I have read the Handbook on Policy, Standards and procedure for Real Estate Valuation, 2011 of the IBA and this report is in conformity to the "Standards" enshrined for valuation in the Part B of the above handbook to the best of my ability.
- s. I have read the International Valuation Standards (IVS) and the report submitted to the Bank for the respective asset class is in conformity to the "Standards" as enshrined for valuation in the IVS in "General Standards" and "Asset Standards" as applicable. The valuation report is submitted in the prescribed format of the bank.
- t. I abide by the Model Code of Conduct for empanelment of valuer in the Bank. (Annexure V A signed copy of same to be taken and kept along with this declaration)
- u. I am valuer registered with Insolvency & Bankruptcy Board of India (IBBI)
- v. My CIBIL Score and credit worthiness is as per Bank's guidelines.
- w. I am Chairman & Managing Director of the company, who is competent to sign this valuation report.
- x. I will undertake the valuation work on receipt of Letter of Engagement generated from the system (i.e., LLMS / LOS) only.
- y. Further, I hereby provide the following information.

Think.Innovate.Create



	Particulars	Valuer comment
1.	Background information of the asset being valued;	The property under consideration is developed by M/s. Nathdwara Developers Pvt. Ltd
2.	Purpose of valuation and appointing authority	As per request from State Bank of India, SME – Vashi Turbhe Branch to assess Fair Market value of the Project for bank loan purpose.
3.	Identity of the Valuer and any other experts involved in the valuation;	Manoj B. Chalikwar – Regd. Valuer Umang Ashwin Patel – Regd. Valuer Prayush P. Parekh – Senior Valuation Engineer Vaibhav Bhagat – Valuation Engineer
4.	Disclosure of Valuer interest or conflict, if any;	We have no interest, either direct or indirect, in the property valued. Further to state that we do not have relation or any connection with property owner / applicant directly or indirectly. Further to state that we are an independent Valuer and in no way related to property owner / applicant
5.	Date of appointment, valuation date and date of report;	Date of Appointment – 30.01.2024  Valuation Date – 22.02.2024  Date of Report – 22.02.2024
6.	Inspections and/or investigations undertaken;	Physical Inspection done on date 31.01.2024
7.	Nature and sources of the information used or relied upon;	<ul> <li>Market Survey at the time of site visit</li> <li>Ready Reckoner rates / Circle rates</li> <li>Online search for Registered Transactions</li> <li>Online Price Indicators on real estate portals</li> <li>Enquiries with Real estate consultants</li> <li>Existing data of Valuation assignments carried out by us</li> </ul>
8.	Procedures adopted in carrying out the valuation and valuation standards followed;	Sales Comparative Method
9.	Restrictions on use of the report, if any;  Think.Innovo	This valuation is for the use of the party to whom it is addressed and for no other purpose. No responsibility is accepted to any third party who may use or rely on the whole or any part of this valuation. The valuer has no pecuniary interest that would conflict with the proper valuation of the property.
10.	Major factors that were taken into account during the valuation;	Current market conditions, demand and supply position, residential land size, location, sustained demand for residential land, all round development of commercial and residential application in the locality etc.
11.	Caveats, limitations and disclaimers to the extent they explain or elucidate the limitations faced by valuer, which shall not be for the purpose of limiting his responsibility for the valuation report.	Attached



Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 37 of 42

#### Assumptions, Disclaimers, Limitations & Qualifications

#### Value Subject to Change

The subject appraisal exercise is based on prevailing market dynamics as on **22**<sup>nd</sup> **February 2024** and does not take into account any unforeseeable developments which could impact the same in the future.

#### **Our Investigations**

We are not engaged to carry out all possible investigations in relation to the subject property. Where in our report we identify certain limitations to our investigations, this is to enable the reliant party to instruct further investigations where considered appropriate or where we recommend as necessary prior to reliance. Vastukala Consultants India Pvt. Ltd. (VCIPL) is not liable for any loss occasioned by a decision not to conduct further investigations

#### **Assumptions**

Assumptions are a necessary part of undertaking valuations. VCIPL adopts assumptions for the purpose of providing valuation advise because some matters are not capable of accurate calculations or fall outside the scope of our expertise, or out instructions. The reliant party accepts that the valuation contains certain specific assumptions and acknowledge and accept the risk of that if any of the assumptions adopted in the valuation are incorrect, then this may have an effect on the valuation.

#### **Information Supplied by Others**

The appraisal is based on the information provided by the client. The same has been assumed to be correct and has been used for appraisal exercise. Where it is stated in the report that another party has supplied information to VCIPL, this information is believed to be reliable but VCIPL can accept no responsibility if this should prove not to be so.

#### **Future Matters**

To the extent that the valuation includes any statement as to a future matter, that statement is provided as an estimate and/or opinion based on the information known to VCIPL at the date of this document. VCIPL does not warrant that such statements are accurate or correct.

#### Map and Plans

Any sketch, plan or map in this report is included to assist the reader while visualising the property and assume no responsibility in connection with such matters.

#### **Site Details**

Based on documents / information received from Client's representative and site visit conducted, we understand that the subject property is currently a Building Under Construction work is in progress contiguous and non-agricultural land parcel admeasuring as per table attached to the report and in the name of **M/s. Nathdwara Developers Pvt. Ltd.** Further, VCIPL has assumed that the subject property is free from any encroachment and is available as on the date of the appraisal.

#### **Property Title**

Based on our discussion with the Client, we understand that the subject property is owned by **M/s. Nathdwara Developers Pvt. Ltd.** For the purpose of this appraisal exercise, we have assumed that the subject property has a clear title and is free from any encumbrances, disputes and claims. VCIPL has made no further enquiries with the relevant local authorities in this regard and does not certify the property as having a clear and marketable title. Further, no legal advice regarding the title and ownership of the subject property has





Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 38 of 42 been obtained for the purpose of this appraisal exercise. It has been assumed that the title deeds are clear and marketable.

#### **Environmental Conditions**

We have assumed that the subject property is not contaminated and is not adversely affected by any existing or proposed environmental law and any processes which are carried out on the property are regulated by environmental legislation and are properly licensed by the appropriate authorities.

#### **Town Planning**

The permissible land use, zoning, achievable FSI, area statement adopted for purpose of this valuation is based on the documents / information provided by the Client's representative and the same has been adopted for this valuation purpose. VCIPL has assumed the same to be correct and permissible. VCIPL has not validated the same from any authority.

#### Area

Based on the document provided by the Client's representative, we understand that the subject property is a Building Under Construction work is in progress, contiguous and non-agricultural land parcel admeasuring as per table attached to the report.

#### **Condition & Repair**

In the absence of any information to the contrary, we have assumed that there are no abnormal ground conditions, nor archaeological remains present which might adversely affect the current or future occupation, development or value of the property. The property is free from rat, infestation, structural or latent defect. No currently known deleterious or hazardous materials or suspect techniques will be used in the construction of or subsequent alteration or additions to the property and comments made in the property details do not purport to express an opinion about, or advise upon, the condition of uninspected parts and should not be taken as making an implied representation or statement about such parts

#### Valuation Methodology

For the purpose of this valuation exercise, the valuation methodology used is Direct Comparison Approach Method and proposed Highest and Best Use model is used for analysing development potential.

The Direct Comparison Approach involves a comparison of the property being valued to similar properties that have actually been sold in arms - length transactions or are offered for sale. This approach demonstrates what buyers have historically been willing to pay (and sellers willing to accept) for similar properties in an open and competitive market and is particularly useful in estimating the value of the land and properties that are typically traded on a unit basis.

In case of inadequate recent transaction activity in the subject micro-market, the appraiser would collate details of older transactions. Subsequently, the appraiser would analyse rental / capital value trends in the subject micro-market in order to calculate the percentage increase / decrease in values since the date of the identified transactions. This percentage would then be adopted to project the current value of the same.

Where reliance has been placed upon external sources of information in applying the valuation methodologies, unless otherwise specifically instructed by Client and/or stated in the valuation, VCIPL has not independently verified that information and VCIPL does not advise nor accept it as reliable. The person or entity to whom the report is addressed acknowledges and accepts the risk that if any of the unverified information in the valuation is incorrect, then this may have an effect on the valuation.

#### Not a Structural Survey

We state that this is a valuation report and not a structural survey





Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 39 of 42 **Other** 

All measurements, areas and ages quoted in our report are approximate

#### Legal

We have not made any allowances with respect to any existing or proposed local legislation relating to taxation on realization of the sale value of the subject property. VCIPL is not required to give testimony or to appear in court by reason of this appraisal report, with reference to the property in question, unless arrangement has been made thereof. Further, no legal advice on any aspects has been obtained for the purpose of this appraisal exercise

#### Property specific assumptions

Based on inputs received from the client and site visit conducted, we understand that the subject property is currently Building Under Construction work is in progress, contiguous and non-agricultural land parcel admeasuring area as per table attached to the report.

#### ASSUMPTIONS, CAVEATS, LIMITATION AND DISCLAIMERS

- 1. We assume no responsibility for matters of legal nature affecting the property appraised or the title thereto, nor do we render our opinion as to the title, which is assumed to be good and marketable.
- 2. The property is valued as though under responsible ownership.
- It is assumed that the property is free of liens and encumbrances.
- 4. It is assumed that there are no hidden or unapparent conditions of the subsoil or structure that would render it more or less valuable. No responsibility is assumed for such conditions or for engineering that might be required to discover such factors.
- 5. There is no direct/ indirect interest in the property valued.
- 6. The rates for valuation of the property are in accordance with the Govt. approved rates and prevailing market rates.

Think.Innovate.Create





(Annexure - II)

#### MODEL CODE OF CONDUCT FOR VALUERS

#### **Integrity and Fairness**

- 1. A valuer shall, in the conduct of his/its business, follow high standards of integrity and fairness in all his/its dealings with his/its clients and other valuers.
- 2. A valuer shall maintain integrity by being honest, straightforward, and forthright in all professional relationships.
- 3. A valuer shall endeavour to ensure that he/it provides true and adequate information and shall not misrepresent any facts or situations.
- 4. A valuer shall refrain from being involved in any action that would bring disrepute to the profession.
- 5. A valuer shall keep public interest foremost while delivering his services.

#### **Professional Competence and Due Care**

- 6. A valuer shall render at all times high standards of service, exercise due diligence, ensure proper care and exercise independent professional judgment.
- 7. A valuer shall carry out professional services in accordance with the relevant technical and professional standards that may be specified from time to time.
- 8. A valuer shall continuously maintain professional knowledge and skill to provide competent professional service based on up-to-date developments in practice, guidelines and techniques.
- 9. In the preparation of a valuation report, the valuer shall not disclaim liability for his/its expertise or deny his/its duty of care, except to the extent that the assumptions are based on statements of fact provided by the company or its auditors or consultants or information available in public domain and not generated by the valuer.
- 10. A valuer shall not carry out any instruction of the client insofar as they are incompatible with the requirements of integrity, objectivity and independence.
- 11. A valuer shall clearly state to his client the services that he would be competent to provide and the services for which he would be relying on other valuers or professionals or for which the client can have a separate arrangement with other valuers.

#### Independence and Disclosure of Interest

- 12. A valuer shall act with objectivity in his/its professional dealings by ensuring that his/its decisions are made without the presence of any bias, conflict of interest, coercion, or undue influence of any party, whether directly connected to the valuation assignment or not.
- 13. A valuer shall not take up an assignment if he/it or any of his/its relatives or associates is not independent in terms of association to the company.
- 14. A valuer shall maintain complete independence in his/its professional relationships and shall conduct the valuation independent of external influences.
- 15. A valuer shall wherever necessary disclose to the clients, possible sources of conflicts of duties and interests, while providing unbiased services.
- 16. A valuer shall not deal in securities of any subject company after any time when he/it first becomes aware of the possibility of his / its association with the valuation, and in accordance with the Securities and Exchange Board of India (Prohibition of Insider Trading)Regulations,2015 or till the time the valuation report becomes public, whichever is earlier.
- 17. A valuer shall not indulge in "mandate snatching" or offering "convenience valuations" in order to cater to a company or client's needs.
- 18. As an independent valuer, the valuer shall not charge success fee.





Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 41 of 42

19. In any fairness opinion or independent expert opinion submitted by a valuer, if there has been a prior engagement in an unconnected transaction, the valuer shall declare the association with the company during the last five years.

#### Confidentiality

20. A valuer shall not use or divulge to other clients or any other party any confidential information about the subject company, which has come to his / its knowledge without proper and specific authority or unless there is a legal or professional right or duty to disclose.

#### **Information Management**

- 21. A valuer shall ensure that he/ it maintains written contemporaneous records for any decision taken, the reasons for taking the decision, and the information and evidence in support of such decision. This shall be maintained so as to sufficiently enable a reasonable person to take a view on the appropriateness of his /its decisions and actions.
- 22. A valuer shall appear, co-operate and be available for inspections and investigations carried out by the authority, any person authorised by the authority, the registered valuers organisation with which he/it is registered or any other statutory regulatory body.
- 23. A valuer shall provide all information and records as may be required by the authority, the Tribunal, Appellate Tribunal, the registered valuers organisation with which he/it is registered, or any other statutory regulatory body.
- 24. A valuer while respecting the confidentiality of information acquired during the course of performing professional services, shall maintain proper working papers for a period of three years or such longer period as required in its contract for a specific valuation, for production before a regulatory authority or for a peer review. In the event of a pending case before the Tribunal or Appellate Tribunal, the record shall be maintained till the disposal of the case.

#### Gifts and hospitality:

- 25. A valuer or his / its relative shall not accept gifts or hospitality which undermines or affects his independence as a valuer.
- 26. Explanation: For the purposes of this code the term 'relative' shall have the same meaning as defined in clause (77) of Section 2 of the Companies Act, 2013 (18 of 2013).
- 27. A valuer shall not offer gifts or hospitality or a financial or any other advantage to a public servant or any other person with a view to obtain or retain work for himself / itself, or to obtain or retain an advantage in the conduct of profession for himself / itself.

#### Remuneration and Costs.

- 28. A valuer shall provide services for remuneration which is charged in a transparent manner, is a reasonable reflection of the work necessarily and properly undertaken, and is not inconsistent with the applicable rules.
- 29. A valuer shall not accept any fees or charges other than those which are disclosed in a written contract with the person to whom he would be rendering service.

#### Occupation, employability and restrictions.

- 30. A valuer shall refrain from accepting too many assignments, if he/it is unlikely to be able to devote adequate time to each of his/ its assignments.
- 31. A valuer shall not conduct business which in the opinion of the authority or the registered valuer organisation discredits the profession.

#### **Miscellaneous**

- 32. A valuer shall refrain from undertaking to review the work of another valuer of the same client except under written orders from the bank or housing finance institutions and with knowledge of the concerned valuer.
- 33. A valuer shall follow this code as amended or revised from time to time.





## Valuation Report Prepared For: SBI / SME Vashi Turbhe Branch / Elite Vivanta (7213/2305241) Page 42 of 42 <u>DEFINITION OF VALUE FOR THIS SPECIFIC PURPOSE</u>

This exercise is to assess Master Valuation of the property under reference as on 22nd February 2024.

The term Fair Market Value is defined as

"The most probable price, as of a specified date, in cash, terms equivalent to cash, or in other precisely revealed terms for which the specified property rights would sell after reasonable exposure in a competitive market under all conditions requisite to a fair sale, with the buyer and seller each acting prudently knowledgeably and for self-interest assuming that neither is under undue duress".

Fundamental assumptions and conditions presumed in this definition are:



- 1. Buyer and seller are motivated by self-interest.
- 2. Buyer and seller are well informed and are acting prudently.
- 3. The property is exposed for a reasonable time on the open market.
- 4. Payment is made in cash or equivalent or in specified financing terms.

#### DECLARATION OF PROFESSIONAL FEES CHARGED

We hereby declare that, our professional fees are not contingent upon the valuation findings. However, if the statute AND/OR clients demands that, the fees should be charged on the percentage of assessed value then, with the full knowledge of the AND/OR end user, it is being charged accordingly.

#### **VALUATION OF THE PROPERTY PREMISES**

Considering various parameters recorded herein above, existing economic scenario, and the information that is available with reference to the development of neighborhood and method selected for valuation, we are of the opinion that, the property premises can be assessed and valued for this particular purpose as per the details provided.

For VASTUKALA CONSULTANTS (I) PVT. LTD.

Think.Innovate.Create

Director

Auth. Sign.

Manoj B. Chalikwar

Registered Valuer Chartered Engineer (India) Reg. No. IBBI / RV / 07/2018/10366

Reg. No. CAT-I-F-1763

SBI Empanelment No.: SME/TCC/2021-22/86/3



