

# Vastukala Consultants (I) Pvt. Ltd.

# PROJECT VALUATION REPORT



Details of the property under consideration:

Name of Developer: M/s. Nandan Buildcon Pvt. Ltd.

Name of Project: Nandan Carnival

"Nandan Carnival", Proposed Residential Building on plot bearing on Plot No. 1A, Survey No. 39/40/41/P/42 to 49/A/B/1, Village - Adgaon, Taluka & District - Nashik, Pin Code - 422 003, State - Maharashtra, Country - India

Latitude Longitude: 20°01'40.5"N 73°51'16.0"E

#### Intended User: Union Bank of India **SAMB Fort Branch**

Bharat House, Ground Floor, 104, M. S. Marg Fort, Mumbai - 400 001 State - Maharashtra, Country - India



♀Aurangabad ♀Pune

Nanded

**♀**Thane **₽**Nashik

PAhmedabad PDelhi NCR

#### Read. Office

BI-001, U/B Floor, BOOMERANG, Chandivali Farm Road, Powai, Andheri East, Mumbai: 400072, (M.S), India

**2** +91 2247495919

🌌 mumbai@vastukala.co.in www.vastukala.co.in



MSME Reg No: UDYAM-MH-18-0083617 An ISO 9001: 2015 Certified Company CIN: U74120MH2010PTC207869

# Vastukala Consultants (I) Pvt. Ltd.

Page 2 of 59

Vastu/UBI/Mumbai/05/2024/8826/2306382 18/15-242-SSPPYU Date: 18.05.2024

#### PROJECT VALUATION REPORT

"Nandan Carnival", Proposed Residential Building on plot bearing on Plot No. 1A, Survey No. 39/40/41/P/42 to 49/A/B/1, Village - Adgaon, Taluka & District - Nashik, Pin Code - 422 003, State - Maharashtra, Country - India

Latitude Longitude: 20°01'40.5"N 73°51'16.0"E

#### NAME OF DEVELOPER: M/s. Nandan Buildcon Pvt. Ltd.

Pursuant to instructions from Union Bank of India, SAMB Fort Branch, we have duly visited, inspected, surveyed & assessed the above said property to determine the fair & reasonable market value of the said property as on 25th April 2024 for to assess Fair Market value of the property for SARFAESI (Securitisation and Reconstruction of Financial Assets and Enforcement of Security Interest Act, 2002) purpose.

#### 1. Location Details:

Proposed Residential Building on plot bearing on Plot No. 1A, Survey No. 39/40/41/P/42 to 49/A/B/1, Village -Adgaon, Taluka & District - Nashik, Pin Code - 422 003. It is about 10.8 Km. travel distance from Nashik Railway station. Surface transport to the property is by buses, taxis & private vehicles. The property is in developing locality. All the amenities like shops, banks, hotels, markets, schools, hospitals, etc. are all available in the surrounding locality. The area is higher middle class & developed.

Developer Details:

Z. Developer Details.	
Name of Developer	M/s. Nandan Buildcon Pvt. Ltd.
Project Registration Number	Nandan Carnival A Building - P51600012372
	Nandan Carnival B Building - P51600012244
	Nandan Carnival C Building - P51600005356
Register office address	M/s. Nandan Buildcon Pvt. Ltd.
•	Amar Business Park, Office No. 406 & 407, Survey No. 105/3,
	Baner Road, Opp. Sadanand Estate, Pune, District - Pune, Pin
	Code - 411 045, State - Maharashtra, Country - India
Contact Numbers	Contact Person:
	Mr. Shashi Bhosale (Sales Manager)
	Mobile No. 9011249977
	Mr. Deepak Sonje (Manager)
	Mobile No. 9822197748
	Mr. Shamkant Kotkar (Owner)
	Mobile No. 9823076277
E - mail ID and Website	

**Boundaries of the Property:** 

Direction	Particulars
On or towards North	Mumbai – Agra Road & D-Mart Adgaon & Open Plot
On or towards South	Open Plot June 1997
On or towards East	Road & Open Plot
On or towards West	Road & Open Plot & Royal Residency
	To the state of th

#### Our Pan India Presence at:

Aurangabad PPune

Nanded Mumbai Thane **Q** Nashik

O Ahmedabad O Delhi NCR

Rajkot ○ Indore Raipur


Jaipur

#### Regd. Office

B1-001, U/B Floor, BOOMERANG, Chandivali Farm Road, Powai, Andheri East, Mumbai: 400072, (M.S), India

\*912247495919

rnumbai@vastukala.co.in



#### Vastukala Consultants (I) Pvt. Ltd.

B1-001, U/B Floor, Boomerang, Chandivali Farm Road, Powai, Andheri (East), Mumbai – 400 072.

To,
The Branch Manager,
Union Bank of India,
SAMB Fort Branch,
Bharat House, Ground Floor,
104, M. S. Marg Fort, Mumbai - 400 001,
State - Maharashtra, Country - India

#### VALUATION REPORT (IN RESPECT OF PROJECT VALUATION REPORT)

	VALUATION REPORT (IN RESPECT OF PROJECT VALUATION REPORT)					
-	General					
1.	Purpose for which the valuation is made		ation is made		Fort Brand property Reconstruc	request from Union Bank of India, SAMB ch to assess Fair Market value of the for SARFAESI (Securitisation and ction of Financial Assets and Enforcement of terest Act, 2002) purpose.
2.	2. a) Date of inspection			25.04.2024	25.04.2024	
		ate on which the v	aluation is made		18.05.2024	
3.	List of doo	cuments produced	for perusal		/	
	Aven dated	ue Supermarts L d 25.06.2020.	imited (The Purc	chaser) th	nrough wide r	an Buildcon Pvt. Ltd (The Owners) And M/s. registered document No. NSN4/4254/2020, 05.2012 b/w M/s. Nandan Buildcon Pvt. Ltd
	(The		ne Borrower) AN	D Bank		he Bank or The Mortgagee) through wide
	(The regis	Mortgagor or The tered document N	ne Borrower) AN o. NSN3/9355/20	D Bank 112.	of Baroda (Th	.09.2012 b/w M/s. Nandan Buildcon Pvt. Ltd he Bank or The Mortgagee) through wide
	Bank	of Baroda (The M	lortgagee Bank) t	hrough w	ide registered	n Buildcon Pvt. Ltd. (The Mortgagor) AND document No. NSN/4/4253/2020.
	Build	con Pvt. Ltd. (The	Releasee) through	gh wide r	egistered docu	Baroda (The Releaser) AND M/s. Nandan ument No. NSN/1/6477/2023.
	No. Z	OSARB / 8 / 2023	3 / 332.		ertificate by B	ank of Baroda dated 21.06.2023 Document
	7. Copy	of 7/12 extract &	Mutation Entries	2012.		
	Sr. No.	Survey No	Date	Mod	dification No.	Occupant Name
	1	40				
	2	41				
	3	42				
	4	43				
	5	44				
	6	45	18.10.2011	1454	/14542/14543	M/s. Nandan Buildcon Pvt. Ltd.
	7	46				
	8	47				
	9	48				
	10	49A				
	11	49B		0000		
		of 7/12 extract 8 M/s. Nandan Bu		s 2022, d	ated 04.08.20	21 latest Modification No. 18580, Occupant
		of Consent ce arashtra Pollution		CBHQ/F	OHQ/Nashik/	CE/CC/509, dated 14.08.2012 issued by
	400 4					11.12







Page 4 of 59

- 10. Copy of NHAI letter Regarding Demarcation & verification of ROW at Gutt No. 39 to 49, dated 18.12.2012 issued by National Highway Authority of India, Document No. NHAI/PIU/NSK/PNG/2012/3392.
- 11. Copy of Fire NOC No. NMC/FIRE/WS/II/87/2012 dated 15.06.2012, issued by Nashik Municipal Corporation.
- 12. Copy of NOC for converting Agricultural Land into Non- Agricultural for Residential / Commercial purpose dated 21.06.2012, issued by National Highway Authority of India, Document No. NHAI/PIU/NSK/NOC/PNG/2012/845.

13. Copy of Previous Owner Sale deed, Release deed, will etc.

Sr. No.	Survey No	Document No	Seller	Purchaser	Date
1	39	NSN/3075/1990	Shri Sitaram Namdev Labhade	Mrs. Pushpavati E. Khernar	24.04.1990
2	39	NSN/2/5519/2007	Shri. Narayan Chikapa Rai.	Shri. Shamrao Keshav Kotkar	14.08.200
3	40	NSK/2800/1981	Mr. Mangilal Shamsukha	Mr. Pravinchand Shaha	06.07.198
4	40	NSN/1/4951/2007	Mr. Pravinchand Shaha	Shri. Shamrao Keshav Kotkar	31.05.200
5	41	NSK/1510/1973		Mr. Purshotam Bhalerao	16.08.197
6	41	NSN/13/336/2005	Shri. Shobana Giridharilal Munot	Mr. Nivrutti Pundalik Mate	19.01.200
7	41	NSN/2/5520/2007	Shri. Shobana Giridharilal Munot	Shri. Shamrao Keshav Kotkar	14.08.200
8	42	NSN/1/4952/2007	Shri. Madhurabai Bandu Mate	Shri. Shamrao Keshav Kotkar	31.05.200
9	43	NSN/4077/1990	Mr. Ganpati Bhika Mate	Mr. Subhashchandra B. Mule	11.06.199
10	43	NSN/3/6016/2003	Mr. Arun Murlidhar Bodhai	Mrs. Suvarna Prakash Bodake	18.12.200
11	43	NSN/4/876/2007	Jhelyabai B. Dhikale, Ganugubai P. Dhikale, Satyabhama K Borade	Shri Runja Ganpat Mate	20.02.200
12	43	NSN/4/1057/2008	Shri. Runja Ganpat Mate	Shri. Shamrao Keshav Kotkar	28.01.200
13	43	NSN/1/4950/2007	Mr. Subhashchandra B. Mule	Shri. Shamrao Keshav Kotkar	31.05.200
14	44		Mrs. Jijabai B. Patil	Mr. Manish H. Kamble	21.06.199
15	44	NSN/2/2287/2008	Mr. Manish H. Kamble	Shri. Shamrao Keshav Kotkar	03.03.200
16	45	NSN/2/4164/1992	Mr. Punja Dashrath Mate	Mrs. Sanjeevani H. Choudhari	17.12.199
17	45		Mrs. Sanjeevani H. Choudhari	Shri. Yogesh B. Shirapure	23.07.199
18	45	NSN/3/1830/2008	M/s. Godawari Urban Co. Op. Bank Ltd. Nashik, Main Branch	Shri. Yogesh B. Shirapure	21.02.200
19	45	NSN/2/6290/2008	Mrs. Sanjeevani H. Choudhari	Shri. Shamrao Keshav Kotkar	08.07.200
20	46		Shrimati. Tulashabai N. Mate	Shri, Yogesh B. Shirapure	14.05.199
21	46	NSN/2/2281/2008	Shrimati. Tulashabai N. Mate & Family	Shri. Shamrao Keshav Kotkar	03.03.200







ONSULTANTE

Valents & Queners

Active des per

Chartered for per

Lander Standard

Additional Particular

Addition

Dogo	_	۰ŧ	50
Page	จ	UΙ	วษ

22	47	NSN/4/876/2007	Jhelyabai B. Dhikale, Ganugubai P. Dhikale, Satyabhama K Borade	Shri Runja Ganpat Mate	20.02.2007
23	47	NSN/4/1058/2008	Shri Runja Ganpat Mate & Family	Shri. Shamrao Keshav Kotkar	28.01.2008
24	48	NSN/4/0853/2008	Shri Ranganath N. Mate & Family	Shri. Shamrao Keshav Kotkar	28.01.2009
25	49		Mrs. Malati Chandrakant Thakur		22.08.2003
26	49	NSN/2/578/1999	Mr. Madhukar Khandu Mate & Family	Shrimati. Malati Chandrakant Thakur	25.01.1999

14. Copy of RERA Certificate No.

P51600012372 - Nandan Carnival A Building dated 09.09.2021

P51600012244 - Nandan Carnival B Building dated 18.05.2020

P51600005356 - Nandan Buildcon C Building dated 09.09.2021

Issued by Maharashtra Real Estate Regulatory Authority

15. Copy of Sale Deed.

15. COp	y of Sale Deed.				
Sr. No	Survey No	Document No	Date	Seller	Purchaser
1	39/41/46	NSN/5/8211/2011	14.10.2011	Mr. Shamakant Keshav Kotkar & Partners	M/s. Nandan Buildcon Pvt. Ltd.
2	40/42/43	NSN/5/8209/2011	14.10.2011	Mr. Shamakant Keshav Kotkar & Partners	M/s. Nandan Buildcon Pvt. Ltd.
3	43/44/45/47/48	NSN/5/8210/2011	14.10.2011	Mr. Shamakant Keshav Kotkar	M/s. Nandan Buildcon Pvt. Ltd.
4	43	NSN/4/4949/2012	16.05.2012	Mrs. Suvarna P. Bodake & Partner	M/s. Nandan Buildcon Pvt. Ltd.
5	49A	NSN/4/5975/2012	11.06.2012	Mr. Madhukar Khandu Mate & Family	M/s. Nandan Buildcon Pvt. Ltd.
6	48B	NSN/4/4251/2012	27.04.2012	Mr. Vishal Chandrakant Thakur	M/s. Nandan Buildcon Pvt. Ltd.

- 16. Copy of Investigation of title dated 18.07.2023 issued by Adv. P.R. Gujarathi.
- 17. Copy of Flow of the Title of the said land dated 18.07.2023 issued by Adv. P.R. Gujarathi.
- 18. Copy of Legal Title Report dated 18.07.2023 issued by Adv. P.R. Gujarathi.
- 19. Copy of Commencement Certificate No. LND/BP/C2/185/2023 dated 18.08.2023 issued by Nashik Municipal Corporation.

#### Permission For Sub-Division + Residential

- 20. Copy of Commencement Certificate No. Town Planning Div. / Sub-Div/105/2020 dated 08.01.2020 issued by Nashik Municipal Corporation.
- 21. Copy of Commencement Certificate No. LND/BP/C2/789/6822 dated 09.03.2017 issued by Nashik Municipal Corporation.

#### Permission For Residential


22. Copy of Commencement Certificate No. LND/BP/Panch/C5/581/3282 dated 24.09.2012 issued by Nashik Municipal Corporation.

#### Permission For Residential + Commercial + Group Housing Scheme.

- 23. Copy of Certificate of Incorporation dated 16.05.2008, issued by Registrar of Companies, Pune, Maharashtra.
- 24. Copy of NA Certificate No. KM/K/3/2/RKA/SR/105/2019 dated 20.03.2020 issued by Resident Collector Nashik.
- 25. Copy of NA Certificate No. MH/K-3/4/VSPK/281/2012 dated 29.08.2012 issued by Collector Nashik.
- 26. Copy of Environment Clearance Certificate No. SEAC/2012/CR-03/TC-III dated 12.07.2016 issued by State level Environment Impact Assessment Authority.
  - 27. Copy of Approved plan dated 18.08.2023, document No. C-2/185/2023, issued by Nashik Municipal



Since 1989





	С	orporation.
Anne	house	Unto:

Approved opto.			
Wings	Wings No. of Floors		
Wing A	Ground Floor + Part Podium & Part 1st Residential floor + 2nd to 13th Upper Floors.		
Wing B	Ground Floor + Part Podium & Part 1st Residential floor + 2nd to 13th Upper Floors.		
Wing C	Ground Floor + Part Podium & Part 1st Residential floor + 2nd to 12th Upper Floors.		
Wing D	Podium + 1st & 2nd Floor (Row House)		

- 28. Copy of Sanction Letter vide No. PCL/2024/LMF/0350 dated 08.05.2024 sanctioned by M/s. Prachay Capital.
- 29. Copy of Indenture of Mortgage Deed through reg. Doc. No. NSN 4/4842/2024 dated 09.05.2024 between M/s. Prachay Capital Private Limited (Lender / Mortgagee) and M/s. Nandan Buildcon Private Limited & M/s. Nandan Associates (Mortgagor).
- 30. Copy of Lapsed Order vide No. MahaRERA/CC/LAO/1518/2024 dated 10.04.2024 issued by Maharashtra Real Estate Regulatory Authority.

Project Name (With address & phone nos.)

"Nandan Carnival", Proposed Residential Building on plot bearing on Plot No. 1A, Survey No. 39/40/41/P/42 to 49/A/B/1, Village – Adgaon, Taluka & District – Nashik, Pin Code – 422 003, State - Maharashtra, Country - India

4. Name of the developer(s) and his / their address (es) with Phone no. (details of share of each owner in case of join t ownership)

#### M/s. Nandan Buildcon Pvt. Ltd.

Amar Business Park, Office No. 406 & 407, Survey No. 105/3, Baner Road, Opp. Sadanand Estate, Pune, District — Pune, Pin Code — 411 045, State - Maharashtra, Country — India

#### Contact Person:

Mr. Shashi Bhosale (Sales Manager)

Mobile No. 9011249977

Mr. Deepak Sonje (Manager)

Mobile No. 9822197748

Mr. Shamkant Kotkar (Owner)

Mobile No. 9823076277

5. Brief description of the property (Including Leasehold / freehold etc.):

#### **About Project:**


MahaRERA Number: P51600012372, P51600012244, P51600005356

Nandan Carnival, an abode of magnificent Apartments with all modern features required for a soulful living. Nestled amidst a posh locality, Adgaon in Nashik, this Residential haven flaunts a resort-like environment that effectively eases off the day's tiredness and makes you discover the difference between a concrete house and a loving home. The builders of the project, Nandan Buildcon Pvt Ltd have ensured that all homes at Nandan Carnival offer privacy and exclusivity to its inhabitants. It is a place that sets a contemporary lifestyle for its residents. The Nandan Carnival offers 288 luxurious, environmentally friendly 2 BHK and 3 BHK beautiful houses. Nandan Carnival in a thoughtfully designed project having world class amenities like 24Hrs Water Supply, 24Hrs Backup Electricity, Amphitheater, Basement Car Parking, CCTV Cameras, Club House, Community Hall, Cricket Court, Fire Safety, Gym, Health Facilities, Jogging Track, Landscaped Garden, Lift, Meditation Hall, Play Area, Rain Water Harvesting, Security Personnel, Senior Citizen Park and Swimming Pool. The project being at an awesome locality enjoys all the perks of a lavish lifestyle. It is legally approved by Nashik Municipal Corporation.

TYPE OF THE BUILDING:

Wings	No. of Floors		
Wing A	Ground Floor + Part Podium & Part 1st Residential floor + 2nd to 13th Upper Floors.		
Wing B	Ground Floor + Part Podium & Part 1st Residential floor + 2nd to 13th Upper Floors.		
Wing C	Ground Floor + Part Podium & Part 1st Residential floor + 2nd to 12th Upper Floors.		









Page 7 of 59

Wing D	Podium + 1st & 2nd Floor (Row House)

LEVEL OF COMPLETEION:

Wings	Present stage of Construction	% of work completion
A	Till 12th floor RCC slab is completed, 1st to 8th floor Block work is completed, 1st to 5th floor Plaster work, Gypsum work, Water proofing, plumbing concealing work is completed, 13th floor 50% slab work is completed.	58.00 %
В	Till 5th floor RCC slab is completed	21.00 %
С	Ground to 12th floor RCC Slab work, block work, plaster work, gypsum work, water proofing work is completed, 1st to 8th floor kitchen platform, flooring, Toilet dadoing, Kitchen tiling, sanitary fitting, door & windows installation work is completed.	81.00 %
D	Work is not started yet	0.00%

#### PROPOSED DATE OF COMPLETION & FUTURE LIFE:

Expected completion date as informed as per RERA for Wing A is 30.12.2021, for Wing B is 30.09.2020. for Wing C is 30.12.2021.

Future estimated life of the Structure is 60 years (after completion) Subject to proper, preventive periodic maintenance & Structural repairs.

As per Approved Plan, Plot area after subdivision of the plot is as below:

Sr. No.	Survey No.	Plot No.	Total Plot Area in Sq. M.	Remark
1	39 to 49	1A	16,062.01	Building permission for the residential building & Owned by Nandan Buildcon Pvt. Ltd.
2	39 to 49	1B	13,653.95	Sold by Nandan Buildcon in the month January 2024
3	39 to 49	2	12,233.00	Sold to D - Mart
4	39 to 49	3	1,840.00	Part portion to Nandan Buildcon Pvt. Ltd.


#### Remark:

- 1. As per site information, construction work is stand still since last 4 to 5 years.
- 2. Project is developed on sub divided Plot No. 1A of Survey No. 39 to 49.
- 3. Property is mortgage to Parchay Capital Pvt. Ltd. as per Mortgage deed dated 09.05.2024.
- 4. Project lapsed order vide no. MahaRERA/CC/LAO/1518/2024 dated 10.04.2024 issued by Maharashtra Real Estate Regulatory Authority.

6.	Loca	ation of property	:			
	a)	Plot No. / Survey No.	:	Plot No. 1A, Survey No. 39/40/41/P/42 to 49/A/B/1		
	b)	Door No.	:	Not applicable		
	c)	C. T.S. No. / Village	:	Village – Adgaon		
	d)	Ward / Taluka	:	Taluka – Nashik		
	e)	Mandal / District	:	District - Nashik		
7.	Post	tal address of the property	:	"Nandan Carnival", Proposed Residential Building on		
				plot bearing on Plot No. 1A, Survey No. 39/40/41/P/42		
				to 49/A/B/1, Village - Adgaon, Taluka & District -		
				Nashik, Pin Code - 422 003, State - Maharashtra,		
				Country - India		
8.	City	/ Town		Village – Adgaon, Nashik		
	Resi	idential area	;	Yes		
	Com	nmercial area	:	No		
	indu	strial area	:	No		



Since 1989





Valuation Report Prepared For: UBI / SAMB Fort Branch / Nandan Carnival (8826/2306382)

Page 8 of 59

Classification of the area

| Middle Class

9.	Classification of the area		;			
	i) High / Middle / Poor		:	Middle Class		
	ii) Urban / Semi Urban / Rural		:	Semi Urban		
10.	Coming under Corporation limit / Villa	ge	:	Village - Adgaon, Nashik		
	Panchayat / Municipality			Nashik Municip	al Corporation.	
11.	Whether covered under any State / Central Govt.			No		
	enactments (e.g., Urban Land Ceiling Act)	or				
	notified under agency area/ scheduled are	1				
	cantonment area					
12.	In Case it is Agricultural land, any conversion to			N.A.		
	house site plots is contemplated					
13.	Boundaries of the property As pe			reement	As per Site Inspection	

13.	Boundaries of the property	Boundaries of the property As per Agreement			
	North	As per attached table below	Mumbai – Agra Road & D-Mart		
			Adgaon & Open Plot		
	South	As per attached table below	Open Plot		
	East	As per attached table below	Road & Open Plot		
	West	As per attached table below	Road & Open Plot & Royal Residency		


Boundaries as per Documents:

Boundaries as per Documents.								
	39	40	41	42	43 (Part)	43 (Part)		
North	12.0 M Wide Service Road	12.0 M Wide Service Road	12.0 M Wide Service Road	Gat No 41	Gat No 42	Gat No 42		
South	Gat No 41	Gat No 41	Gat No 42	Gat No 43	Gat No 44 & 45	Gat No 44 & 45		
East	Gat No. 38	Gat No 39	Gat No 40 & 18.00 M DP road	18.00 M wide DP road	18.00 M wide DP road	18.00 M wide DP road		
West	Gat No 40	Gat No 41	Gat No 459	Gat No 459	Gat No 459	Gat No 459		

	43	44	45	46	47	48	49A	49B
				<b>V</b>				Gat No
North	Gat No	Gat No	Gat No	Gat No	Gat No	Gat No	Gat No	48 & Gat
North	42	43	43	43	45	45	46	No 49
				Y Company				(Part)
South	Gat No	Gat No	Gat No	Gat No	Gat No	Gat No	Gat No	Gat No
South	45	46	47,49	46	48	48	50	50
			E-356				Gat No	
East	Gat No	Gat No	Gat No	Gat No	Gat No	, Gat No	49 (Part)	Gat No
Last	43 (Part)	67	44,46	44	67	67	& Gat No	65 & 66
							48,47	
West	Gat No	Gat No	Survey	Gat No	Gat No	Gat No	Gat No	7.5 M
west	43 (Part)	45	No 459	45	49	49	470	Road

	43 (Pan) 45 No 459	4:	9 49	49	4/0	Road
14.1	4.1 Dimensions of the site		N. A. as the land is	irregular ir	n shape	
			A As per the D	eed	B Ac	tuals
	North	:	-			-
	South	:	-			-
	East	:	-			
	West	:				
14.2	Latitude, Longitude & Co-ordinates of property	;	20°01'40.5"N 73°5	1'16.0"E		
14.	Extent of the site	:	Net Plot area of Plot No. 1A = 16,062.01 Sq. M. (As per Approved Plan) Structure - As per table attached to the report			
15.	Extent of the site considered for Valuation (least of 14A& 14B)	:	Net Plot area of Plot (As per Approved F	ot No. 1A =	The state of the s	









Valuation Report Prepared For: UBI / SAMB Fort Branch / Nandan Carnival (8826/2306382) Page 9 of 59

Structure - As per table attached to the report

			Structure - As per table attached to the report		
16	Whether occupied by the owner / tenant? If occupied by tenant since how long? Rent received	:	Building construction work is in progress.		
	per month.				
il	CHARACTERSTICS OF THE SITE				
1.	Classification of locality	<del>-</del> -	Middle class		
2.	Development of surrounding areas	:	Good		
3.	Possibility of frequent flooding/ sub-merging	:	No		
4.	Feasibility to the Civic amenities like School,	:	All available near by		
7.	Hospital, Bus Stop, Market etc.		All available fleat by		
5.	Level of land with topographical conditions	:	Plain		
6.	Shape of land		Irregular		
7.	Type of use to which it can be put		For residential purpose		
8.	Any usage restriction	:	Residential		
9.	Is plot in town planning approved layout?		Copy of Approved plan dated 18.08.2023, document		
0.	to plot in town planning approved layout.		No. C-2/185/2023, issued by Executive Engineer Town		
			Planning Nashik Municipal Corporation.		
			Approved Upto:		
			Wings No. of Floors		
			Wing A Ground Floor + Part Podium & Part 1st		
			Residential floor + 2 <sup>nd</sup> to 13 <sup>th</sup> Upper		
		1	Floors.		
ı			Wing B Ground Floor + Part Podium & Part 1st		
	The second second		Residential floor + 2 <sup>nd</sup> to 13 <sup>th</sup> Upper		
			Floors.		
			Wing C Ground Floor + Part Podium & Part 1st		
	, the state of the		Residential floor + 2 <sup>nd</sup> to 12 <sup>th</sup> Upper		
			Floors.		
	A A	A	Wing D Podium + 1st & 2nd Floor (Row House)		
10.	Corner plot or intermittent plot?		Intermittent		
11.	Road facilities	;	Yes		
12.	Type of road available at present	:	B.T. Road		
13.	Width of road – is it below 20 ft. or more than 20	:	9.00 Mt. wide Road		
	ft.				
14.	Is it a Land - Locked land?	-	No		
15.	Water potentiality	:	Municipal Water supply		
16.	Underground sewerage system	;	Connected to Municipal sewer		
17.	Is Power supply is available in the site	ļ:	Yes		
18.	Advantages of the site	<u> </u> :	Located in developed area		
19.	Special remarks, if any like threat of acquisition of	:	N.A., the land falls under the residential zone		
	land for publics service purposes, road widening				
	or applicability of CRZ provisions etc. (Distance	1			
	from sea-cost / tidal level must be incorporated)	ļ			
	- A (Valuation of land)		N + P  + (P  + 4) + 40,000,04,0 - 14		
1	Size of plot		Net Plot area of Plot No. 1A = 16,062.01 Sq. M.		
		<del> </del>	(As per Approved Plan)		
	North & South				
	East & West	3.º 3.º	-		
2	Total extent of the plot	-	As per table attached to the report		
3	Prevailing market rate (Along With details /	**	As per table attached to the report		
	reference of at least two latest deals / transactions		Details of second to second to the Parket		
l <sub>l</sub>	with respect to adjacent properties in the areas)		Details of recent transactions/online listings are		
			attached with the report.		





Valuat	ion Report Prepared Fo	or: UBI / SAMB Fort Branch / Nanda	n Ca	arnival (8826/2306382) Page 10 of 59			
4	Guideline rate obtai	ined from the Register's Office	:	Land Rate ₹ 7,300.00 per Sq. M.			
	(evidence thereof to	be enclosed)		Residential Rate ₹ 31,200.00 per Sq. M.			
5	Assessed / adopted	rate of valuation		As per table attached to the report			
6	Estimated value	of land	:	As per table attached to the report			
Part -	Part – B (Valuation of Building)						
1	1 Technical details of the building						
	a) Type of Buildir Industrial)	ng (Residential / Commercial /		Residential			
		ruction (Load bearing / RCC /		R.C.C. Framed structure			
	Steel Framed)	uction (Load bearing / 1100 /		11.0.0.1 Tarried structure			
	c) Year of constru	iction	:	Construction Work in progress.			
		ors and height of each floor ment, if any	:				
	Wings			No. of Floors			
	Wing A	Ground Floor + Part Podium &	Par	rt 1st Residential floor + 2nd to 13th Upper Floors.			
	Wing B	Ground Floor + Part Podium &	Par	rt 1st Residential floor + 2nd to 13th Upper Floors.			
	Wing C	Ground Floor + Part Podium &	Par	rt 1st Residential floor + 2nd to 12th Upper Floors.			
	Wing D	Podium + 1st & 2nd Floor (Row	Ηοι	use)			
	e) Plinth area floo	r-wise	:	As per table attached to the report			
	f) Condition of the	e building	:				
	<ol> <li>Exterior – Excel</li> </ol>	lent, Good, Normal, Poor	:	Partly Good & Partly N.A. Building Construction work			
			is in progress  Partly Good & Partly N.A. Building Construction work is in progress				
	ii. Interior – Excelle	ent, Good, Normal, Poor					
	g) Date of issue approved map	e and validity of layout of	•	Copy of Approved plan dated 18.08.2023, document No. C-2/185/2023, issued by Executive Engineer Town Planning Nashik Municipal Corporation.  Approved Upto:			
		William V		Wings No. of Floors			
			Á	Wing A Ground Floor + Part Podium & Part 1st Residential floor + 2 <sup>nd</sup> to 13 <sup>th</sup> Upper			
				Floors.			
				Wing B Ground Floor + Part Podium & Part 1st Residential floor + 2 <sup>nd</sup> to 13 <sup>th</sup> Upper			
				Floors.			
				Wing C Ground Floor + Part Podium & Part 1st			
				Residential floor + 2 <sup>nd</sup> to 12 <sup>th</sup> Upper			
				Floors.			
				Wing D Podium + 1st & 2nd Floor (Row House)			
		/ plan issuing authority	:	Nashik Municipal Corporation.			
	,	uineness or authenticity of	:	Verified			
		/ plan is verified	ļ				
	,,,	omments by our empanelled	;	N.A.			
	valuers on auth	nentic of approved plan					






Sr. No.	ations of construction (floor-wise) in respect  Description	Ť.			
1.	Foundation		R.C.C. Footing		
2.	Basement	÷	N.A.		
3.	Superstructure	÷	Proposed as per IS Code requirements		
4.	Joinery / Doors & Windows (Please furnish		Partly Wooden Door & Partly Proposed Wooden		
4.	details about size of frames, shutters, glazing,		Door		
	fitting etc. and specify the species of timber		D001		
5.	RCC Works		Yes		
6.	Plastering		Yes		
7.	Flooring, Skirting, dado	<u>;</u>	Partly Vitrified Tiles Flooring, Proposed Vitrified		
۲.	Flooring, Okirting, dado		tiles flooring		
8.	Special finish as marble, granite, wooden	<u> </u>	N.A. Building Construction work is in progress		
0.	paneling, grills etc.		This is building defined defined work to in progress		
9.	Roofing including weather proof course	1	N.A. Building Construction work is in progress		
10.	Drainage	Ė	Proposed		
2.	Compound Wall	1:			
	Height	:	N.A. Building Construction work is in progress		
	Length	:			
	Type of construction	:			
3.	Electrical installation	:	N.A. Building Construction work is in progress		
	Type of wiring	:			
	Class of fittings (superior / ordinary / poor)	:			
-	Number of light points	:/	N.A. Building Construction work is in progress		
	Fan points	A			
	Spare plug points	:			
	Any other item	:			
4.	Plumbing installation		N.A. Building Construction work is in progress		
	a) No. of water closets and their type	7.			
	b) No. of wash basins				
	c) No. of urinals	1			
	d) No. of bath tubs				
	e) Water meters, taps etc.				
	f) Any other fixtures	:			

	Amount in ₹
:	
:	
:	N.A. Building Construction work is in progress
:	N.A. Building Construction work is in progress
:	
:	Amount in ₹
;	
;	
:	
:	N.A. Ruilding Construction work is in progress
	N.A. Building Construction work is in progress





Valua	tion Report Prepared For: UBI / SAMB Fort Brai	nch / Nai	ndan Carnival (8826/2306382) Page <b>12</b> of <b>59</b>
	Total		
Part – E (Miscellaneous) :			Amount in ₹
1.	Separate toilet room	:	
2.	Separate lumber room	:	
3.	Separate water tank / sump	:	N.A. Building Construction work is in progress
4.	Trees, gardening		
	Total		
Part	F (Services)	:	Amount in ₹
1.	Water supply arrangements	:	
2.	Drainage arrangements	:	
3.	Compound wall	:	N.A. Ruilding Construction work is in progress
4.	4. C.B. deposits, fittings etc.		N.A. Building Construction work is in progress
5.	Pavement		

Total abstract of the entire property

Part – A	Land	:	
Part – B	Building	:	
	Land development		
Part – C	Compound wall	:	As per below table attached in the report
Part - D	Amenities		
Part – E	Pavement	:	
Part – F	Services	:	

#### Remark:

Total

- 1. As per site information, construction work is stand still since last 4 to 5 years.
- 2. Project is developed on sub divided Plot No. 1A of Survey No. 39 to 49.
- 3. Property is mortgage to Parchay Capital Pvt. Ltd. as per Mortgage deed dated 09.05.2024.
- 4. Project lapsed order vide no. MahaRERA/CC/LAO/1518/2024 dated 10.04.2024 issued by Maharashtra Real Estate Regulatory Authority.

#### CONFIGURATION OF UNITS TO BE AS PER DEVELOPER'S INFORMATION

The floor wise Area Statement of the Project is as table below:

Sr.	Tower	RERA Carpet	Saleable Area	Total No. of	No. of Sold	No. of Unsold
No.	No.	Area in Sq. Ft.	in Sq. Ft.	Units	Units	Units
1	Α	85,970.83	1,16,060.63	104.00	19.00	85.00
2	В	1,37,270.14	1,85,314.69	104.00	14.00	90.00
3	С	79,755.06	1,07,669.33	96.00	43.00	53.00
4	D	17,801.93	24,032.61	12.00	-	12.00
T	OTAL	3,20,797.97	4,33,077.26	316.00	76.00	240.00





Wing A:
Work Completion Status:

Floor	Work completion as on 25.04.2024	% of work is completed
Ground floor	Slab work is completed	50%
1 <sup>st</sup> floor	Slab work, block work, plaster work, gypsum work, water proofing, plumbing concealing work is completed	70%
2 <sup>nd</sup> floor	Slab work, block work, plaster work, gypsum work, water proofing, plumbing concealing work is completed	70%
3 <sup>rd</sup> floor	Slab work, block work, plaster work, gypsum work, water proofing, plumbing concealing work is completed	70%
4 <sup>th</sup> floor	Slab work, block work, plaster work, gypsum work, water proofing, plumbing concealing work is completed	70%
5 <sup>th</sup> floor	Slab work, block work, plaster work, gypsum work, water proofing, plumbing concealing work is completed	70%
6th floor	Slab work, block work, plaster work, is completed	65%
7 <sup>th</sup> floor	Slab work, block work, plaster work, is completed	65%
8th floor	Slab work, block work, plaster work, is completed	65%
9 <sup>th</sup> floor	Slab work is completed	50%
10th floor	Slab work is completed	50%
11th floor	Slab work is completed	50%
12 <sup>th</sup> floor	Slab work is completed	50%
13th floor	50% Slab work is completed	25%
Terrace / OHT	transmit the first terms of the	0%

#### **Construction Area:**

Oonstruction Arca.	
Floor	Built Up Area in Sq. M.
Ground / Podium Floor	739.41
1st Floor	692.64
2 <sup>nd</sup> Floor	739.41
3 <sup>rd</sup> Floor	752.18
4th Floor	739.41
5 <sup>th</sup> Floor	752.18
6th Floor	739.41
7 <sup>th</sup> Floor	752.18
8 <sup>th</sup> Floor	739.41
9th Floor	752.18
10 <sup>th</sup> Floor	739.41
11th Floor	752.18
12 <sup>th</sup> Floor	739.41
13th Floor	752.18
Terrace/OHT	35.24
TOTAL	10,416.83





Construction Cost of Wing A:

Sr.	Floor	Built Up Area in Sq. M.	Rate per Sq. M.	Cost of Construction in ₹	% of work completed	Construction Cost Incurred as on date in ₹	Cost to be incurred in ₹
	Ground /						
1	Podium Floor	739.41	25,000.00	1,84,85,250.00	50%	92,42,625.00	92,42,625.00
2	1st Floor	692.64	25,000.00	1,73,16,000.00	70%	1,21,21,200.00	51,94,800.00
3	2nd Floor	739.41	25,000.00	1,84,85,250.00	70%	1,29,39,675.00	55,45,575.00
4	3rd Floor	752.18	25,000.00	1,88,04,500.00	70%	1,31,63,150.00	56,41,350.00
5	4th Floor	739.41	25,000.00	1,84,85,250.00	70%	1,29,39,675.00	55,45,575.00
6	5th Floor	752.18	25,000.00	1,88,04,500.00	70%	1,31,63,150.00	56,41,350.00
7	6th Floor	739.41	25,000.00	1,84,85,250.00	65%	1,20,15,412.50	64,69,837.50
8	7th Floor	752.18	25,000.00	1,88,04,500.00	65%	1,22,22,925.00	65,81,575.00
9	8th Floor	739.41	25,000.00	1,84,85,250.00	65%	1,20,15,412.50	64,69,837.50
10	9th Floor	752.18	25,000.00	1,88,04,500.00	50%	94,02,250.00	94,02,250.00
11	10th Floor	739.41	25,000.00	1,84,85,250.00	50%	92,42,625.00	92,42,625.00
12	11th Floor	752.18	25,000.00	1,88,04,500.00	50%	94,02,250.00	94,02,250.00
13	12th Floor	739.41	25,000.00	1,84,85,250.00	50%	92,42,625.00	92,42,625.00
14	13th Floor	752.18	25,000.00	1,88,04,500.00	25%	47,01,125.00	1,41,03,375.00
15	OHT, LMR Area	35.24	25,000.00	8,81,000.00	0%	-	8,81,000.00
	TOTAL	10,416.83		26,04,20,750.00	58%	15,18,14,100.00	10,86,06,650.00

Other Expenditure Cost for Wing A: -

Sr. No.	Particulars		Cost in ₹			
1	Admin Cost	6% of Total cost of Construction	1,87,50,294.00			
2	Professional Fees	5% of Total cost of Construction	1,56,25,245.00			
3	Marketing Cost	3% of Total Income from project	71,29,842.00			
4	Contingency Cost	3% of Total cost of Construction	1,87,50,294.00			
	TOTAL					

Flatwise Inventory Details:

Flatwise inventory Details:						
Sr. No.	Unit No.	Wing	Comp.	RERA Carpet Area (Sq. ft.)	Saleable Area (Sq. Ft.)	Sold / Unsold Inventory
1 & 2	101 & 104	Α	2 BHK	1,660.00	2,241.00	Sold
3	102	Α	2 BHK	1,391.35	1,878.33	Unsold
4	103	Α	2 BHK	1,273.49	1,719.21	Unsold
5	105	Α	2 BHK	1,273.49	1,719.21	Sold
6	106	А	2 BHK	1,273.49	1,719.21	Unsold
7	107	А	2 BHK	1,391.35	1,878.33	Unsold
8	108	А	2 BHK	1,391.35	1,878.33	Unsold
9	201	А	2 BHK	817.31	1,103.37	Sold
10	202	А	2 BHK	817.31	1,103.37	Unsold
11	203	A	2 BHK	754.45	1,018.51	Unsold
12	204	Α	2 BHK	754.45	1,018.51	Unsold
13	205	А	2 BHK	754.45	1,018.51	Unsold
14	206	А	2 BHK	754.45	1,018.51	Unsold
15	207	A	2 BHK	817.31	1,103.37	Unsold
16	208	А	2 BHK	817.31	1,103.37	Unsold
17	301	А	2 BHK	841.21	1,135.63	Sold
18	302	Α	2 BHK	841.21	1,135.63	Unsold
19	303	Α	2 BHK	775.76	1,047.28	Unsold




Since 1989



Valuation	report repair	<u> </u>	SAMD FOIL DIE	inch / Nandan Carnival	i	Page 15 of 59
Sr. No.	Unit No.	Wing	Comp.	RERA Carpet	Saleable Area	Sold / Unsold
		9	·	Area (Sq. ft.)	(Sq. Ft.)	Inventory
20	304	A	2 BHK	740.99	1,000.34	_Sold
21	305	A	2 BHK	775.76	1,047.28	Unsold
22	306	Α	2 BHK	775.76	<u>1,0</u> 47.28	Unsold
23	307	Α	2 BHK	841.21	1,135.63	_Unsold
24	308	Α	2 BHK	804.93	1,086.66	Sold
25	401	Α	2 BHK	817.31	1,103.37	Unsold
26	402	Α	2 BHK	817.31	1,103.37	Unsold
27	403	Α	2 BHK	754.45	1,018.51	Unsold
28	404	А	2 BHK	754.45	1,018.51	Unsold
29	405	А	2 BHK	754.45	1,018.51	Unsold
30	406	A	2 BHK	754.45	1,018.51	Unsold
31	407	A	2 BHK	817.31	1,103.37	Unsold
32	408	A	2 BHK	786.96	1,062.39	Sold
33	501	A	2 BHK	804.93	1,086.66	Sold
34	502	A	2 BHK	841.21	1,135.63	Unsold
35	503	A	2 BHK	775.76	1,047.28	Unsold
36	504	A	2 BHK	775.76	1,047.28	Sold
37	505	A	2 BHK	775.76	1,047.28	Unsold
38	506	A	2 BHK	775.76	1,047.28	
39	507	The state of the s		841.21		Unsold
		A	2 BHK		1,135.63	Unsold
40	508	A	2 BHK	841.21	1,135.63	Unsold
41	601	Α	2 BHK	817.31	1,103.37	Sold
42	602	A	2 BHK	817.31	1,103.37	Unsold
43	603	A	2 BHK	754.45	1,018.51	Unsold
44	604	A	2 BHK	723.99	977.38	Sold
45	605	A	2 BHK	754.45	1,018.51	Sold
46	606	A	2 BHK	754.45	1,018.51	Unsold
47	607	A	2 BHK	817.31	1,103.37	Unsold
48	608	Α	2 BHK	817.31	1,103.37	Unsold
49	701	Α	2 BHK	804.93	1,086.66	Sold
50	702	А	2 BHK	804.93	1,086.66	Sold
51	703	Α	2 BHK	775.76	1,047.28	Unsold
52	704	A	2 BHK	740.99	1,000.34	Sold
53	705	A	2 BHK	775.76	1,047.28	Sold
54	706	Α	2 BHK	775.76	1,047.28	Unsold
55	707	Α	2 BHK	841.21	1,135.63	Unsold
56	708	А	2 BHK	804.93	1,086.66	Sold
57	801	Α	2 BHK	817.31	1,103.37	Unsold
58	802	А	2 BHK	817.31	1,103.37	Unsold
59	803	Α	2 BHK	754.45	1,018.51	Unsold
60	804	Α	2 BHK	754.45	1,018.51	Unsold
61	805	Α	2 BHK	754.45	1,018.51	Unsold
62	806	Α	2 BHK	754.45	1,018.51	Unsold
63	807	Α	2 BHK	817.31	1,103.37	Unsold
64	808	A	2 BHK	817.31	1,103.37	Unsold
65	901	A	2 BHK	841.21	1,135.63	Unsold
66	902	A	2 BHK	841.21	1,135.63	Unsold
67	903	Α	2 BHK	775.76	1,047.28	Unsold
68	904	A	2 BHK	775.76	1,047.28	Unsold
69	905	A	2 BHK	775.76	1,047.28	Unsold
70	906	A	2 BHK	775.76	1,047.28	Unsold
	300 ( )	1 //		, ., .	.,017.20	



Since 1989



Values & Accration
Archier, &
Internal Deshies
Literate (Fig. 1)
Tev Carteries & Reality
Att 2010 PVC1


Valuation Report Prepared For: UBI / SAMB Fort		SAMB FOR Bra		<del>'</del>	Page 16 of 59	
Sr. No.	Unit No.	Wing	Comp.	RERA Carpet	Saleable Area	Sold / Unsold
				Area (Sq. ft.)	(Sq. Ft.)	Inventory
71	907	Α	2 BHK	841.21	1,135.63	Unsold
72	908	Α	2 BHK	841.21	1,135.63	Sold
73	1001	Α	2 BHK	817.31	1,103.37	Unsold
74	1002	Α	2 BHK	817.31	1,103.37	Unsold
75	1003	Α	2 BHK	754.45	1,018.51	Unsold
76	1004	Α	2 BHK	754.45	1,018.51	Unsold
77	1005	Α	2 BHK	754.45	1,018.51	Unsold
78	1006	Α	2 BHK	754.45	1,018.51	Unsold
79	1007	Α	2 BHK	817.31	1,103.37	Unsold
80	1008	Α	2 BHK	817.31	1,103.37	Unsold
81	1101	Α	2 BHK	841.21	1,135.63	Unsold
82	1102	A	2 BHK	841.21	1,135.63	Unsold
83	1103	Α	2 BHK	775.76	1,047.28	Unsold
84	1104	Α	2 BHK	775.76	1,047.28	Unsold
85	1105	Α	2 BHK	775.76	1,047.28	Unsold
86	1106	Α	2 BHK	775.76	1,047.28	Unsold
87	1107	A	2 BHK	841.21	1,135.63	Unsold
88	1108	А	2 BHK	841.21	1,135.63	Unsold
89	1201	A	2 BHK	817.31	1,103.37	Unsold
90	1202	Α	2 BHK	817.31	1,103.37	Unsold
91	1203	Α	2 BHK	754.45	1,018.51	Unsold
92	1204	Α	2 BHK	754.45	1,018.51	Unsold
93	1205	А	2 BHK	754.45	1,018.51	Unsold
94	1206	Α	2 BHK	754.45	1,018.51	Unsold
95	1207	Α	2 BHK	817.31	1,103.37	Unsold
96	1208	A	2 BHK	817.31	1,103.37	Unsold
97	1301	A	2 BHK	841.21	1,135.63	Unsold
98	1302	A	2 BHK	841.21	1,135.63	Unsold
99	1303	Α	2 BHK	775.76	1,047.28	Unsold
100	1304	А	2 BHK	775.76	1,047.28	Unsold
101	1305	Α	2 BHK	775.76	1,047.28	Unsold
102	1306	Α	2 BHK	775.76	1,047.28	Unsold
103	1307	А	2 BHK	890.49	1,202.17	Unsold
104	1308	А	2 BHK	890.49	1,202.17	Unsold
	TO	TAL		85,970.83	1,16,060.63	

**Unsold Flat Inventory:** 

Sr. No.	Unit No.	Wing	Comp.	RERA Carpet Area (Sq. ft.)	Saleable Area (Sq. Ft.)	Rate per Sq. Ft. on Saleable Area	Value in ₹
1	102	Α	2 BHK	1,391.35	1,878.33	3,000.00	56,34,986.00
2	103	Α	2 BHK	1,273.49	1,719.21	3,000.00	51,57,630.00
3	106	Α	2 BHK	1,273.49	1,719.21	3,000.00	51,57,630.00
4	107	Α	2 BHK	1,391.35	1,878.33	3,000.00	56,34,986.00
5	108	Α	2 BHK	1,391.35	1,878.33	3,000.00	56,34,986.00
6	202	Α	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
7	203	Α	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
8	204	Α	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
9	205	Α	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
10	206	Α	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
11	207	Α	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00










		oparoa r a		D FUIL DIANGITI NAII	1		rage II OI 33
Sr. No.	Unit No.	Wing	Comp.	RERA Carpet Area (Sq. ft.)	Saleable Area (Sq. Ft.)	Rate per Sq. Ft. on	Value in ₹
				, , ,		Saleable Area	
12	208	Α	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
13	302	Α	2 BHK	841.21	1,135.63	3,000.00	34,06 <u>,</u> 887.00
14	303	Α	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
15	305	Α	2 BHK	775.76	1,047.28	3,000.00	<u>3</u> 1,41,834.00
16	306	Α	2 BHK	775.76	1,047.28	3,000.00	31,41 <u>,</u> 834.00
17	307	Α	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
_18	401	Α	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
19	402	Α	2 BHK	817.31	1,103.37	3,000.00	33 <u>,</u> 10,108.00
20	403	Α	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
21	404	Α	2 BHK	754.45	1,018.51	3,000.00	30,55,5 <u>1</u> 7.00
22	405	Α	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
23	406	Α	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
24	407	Α	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
25	502	Α	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
26	503	Α	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
27	505	А	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
28	506	Α	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
29	507	Α	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
30	508	Α	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
31	602	Α	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
32	603	Α	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
33	606	Α	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
34	607	А	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
35	608	A	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
36	703	A	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
37	706	A	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
38	707	A	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
39	801	A	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
40	802	A	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
41	803	Α	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
42	804	А	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
43	805	Α	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
44	806	A	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
45	807	A	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
46	808	A	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
47	901	A	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
48	902	A	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
49	903	A	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
50	904	Α	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
51	905	A	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
52	906	A	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
53	907	A	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
54	1001	A	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
55	1002	A	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
56	1003	A	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
57	1004	A	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
58	1005	A	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
59	1006	A	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
60	1007	A	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
61	1008	A	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
91	,000	- / \		011.01	1,100.01	0,000.00	55,10,100.00








valual	luation Report Prepared Por. OBL/ SAMB Port Branch / Nandah Carmval (6626/2306362)						rage 16 of 59
Sr. No.	Unit No.	Wing	Comp.	RERA Carpet Area (Sq. ft.)	Saleable Area (Sq. Ft.)	Rate per Sq. Ft. on Saleable Area	Value in ₹
62	1101	Α	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
63	1102	Α	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
64	1103	Α	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
65	1104	Α	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
66	1105	Α	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
67	1106	Α	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
68	1107	A	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
69	1108	Α	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
70	1201	Α	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
71	1202	Α	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
72	1203	Α_	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
73	1204	Α	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
74	1205	Α	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
75	1206	Α	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
76	1207	Α	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
77	1208	Α	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
78	1301	Α	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
79	1302	Α	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
80	1303	Α	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
81	1304	Α	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
82	1305	Α	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
83	1306	Α	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
84	1307	Α	2 BHK	890.49	1,202.17	3,000.00	36,06,496.00
85	1308	А	2 BHK	890.49	1,202.17	3,000.00	36,06,496.00
	TOTAL		70,396.75	95,035.61	( ) ( ) ( ) ( ) ( ) ( ) ( ) ( ) ( ) ( )	28,51,06,837.00	

Sold Flat Inventory:

Sr. No.	Unit No.	Wing	Comp.	RERA Carpet Area (Sq. ft.)	Saleable Area (Sq. Ft.)	Agreement Value in ₹	Received Amount in ₹	Receivable Amount in ₹
1 & 2	101 & 104	Α	2 BHK	1,660.00	2,241.00	90,00,000.00	61,06,905.00	28,93,095.00
3	105	Α	2 BHK	1,273.49	1,719.21	42,32,229.00	4,85,013.00	37,47,216.00
4	201	Α	2 BHK	817.31	1,103.37	39,25,200.00	17,66,340.00	21,58,860.00
5	301	Α	2 BHK	841.21	1,135.63	38,87,500.00	1,94,006.00	36,93,494.00
6	304	Α	2 BHK	740.99	1,000.34	37,71,088.00	23,45,225.00	14,25,863.00
7	308	Α	2 BHK	804.93	1,086.66	39,66,425.00	23,83,121.00	15,83,304.00
8	408	Α	2 BHK	786.96	1,062.39	36,36,375.00	32,50,825.00	3,85,550.00
9	501	Α	2 BHK	804.93	1,086.66	41,71,425.00	23,87,207.00	17,84,218.00
10	504	Α	2 BHK	775.76	1,047.28	38,65,488.00	15,83,484.00	22,82,004.00
11	601	Α	2 BHK	817.31	1,103.37	41,03,439.00	-	41,03,439.00
12	604	Α	2 BHK	723.99	977.38	30,81,000.00	22,57,338.00	8,23,662.00
13	605	Α	2 BHK	754.45	1,018.51	32,01,279.00	3,32,565.00	28,68,714.00
14	701	Α	2 BHK	804.93	1,086.66	30,68,925.00	20,21,443.00	10,47,482.00
15	702	Α	2 BHK	804.93	1,086.66	39,90,000.00	24,81,366.00	15,08,634.00
16	704	Α	2 BHK	740.99	1,000.34	38,65,488.00	23,89,218.00	14,76,270.00
17	705	Α	2 BHK	775.76	1,047.28	36,98,400.00	48,502.00	36,49,898.00
18	708	Α	2 BHK	804.93	1,086.66	29,42,500.00	20,53,143.00	8,89,357.00
19	908	Α	2 BHK	841.21	1,135.63	29,78,492.00	2,00,000.00	27,78,492.00
	TOT/	AL		15,574.08	21,025.01	7,13,85,253.00	3,22,85,701.00	3,90,99,552.00







## Wing B:

## Work Completion Status:

Floor	Work completion as on 25.04.2024	% of work is completed
Ground floor	Slab work is completed	50%
1 <sup>st</sup> floor	Slab work is completed	50%
2 <sup>nd</sup> floor	Slab work is completed	50%
3 <sup>rd</sup> floor	Slab work is completed	50%
4 <sup>th</sup> floor	Slab work is completed	50%
5 <sup>th</sup> floor	Slab work is completed	50%
6 <sup>th</sup> floor		
7 <sup>th</sup> floor		
8 <sup>th</sup> floor		
9 <sup>th</sup> floor		
10 <sup>th</sup> floor		
11 <sup>th</sup> floor	-	
12th floor		
13 <sup>th</sup> floor		
Terrace / OHT		

#### Construction Area:

Floor	Built Up Area in Sq. M.				
Ground / Podium Floor	1,137.53				
1st Floor	1,032.81				
2nd Floor	1,137.53				
3rd Floor	1,131.64				
4th Floor	1,137.53				
5th Floor	1,131.64				
6th Floor	1,137.53				
7th Floor	1,131.64				
8th Floor	1,137.53				
9th Floor	1,131.64				
10th Floor	1,137.53				
11th Floor	1,131.64				
12 <sup>th</sup> Floor	1,137.53				
13 <sup>th</sup> Floor	1,131.64				
Terrace / OHT	40.76				
TOTAL	15,826.12				





**Construction Cost:** 

Sr.	Floor	Built Up Area in Sq. M.	Rate per Sq. M.	Cost of Construction in ₹	% of work completed	Construction Cost Incurred as on date in ₹	Cost to be incurred in ₹
1	Ground / Podium Floor	1,137.53	30,000.00	3,41,25,900.00	50%	1,70,62,950.00	1,70,62,950.00
2	1st Floor	1,032.81	30,000.00	3,09,84,300.00	50%	1,54,92,150.00	1,54,92,150.00
3	2nd Floor	1,137.53	30,000.00	3,41,25,900.00	50%	1,70,62,950.00	1,70,62,950.00
4	3rd Floor	1,131.64	30,000.00	3,39,49,200.00	50%	1,69,74,600.00	1,69,74,600.00
5	4th Floor	1,137.53	30,000.00	3,41,25,900.00	50%	1,70,62,950.00	1,70,62,950.00
6	5th Floor	1,131.64	30,000.00	3,39,49,200.00	50%	1,69,74,600.00	1,69,74,600.00
7	6th Floor	1,137.53	30,000.00	3,41,25,900.00	0%	-	3,41,25,900.00
8	7th Floor	1,131.64	30,000.00	3,39,49,200.00	0%	-	3,39,49,200.00
9	8th Floor	1,137.53	30,000.00	3,41,25,900.00	0%	-	3,41,25,900.00
10	9th Floor	1,131.64	30,000.00	3,39,49,200.00	0%	-	3,39,49,200.00
11	10th Floor	1,137.53	30,000.00	3,41,25,900.00	0%	-	3,41,25,900.00
12	11th Floor	1,131.64	30,000.00	3,39,49,200.00	0%	-	3,39,49,200.00
13	12th Floor	1,137.53	30,000.00	3,41,25,900.00	0%	-	3,41,25,900.00
14	13th Floor	1,131.64	30,000.00	3,39,49,200.00	0%	-	3,39,49,200.00
15	OHT, LMR Area	40.76	30,000.00	12,22,920.00	0%	-	12,22,920.00
	TOTAL	15,826.12		47,47,83,720.00	21%	10,06,30,200.00	37,41,53,520.00

Other Expenditure Cost for Wing B: -


Sr. No.	Particulars		Cost in ₹				
1	Admin Cost	6% of Total cost of Construction	2,84,87,023.00				
2	Professional Fees	5% of Total cost of Construction	2,37,39,186.00				
3	Marketing Cost	3% of Total Income from project	1,09,93,411.00				
4	Contingency Cost	3% of Total cost of Construction	2,84,87,023.00				
	TOTAL						

Flatwise Inventory Details:

	mironicol y Doc		2010 Table 100 T	CONT. ACCOUNTS OF THE PARTY		
Sr. No.	Unit No.	Wing	Comp.	RERA Carpet Area (Sq. ft.)	Saleable Area (Sq. Ft.)	Sold / Unsold Inventory
1	101	В	3 BHK	2,100.81	2,836.09	Sold
2	102	В	3 BHK	2,100.81	2,836.09	Sold
3	103	В	3 BHK	1,944.84	2,625.53	Sold
4	104	В	3 BHK	1,944.84	2,625.53	Unsold
5	105	В	3 BHK	1,252.14	1,690.39	Sold
6	106	В	3 BHK	1,944.84	2,625.53	Unsold
7	107	В	3 BHK	2,100.81	2,836.09	Unsold
8	108	В	3 BHK	2,100.81	2,836.09	Unsold
9	201	В	3 BHK	1,309.98	1,768.47	Unsold
10	202	В	3 BHK	1,309.98	1,768.47	Unsold
11	203	В	3 BHK	1,221.71	1,649.31	Unsold
12	204	В	3 BHK	1,221.71	1,649.31	Unsold
13	205	В	3 BHK	1,221.71	1,649.31	Unsold
14	206	В	3 BHK	1,221.71	1,649.31	Unsold
15	207	В	3 BHK	1,309.98	1,768.47	Unsold
16	208	В	3 BHK	1,309.98	1,768.47	Sold
17	301	В	3 BHK	1,318.37	1,779.81	Unsold
18	302	В	3 BHK	1,318.37	1,779.81	Unsold
19	303	В	3 BHK	1,230.11	1,660.65	Unsold
20	304	В	3 BHK	1,230.11	1,660.65	Unsold



Since 1989






			T OIL BIGHOUT I	DEDA Com of		Cold I I noold
Sr. No.	Unit No.	Wing	Comp.	RERA Carpet	Saleable Area	Sold / Unsold
04	205	0	2 DUIK	Area (Sq. ft.)	(Sq. Ft.)	Inventory
21	305	В	3 BHK	1,230.11	1,660.65	Sold
22	306	В	3 BHK	1,230.11	1,660.65	Unsold
23	307	В	3 BHK	1,318.37	1,779.81	Unsold
24	308	В	3 BHK	1,318.37	1,779.81	Unsold
25	401	В	3 BHK	1,309.98	1,768.47	Sold
26	402	В	3 BHK	1,309.98	1,768.47	Unsold
27	403	В	3 BHK	1,221.71	1,649.31	Unsold
28	404	В	3 BHK	1,221.71	1,649.31	Sold
29	405	В	3 BHK	1,221.71	1,649.31	Sold
30	406	В	3 BHK	1,221.71	1,649.31	Unsold
31	407	В	3 BHK	1,309.98	1,768.47	Unsold
32	408	В	3 BHK	1,309.98	1,768.47	Sold
33	501	В	3 BHK	1,318.37	1,779.81	Unsold
34	502	В	3 BHK	1,318.37	1,779.81	Unsold
35	503	В	3 BHK	1,230.11	1,660.65	Unsold
36	504	В	3 BHK	1,230.11	1,660.65	Unsold
37	505	В	3 BHK	1,230.11	1,660.65	Unsold
38	506	В	3 BHK	1,230.11	1,660.65	Unsold
39	507	В	3 BHK	1,318.37	1,779.81	Unsold
40	508	В	3 BHK	1,318.37	1,779.81	Sold
41	601	В	3 BHK	1,309.98	1,768.47	Unsold
42	602	В	3 BHK	1,309.98	1,768.47	Unsold
43	603	В	3 BHK	1,221.71	1,649.31	Unsold
44	604	В	3 BHK	1,221.71	1,649.31	Unsold
45	605	В	3 BHK	1,221.71	1,649.31	Unsold
46	606	В	3 BHK	1,221.71	1,649.31	Unsold
47	607	В	3 BHK	1,309.98	1,768.47	Unsold
48	608	В	3 BHK	1,309.98	1,768.47	Unsold
49	701	В	3 BHK	1,266.06	1,709.18	Sold
50	701	В	3 BHK	1,318.37	1,779.81	Unsold
51	703	В	3 BHK	1,230.11	1,660.65	
52	704	В	3 BHK	1,230.11	1,660.65	Unsold
53	704	В	3 BHK		·	Unsold
			3 BHK	1,180.06	1,593.08	Sold
54 55	706 707	В	3 BHK	1,230.11	1,660.65	Unsold
56	707	B	3 BHK	1,318.37	1,779.81 1,779.81	Unsold
57	801	B	3 BHK	1,318.37		Unsold
$\overline{}$				1,309.98	1,768.47	Unsold
58	802	В	3 BHK	1,309.98	1,768.47	Unsold
59	803	В	3 BHK	1,221.71	1,649.31	Unsold
60	804	В	3 BHK	1180.06	1,593.08	Sold
61	805	В	3 BHK	1,221.71	1,649.31	Unsold
62	806	В	3 BHK	1,221.71	1,649.31	Unsold
63	807	В	3 BHK	1,309.98	1,768.47	Unsold
64	808	В	3 BHK	1,309.98	1,768.47	Unsold
65	901	В	3 BHK	1,318.37	1,779.81	Unsold
66	902	В	3 BHK	1,318.37	1,779.81	Unsold
67	903	В	3 BHK	1,230.11	1,660.65	Unsold
68	904	В	3 BHK	1,230.11	1,660.65	Unsold
69	905	В	3 BHK	1,230.11	1,660.65	Unsold
70	906	В	3 BHK	1,230.11	1,660.65	Unsold
71	907	В	3 BHK	1,318.37	1,779.81	Unsold



Since 1989



CONSULTANTE

Actions

Actions

Actions

Chartened territoria

Linders & Copiese

Chartened territoria

Charten


Sr. No.	Unit No.	Wing	Comp.	RERA Carpet	Saleable Area	Sold / Unsold
31. NO.	Ont No.	wilig	Comp.	Area (Sq. ft.)	(Sq. Ft.)	Inventory
72	908	В	3 BHK	1,318.37	1,779.81	Unsold
73	1001	В	3 BHK	1,309.98	1,768.47	Unsold
74	1002	В	3 BHK	1,309.98	1,768.47	Unsold
75	1003	В	3 BHK	1,221.71	1,649.31	Unsold
76	1004	В	3 BHK	1,221.71	1,649.31	Unsold
77	1005	В	3 BHK	1,221.71	1,649.31	Unsold
78	1006	В	3 BHK	1,221.71	1,649.31	Unsold
79	1007	В	3 BHK	1,309.98	1,768.47	Unsold
80	1008	В	3 BHK	1,309.98	1,768.47	Unsold
81	1101	В	3 BHK	1,318.37	1,779.81	Unsold
82	1102	В	3 BHK	1,318.37	1,779.81	Unsold
83	1103	В	3 BHK	1,230.11	1,660.65	Unsold
84	1104	В	3 BHK	1,230.11	1,660.65	Unsold
85	1105	В	3 BHK	1,230.11	1,660.65	Unsold
86	1106	В	3 BHK	1,230.11	1,660.65	Unsold
87	1107	В	3 BHK	1,318.37	1,779.81	Unsold
88	1108	В	3 BHK	1,318.37	1,779.81	Unsold
89	1201	В	3 BHK	1,309.98	1,768.47	Unsold
90	1202	В	3 BHK	1,309.98	1,768.47	Unsold
91	1203	В	3 BHK	1,221.71	1,649.31	Unsold
92	1204	В	3 BHK	1,221.71	1,649.31	Unsold
93	1205	В	3 BHK	1,221.71	1,649.31	Unsold
94	1206	В	3 BHK	1,221.71	1,649.31	Unsold
95	1207	В	3 BHK	1,309.98	1,768.47	Unsold
96	1208	В	3 BHK	1,309.98	1,768.47	Unsold
97	1301	В	3 BHK	1,318.37	1,779.81	Unsold
98	1302	В	3 BHK	1,318.37	1,779.81	Unsold
99	1303	В	3 BHK	1,230.11	1,660.65	Unsold
100	1304	В	3 BHK	1,230.11	1,660.65	Unsold
101	1305	В	3 BHK	1,230.11	1,660.65	Unsold
102	1306	В	3 BHK	1,230,11	1,660.65	Unsold
103	1307	В	3 BHK	1,318.37	1,779.81	Unsold
104	1308	В	3 BHK	1,318.37	1,779.81	Unsold
	TO	TAL		1,37,270.14	1,85,314.69	

**Unsold Flat Inventory:** 

91100	ia i iat ii	rontory	<u>-</u>				<del>-</del> -
Sr. No.	Unit No.	Wing	Comp.	RERA Carpet Area (Sq. ft.)	Saleable Area (Sq. Ft.)	Rate per Sq. Ft. on Saleable Area	Value in ₹
1	104	В	3 BHK	1,944.84	2,625.53	3,000.00	78,76,600.00
2	106	В	3 BHK	1,944.84	2,625.53	3,000.00	78,76,600.00
3	107	В	3 BHK	2,100.81	2,836.09	3,000.00	85,08,280.00
4	108	В	3 BHK	2,100.81	2,836.09	3,000.00	85,08,280.00
5	201	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
6	202	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
7	203	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
8	204	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
9	205	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
10	206	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
11	207	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
12	301	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
13	302	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00










		riepaieu	1 01. 0 DI 7 3 AI	DEDA Como A			Page 23 01 39
Sr.	Unit	Wing	Comp.	RERA Carpet	Saleable Area	Rate per Sq. Ft.	Value in ₹
No.	No.			Area (Sq. ft.)	(Sq. Ft.)	on Saleable Area	40.01.045.00
14	303	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
15	304	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
16	306	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
17	307	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
18	308	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
19	402	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
20	403	В	3 BHK	1 <u>,221.71</u>	1,649.31	3,000.00	49,47,942.00
21	406	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
22	407	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
23	501	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
24	502	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
25	503	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
26	504	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
27	505	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
28	506	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
29	507	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
30	601	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
31	602	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
32	603	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
33	604	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
34	605	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
35	606	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
36	607	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
37	608	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
38	702	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
39	703	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
40	704	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
41	706	B	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
42	707	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
43	708	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
44	801	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
45	802	В	3 BHK			3,000.00	
		В		1,309.98	1,768.47		53,05,414.00
46	803		3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
47	805	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
48	806	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
49	807	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
50	808	B	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
51	901	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
52	902	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
53	903	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
54	904	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
55	905	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
56	906	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
57	907	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
58	908	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
59	1001	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
60	1002	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
61	1003	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
62	1004	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
63	1005	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
64	1006	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
	will be the same	100					







Sr.	Unit	1		RERA Carpet	Saleable Area	Rate per Sq. Ft.	Page 24 or 59
No.	No.	Wing	Comp.	Area (Sq. ft.)	(Sq. Ft.)	on Saleable Area	Value in ₹
65	1007	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
66	1008	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
67	1101	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
68	1102	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
69	1103	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
70	1104	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
71	1105	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
72	1106	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
73	1107	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
74	1108	В	3 BHK	1,318.37	_1,779.81	3,000.00	53,39,418.00
75	1201	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
76	1202	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
77	1203	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
78	1204	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
79	1205	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
80	1206	В	3 BHK	1,221.71	1,649.31	3,000.00	49,47,942.00
81	1207	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
82	1208	В	3 BHK	1,309.98	1,768.47	3,000.00	53,05,414.00
83	1301	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
84	1302	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
85	1303	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
86	1304	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
87	1305	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
88	1306	В	3 BHK	1,230.11	1,660.65	3,000.00	49,81,945.00
89	1307	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
90	1308	В	3 BHK	1,318.37	1,779.81	3,000.00	53,39,418.00
TOTAL		1,17,323.51	1,58,386.74	( u	47,51,60,222.00		

**Sold Flat Inventory:** 

Sr. No.	Unit No.	Wing	Comp.	RERA Carpet Area (Sq. ft.)	Saleable Area (Sq. Ft.)	Agreement Value in ₹	Received Amount in ₹	Receivable Amount in ₹
1	101	В	3 BHK	2,100.81	2,836.09	55,75,200.00	-	55,75,200.00
2	102	В	3 BHK	2,100.81	2,836.09	55,75,200.00	-	55,75,200.00
3	103	В	3 BHK	1,944.84	2,625.53	52,08,400.00		52,08,400.00
4	105	В	3 BHK	1,252.14	1,690.39	64,35,500.00	8,93,195.00	55,42,305.00
5	208	В	3 BHK	1,309.98	1,768.47	63,80,970.00	10,95,243.00	52,85,727.00
6	305	В	3 BHK	1,230.11	1,660.65	28,19,322.00	2,00,000.00	26,19,322.00
7	401	В	3 BHK	1,309.98	1,768.47	45,77,981.00	-	45,77,981.00
8	404	В	3 BHK	1,221.71	1,649.31	44,69,277.00	-	44,69,277.00
9	405	В	3 BHK	1,221.71	1,649.31	56,69,077.00	97,003.00	55,72,074.00
10	408	В	3 BHK	1,309.98	1,768.47	62,57,000.00	97,003.00	61,59,997.00
11	508	В	3 BHK	1,318.37	1,779.81	63,80,970.00	-	63,80,970.00
12	701	В	3 BHK	1,266.06	1,709.18	63,80,970.00	22,33,340.00	41,47,630.00
<sub>L</sub> 13	705	В	3 BHK	1,180.06	1,593.08	37,52,300.00	10,41,583.00	27,10,717.00
14	804	В	3 BHK	1,180.06	1,593.08	50,28,150.00	22,06,456.00	28,21,694.00
	TOTAL		19,946.63	26,927.95	7,45,10,317.00	78,63,823.00	6,66,46,494.00	





Wing C: Work Completion Status:

Floor	Work completion as on 25.04.2024	% of work is completed
Ground floor	Slab work, block work, plaster work, gypsum work, water proofing, door & windows installed, internal painting, electrical work is completed	90%
1 <sup>st</sup> floor	Slab work, block work, plaster work, gypsum work, water proofing, kitchen platform, flooring, Kitchen tiling, toilet dadoing, sanitary fitting, door & windows installed, internal painting, electrical work is completed	90%
2 <sup>nd</sup> floor	Slab work, block work, plaster work, gypsum work, water proofing, kitchen platform, flooring, Kitchen tiling, toilet dadoing, sanitary fitting, door & windows installed, internal painting, electrical work is completed	90%
3 <sup>rd</sup> floor	Slab work, block work, plaster work, gypsum work, water proofing, kitchen platform, flooring, Kitchen tiling, toilet dadoing, sanitary fitting plumbing concealing work is completed	85%
4 <sup>th</sup> floor	Slab work, block work, plaster work, gypsum work, water proofing, kitchen platform, flooring, Kitchen tiling, toilet dadoing, sanitary fitting	85%
5 <sup>th</sup> floor	Slab work, block work, plaster work, gypsum work, water proofing, kitchen platform, flooring, Kitchen tiling, toilet dadoing, sanitary fitting	85%
6th floor	Slab work, block work, plaster work, gypsum work, water proofing, kitchen platform, flooring, Kitchen tiling, toilet dadoing, sanitary fitting	85%
7 <sup>th</sup> floor	Slab work, block work, plaster work, gypsum work, water proofing, kitchen platform, flooring, Kitchen tiling, toilet dadoing, sanitary fitting	85%
8 <sup>th</sup> floor	Slab work, block work, plaster work, gypsum work, water proofing, kitchen platform, flooring, Kitchen tiling, toilet dadoing, sanitary fitting	85%
9th floor	Slab work, block work, plaster work, gypsum work, water proofing work is completed	70%
10th floor	Slab work, block work, plaster work, gypsum work, water proofing work is completed	70%
11 <sup>th</sup> floor	Slab work, block work, plaster work, gypsum work, water proofing work is completed	70%
12 <sup>th</sup> floor	Slab work, block work, plaster work, gypsum work, water proofing work is completed	70%
Terrace / OHT	Slab work, block work, plaster work, gypsum work, water proofing work is completed	70%



**Construction Area:** 

Floor	Built Up Area in Sq. M.			
Ground / Podium Floor	739.41			
1st Floor	692.64			
2nd Floor	739.41			
3rd Floor	752.18			
4th Floor	739.41			
5th Floor	752.18			
6th Floor	739.41			
7th Floor	752.18			
8th Floor	739.41			
9th Floor	752.18			
10 <sup>th</sup> Floor	739.41			
11 <sup>th</sup> Floor	752.18			
12 <sup>th</sup> Floor	739.41			
Terrace / OHT	40.92			
TOTAL	9,670.33			

**Construction Cost:** 

001	istruction cost:	<b>-</b> =					
Sr.	Floor	Built Up Area in Sq. M.	Rate per Sq. M.	Cost of Construction in ₹	% of work completed	Construction Cost Incurred as on date in ₹	Cost to be incurred in ₹
1	Ground / Podium Floor	739.41	30,000.00	2,21,82,300.00	90%	1,99,64,070.00	22,18,230.00
2	1st Floor	692.64	30,000.00	2,07,79,200.00	90%	1,87,01,280.00	20,77,920.00
3	2nd Floor	739.41	30,000.00	2,21,82,300.00	90%	1,99,64,070.00	22,18,230.00
4	3rd Floor	752.18	30,000.00	2,25,65,400.00	85%	1,91,80,590.00	33,84,810.00
5	4th Floor	739.41	30,000.00	2,21,82,300.00	85%	1,88,54,955.00	33,27,345.00
6	5th Floor	752.18	30,000.00	2,25,65,400.00	85%	1,91,80,590.00	33,84,810.00
7	6th Floor	739.41	30,000.00	2,21,82,300.00	85%	1,88,54,955.00	33,27,345.00
8	7th Floor	752.18	30,000.00	2,25,65,400.00	85%	1,91,80,590.00	33,84,810.00
9	8th Floor	739.41	30,000.00	2,21,82,300.00	85%	1,88,54,955.00	33,27,345.00
10	9th Floor	752.18	30,000.00	2,25,65,400.00	70%	1,57,95,780.00	67,69,620.00
11	10th Floor	739.41	30,000.00	2,21,82,300.00	70%	1,55,27,610.00	66,54,690.00
12	11th Floor	752.18	30,000.00	2,25,65,400.00	70%	1,57,95,780.00	67,69,620.00
13	12th Floor	739.41	30,000.00	2,21,82,300.00	70%	1,55,27,610.00	66,54,690.00
14	OHT / LMR Area	40.92	30,000.00	12,27,510.00	70%	8,59,257.00	3,68,253.00
	TOTAL	9,670.33		29,01,09,810.00	81%	23,62,42,092.00	5,38,67,718.00

Other Expenditure Cost for Wing C: -

Sr. No.	Particulars		Cost in ₹			
1	Admin Cost	6% of Total cost of Construction	1,74,06,589.00			
2	Professional Fees	5% of Total cost of Construction	1,45,05,491.00			
3	Marketing Cost	3% of Total Income from project	64,08,634.00			
4	Contingency Cost	3% of Total cost of Construction	1,74,06,589.00			
	TOTAL 5,57,27,303.00					





Sr.	se Inventory Flat No.	Wing	Comp.	RERA Carpet	Saleable Area	Sold / Unsold
No.			· ·	Area (Sq. ft.)	(Sq. Ft.)	Inventory
1	101	С	2 BHK	1,391.35	1,878.33	Unsold
2	102	С	2 BHK	1,391.35	1,878.33	Unsold
3	103	С	2 BHK	1,273.49	1,719.21	Unsold
4	104	C	2 BHK	795.00	1,073.25	Sold
5	105	С	2 BHK	1,273.49	1,719.21	Sold
6	106	С	2 BHK	1391.35	1,878.33	Sold
7	107	С	2 BHK	1209.21	1,632.44	Sold
8	108	С	2 BHK	1,391.35	1,878.33	Unsold
9	201	С	2 BHK	817.31	1,103.37	Unsold
10	202	С	2 BHK	817.31	1,103.37	Unsold
11	203	С	2 BHK	754.45	1,018.51	Unsold
12	204	С	2 BHK	723.99	977.38	Sold
13	205	C	2 BHK	754.45	1,018.51	Sold
14	206	C	2 BHK	754.45	1,018.51	Sold
15	207	C	2 BHK	817.31	1,103.37	Unsold
16	208	C	2 BHK	817.31	1,103.37	Sold
17	301	C	2 BHK	845.73	1,141.73	Sold
18	302	C	2 BHK	841.21	1,135.63	Unsold
19	303	С	2 BHK	775.76	1,047.28	Unsold
20	304	C	2 BHK	775.76	1,047.28	Unsold
21	305	C	2 BHK	775.76	1,047.28	Sold
22	306	C	2 BHK	775.76	1,047.28	Unsold
23	307	C	2 BHK	841.21	1,135.63	Sold
24	308	C	2 BHK	804.93	1,086.66	Sold
25	401	C	2 BHK	817.31	1,103.37	Sold
26	402	C	2 BHK	817.31	1,103.37	Unsold
27	403	C	2 BHK	754.45	1,018.51	Unsold
28	404	C	2 BHK	723.99	977.38	Sold
29	405	C	2 BHK	723.99	977.38	Sold
30	406	C	2 BHK	761.34	1,027.81	Sold
31	407	C	2 BHK	826.89	1,116.30	Sold
32	408	C	2 BHK	786.96	1,062.39	Sold
33	501	C	2 BHK	841.21	1,135.63	Unsold
34	502	C	2 BHK	841.21	1,135.63	Unsold
35	503	C	2 BHK	775.76	1,047.28	Unsold
36	504	C	2 BHK	775.76	1,047.28	Sold
37	505	C	2 BHK	775.76	1,047.28	Sold
38	506	C	2 BHK	775.76	1,047.28	Unsold
39	507	C	2 BHK	841.21	1,135.63	Unsold
40	508	C	2 BHK	841.21	1,135.63	Sold
41	601	G	2 BHK	826.89	1,116.30	Sold
42	602	C	2 BHK	817.31	1,103.37	Unsold
		C	2 BHK			Unsold
43	603			754.45	1,018.51	
44	604	С	2 BHK	723.99	977.38	Sold
45	605	C	2 BHK	723.99	977.38	Sold
46	606	C	2 BHK	723.99 817.31		Sold
47	607		2 BHK		1,103.37	Unsold
48	608	C	2 BHK	786.96	1,062.39	Sold
49	701	С	2 BHK	804.93	1,086.66	Sold
50	702	C	2 BHK	841.21	1,135.63	Unsold



Since 1989





	uation Report Prepared For: UBI / SAMB Fort Branch / Nandan Carnival (8826/2306382)					
Sr. No.	Flat No.	Wing	Comp.	RERA Carpet Area (Sq. ft.)	Saleable Area (Sq. Ft.)	Sold / Unsold Inventory
51	703	С	2 BHK	775.76	1,047.28	Unsold
52	704	C	2 BHK	740.99	1,000.34	Sold
53	705	С	2 BHK	775.76	1,047.28	Sold
54	706	С	2 BHK	775.76	1,047.28	Unsold
55	707	С	2 BHK	804.93	1,086.66	Sold
56	708	С	2 BHK	804.93	1,086.66	Sold
57	801	С	2 BHK	786.96	1,062.39	Sold
58	802	С	2 BHK	817.31	1,103.37	Unsold
59	803	С	2 BHK	754.45	1,018.51	Unsold
60	804	С	2 BHK	754.45	1,018.51	Unsold
61	805	C	2 BHK	754.45	1,018.51	Sold
62	806	С	2 BHK	754.45	1,018.51	Unsold
63	807	C	2 BHK	817.31	1,103.37	Sold
64	808	C	2 BHK	817.31	1,103.37	Sold
65	901	C	2 BHK	841.21	1,135.63	Sold
66	902	C	2 BHK	841.21	1,135.63	Unsold
67	903	C	2 BHK	775.76	1,047.28	Unsold
68	904	C	2 BHK	775.76	1,047.28	Unsold
69	905	C	2 BHK	775.76	1,047.28	Unsold
70	906	C	2 BHK	775.76	1,047.28	Unsold
71	907	C	2 BHK	841.21	1,135.63	Unsold
72	908	C	2 BHK	841.21	1,135.63	Unsold
73	1001	C	2 BHK	817.31	1,103.37	Unsold
74	1001	C	2 BHK	817.31	1,103.37	Unsold
7 <u>4</u> 75	1002	C	2 BHK	754.45	1,018.51	Unsold
76	1003	C		754.45		
		C	2 BHK	754.45	1,018.51	Unsold Sold
77	1005	C	2 BHK		1,018.51	
78	1006		2 BHK	754.45	1,018.51	Unsold
79	1007	С	2 BHK	817.31	1,103.37	Sold
80	1008	С	2 BHK	817.31	1,103.37	Sold
81	1101	С	2 BHK	841.21	1,135.63	Sold
82	1102	С	2 BHK	841.21	1,135.63	Unsold
83	1103	O	2 BHK	775.76	1,047.28	Unsold
84	1104	C	2 BHK	775.76	1,047.28	Unsold
85	1105	C	2 BHK	775.76	1,047.28	Unsold
86	1106	С	2 BHK	775.76	1,047.28	Unsold
87	1107	С	2 BHK	841.21	1,135.63	Unsold
88	1108	С	2 BHK	841.21	1,135.63	Sold
89	1201	C	2 BHK	817.31	1,103.37	Unsold
90	1202	С	2 BHK	817.31	1,103.37	Unsold
91	1203	C	2 BHK	754.45	1,018.51	Unsold
92	1204	С	2 BHK	754.45	1,018.51	Unsold
93	1205	С	2 BHK	754.45	1,018.51	Sold
94	1206	С	2 BHK	754.45	1,018.51	Unsold
95	1207	С	2 BHK	817.31	1,103.37	Unsold
96	1208	С	2 BHK	817.31	1,103.37	Sold
	<u>T</u>	OTAL		79,755.06	1,07,669.33	






Sr.	ld Flat In Unit			RERA Carpet	Saleable Area	Rate per Sq. Ft.	Value in ₹
No.	No.	Wing	Comp.	Area (Sq. ft.)	(Sq. Ft.)	on Saleable Area	Value in ₹
1	101	С	2 BHK	1,391.35	1,878.33	3,000.00	56,34,986.00
2	102	С	2 BHK	1,391.35	1,878.33	3,000.00	56,34,986.00
3	103	C	2 BHK	1,273.49	1,719.21	3,000.00	51,57,630.00
4	108	C	2 BHK	1,391.35	1,878.33	3,000.00	56,34,986.00
5	201	Č	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
6	202	Ċ	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
7	203	C	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
8	207	C	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
9	302	C	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
10	303	C	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
11	304	C	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
12	306	C	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
13	402	C	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
14		C			<del>-</del>	3,000.00	30,55,517.00
	403	C	2 BHK 2 BHK	754.45	1,018.51	3,000.00	
15	501			841.21	1,135.63	· · · · · · · · · · · · · · · · · · ·	34,06,887.00
16	502	С	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
17	503	С	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
18	506	С	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
19	507	С	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
20	602	С	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
21	603	С	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
22	607	С	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
23	702	С	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
24	703	С	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
25	706	С	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
26	802	С	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
27	803	С	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
28	804	С	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
29	806	С	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
30	902	С	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
31	903	С	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
32	904	С	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
33	905	С	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
34	906	C	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
35	907	С	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
36	908	С	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
37	1001	С	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
38	1002	С	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
39	1003	С	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
40	1004	С	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
41	1006	С	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
42	1102	С	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
43	1103	С	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
44	1104	С	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
45	1105	С	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
46	1106	С	2 BHK	775.76	1,047.28	3,000.00	31,41,834.00
47	1107	С	2 BHK	841.21	1,135.63	3,000.00	34,06,887.00
48	1201	С	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
49	1202	C	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
50	1203	C	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00



Since 1989





Page 30 of 59


Sr. No.	Unit No.	Wing	Comp.	RERA Carpet Area (Sq. ft.)	Saleable Area (Sq. Ft.)	Rate per Sq. Ft. on Saleable Area	Value in ₹
51	1204	С	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
52	1206	С	2 BHK	754.45	1,018.51	3,000.00	30,55,517.00
53	1207	С	2 BHK	817.31	1,103.37	3,000.00	33,10,108.00
	TOTAL			44,357.15	59,882.16		17,96,46,468.00

Sold Flat Inventory:

3010	Flat ir	- Trenton	<del>"·</del>	RERA	Saleable			
Sr.	Unit	Wing	Comp.	Carpet Area	Area (Sq.	Agreement	Received	Receivable
No.	No.	wing	Comp.	(Sq. ft.)	Ft.)	Value in ₹	Amount in ₹	Amount in ₹
1	104	С	2 BHK	795.00	1,073.25	41,95,500.00	22,78,336.00	19,17,164.00
2	105	Č	2 BHK	1,273.49	1,719.21	33,62,493.00	22,70,000.00	33,62,493.00
3	106	C	2 BHK	1,391.35	1,878.33	27,50,000.00	4,03,634.00	23,46,366.00
4	107	C	2 BHK	1,209.21	1,632.44	39,31,789.00	25,62,202.00	13,69,587.00
5	204	C	2 BHK	723.99	977.38	36,37,200.00	18,05,438.00	18,31,762.00
6	205	C	2 BHK	754.45	1,018.51	28,27,500.00	-	28,27,500.00
7	206	C	2 BHK	754.45	1,018.51	30,29,700.00	_	30,29,700.00
8	208	C	2 BHK	817.31	1,103.37	30,42,500.00	5,00,000.00	25,42,500.00
9	301	C	2 BHK	845.73	1,141.73	26,00,000.00	6,69,240.00	19,30,760.00
10	305	С	2 BHK	775.76	1,047.28	28,19,322.00	_	28,19,322.00
11	307	С	2 BHK	841.21	1,135.63	28,66,888.00	_	28,66,888.00
12	308	С	2 BHK	804.93	1,086.66	40,68,925.00	40,68,925.00	-
13	401	С	2 BHK	817.31	1,103.37	29,33,283.00	3,50,000.00	25,83,283.00
14	404	С	2 BHK	723.99	977.38	36,83,550.00	34,99,372.00	1,84,178.00
15	405	С	2 BHK	723.99	977.38	36,15,879.00	20,73,498.00	15,42,381.00
16	406	С	2 BHK	761.34	1,027.81	26,00,000.00	25,21,000.00	79,000.00
17	407	С	2 BHK	826.89	1,116.30	28,00,000.00	27,13,000.00	87,000.00
18	408	С	2 BHK	786.96	1,062.39	33,21,000.00	28,22,706.00	4,98,294.00
19	504	С	2 BHK	775.76	1,047.28	34,65,488.00	-	34,65,488.00
20	505	С	2 BHK	775.76	1,047.28	28,67,500.00	-	28,67,500.00
21	508	С	2 BHK	841.21	1,135.63	41,71,425.00	-	41,71,425.00
22	601	С	2 BHK	826.89	1,116.30	29,42,000.00	12,63,817.00	16,78,183.00
23	604	С	2 BHK	723.99	977.38	36,38,127.00	28,95,383.00	7,42,744.00
24	605	С	2 BHK	723.99	977.38	38,01,279.00	35,20,875.00	2,80,404.00
25	606	С	2 BHK	723.99	977.38	35,44,500.00	33,67,275.00	1,77,225.00
26	608	С	2 BHK	786.96	1,062.39	31,03,439.00	26,37,924.00	4,65,515.00
27	701	С	2 BHK	804.93	1,086.66	40,68,925.00	32,79,626.00	7,89,299.00
28	704	С	2 BHK	740.99	1,000.34	36,04,000.00	30,63,400.00	5,40,600.00
29	705	С	2 BHK	775.76	1,047.28	28,67,500.00	-	28,67,500.00
30	707	С	2 BHK	804.93	1,086.66	41,43,750.00	31,08,186.00	10,35,564.00
31	708	С	2 BHK	804.93	1,086.66	41,71,425.00	32,56,404.00	9,15,021.00
32	801	С	2 BHK	786.96	1,062.39	30,21,000.00	28,99,959.00	1,21,041.00
33	805	С	2 BHK	754.45	1,018.51	28,27,500.00	5,00,000.00	23,27,500.00
34	807	С	2 BHK	817.31	1,103.37	30,42,500.00	-	30,42,500.00
35	808	С	2 BHK	817.31	1,103.37	30,42,500.00	5,00,000.00	25,42,500.00
36	901	С	2 BHK	841.21	1,135.63	32,01,600.00	-	32,01,600.00
37	1005	С	2 BHK	754.45	1,018.51	28,27,500.00	-	28,27,500.00
38	1007	С	2 BHK	817.31	1,103.37	30,42,500.00	-	30,42,500.00
39	1008	С	2 BHK	817.31	1,103.37	34,21,700.00		34,21,700.00
40	1101	С	2 BHK	841.21	1,135.63	29,78,492.00	1,00,000.00	28,78,492.00
41	1108	С	2 BHK	841.21	1,135.63	32,01,600.00	-	32,01,600.00
42	1205	С	2 BHK	754.45	1,018.51	27,47,631.00	-	27,47,631.00









Page **31** of **59** 

Sr. No.	Unit No.	Wing	Comp.	RERA Carpet Area (Sq. ft.)	Saleable Area (Sq. Ft.)	Agreement Value in ₹	Received Amount in ₹	Receivable Amount in ₹
43	1208	С	2 BHK	817.31	1,103.37	29,55,837.00	-	29,55,837.00
	T	OTAL		35,397.91	47,787.18	14,07,85,247.00	5,66,60,200.00	8,41,25,047.00

## Wing D:

**Work Completion Status:** 

Floor	Work completion as on 25.04.2024	% of work is completed
Ground / Podium Floor		-
1st Floor	Mark is not started yet	00/
2 <sup>nd</sup> Floor	Work is not started yet	0%
Terrace / OHT		

**Construction Area:** 

Floor	Built Up Area in Sq. M.
Ground / Podium Floor	191.07
1st Floor	812.10
2 <sup>nd</sup> Floor	724.63
TOTAL	1,727.80

**Construction Cost:** 

Sr.	Floor	Built Up Area in Sq. M.	Rate per Sq. M.	Cost of Construction in ₹	% of work completed	Construction Cost Incurred as on date in ₹	Cost to be incurred in ₹
1	Ground Floor	191.07	30,000.00	57,32,100.00	0%	•	57,32,100.00
2	1st Floor	812.10	30,000.00	2,43,63,000.00	0%	-	2,43,63,000.00
3	2nd Floor	724.63	30,000.00	2,17,38,900.00	0%	-	2,17,38,900.00
Total		1,727.80		5,18,34,000.00	0%	-	5,18,34,000.00

Other Expenditure Cost for Wing D: -

Sr. No.	Particulars		Cost in ₹
1	Admin Cost	6% of Total cost of Construction	31,10,040.00
2	Professional Fees	5% of Total cost of Construction	25,91,700.00
3	Marketing Cost	2% of Total Income from project	16,82,283.00
4	Contingency Cost	3% of Total cost of Construction	31,10,040.00
	1,04,94,063.00		

Flatwise Inventory Details:

Sr. No.	Unit No.	Wing	Comp.	RERA Carpet Area (Sq. ft.)	Saleable Area (Sq. Ft.)	Sold / Unsold Inventory
1	R-1	D	Row House	1,483.49	2,002.72	Unsold
2	R-2	D	Row House	1,483.49	2,002.72	Unsold
3	R-3	D	Row House	1,483.49	2,002.72	Unsold
4	R-4	D	Row House	1,483.49	2,002.72	Unsold
5	R-5	D	Row House	1,483.49	2,002.72	Unsold
6	R-6	D	Row House	1,483.49	2,002.72	Unsold
7	R-7	D	Row House	1,483.49	2,002.72	Unsold
8	R-8	D	Row House	1,483.49	2,002.72	Unsold
9	R-9	D	Row House	1,483.49	2,002.72	Unsold
10	R-10	D	Row House	1,483.49	2,002.72	Unsold
11	R-11	D	Row House	1,483.49	2,002.72	Unsold
12	R-12	D	Row House	1,483.49	2,002.72	Unsold



Since 1989





Page 32 of 59

Sr. No.	Unit No.	Wing	Comp.	RERA Carpet Area (Sq. ft.)	Saleable Area (Sq. Ft.)	Sold / Unsold Inventory
TOTAL				17,801.93	24,032.61	

**Unsold Inventory:** 

Sr. No.	Unit No.	Wing	Comp.	RERA Carpet Area (Sq. ft.)	Saleable Area (Sq. Ft.)	Rate per Sq. Ft. on Saleable Area	Value in ₹
1	R-1	D	Row House	1,483.49	2,002.72	3,500.00	70,09,511.00
2	R-2	D	Row House	1,483.49	2,002.72	3,500.00	70,09,511.00
3	R-3	D	Row House	1,483.49	2,002.72	3,500.00	70,09,511.00
4	R-4	D	Row House	1,483.49	2,002.72	3,500.00	70,09,511.00
5	R-5	D	Row House	1,483.49	2,002.72	3,500.00	70,09,511.00
6	R-6	D	Row House	1,483.49	2,002.72	3,500.00	70,09,511.00
7	R-7	D	Row House	1,483.49	2,002.72	3,500.00	70,09,511.00
8	R-8	О	Row House	1,483.49	2,002.72	3,500.00	70,09,511.00
9_	R-9	D	Row House	1,483.49	2,002.72	3,500.00	70,09,511.00
10	R-10	D	Row House	1,483.49	2,002.72	3,500.00	70,09,511.00
11	R-11	D	Row House	1,483.49	2,002.72	3,500.00	70,09,511.00
12	R-12	D	Row House	1,483.49	2,002.72	3,500.00	70,09,511.00
		TOTAL		17,801.93	24,032.61		8,41,14,132.00





#### **SUMMARY**

#### **Construction Cost:**

Sr. No.	Wing	Built Up Area in Sq. M.	Rate per Sq. M.	Cost of Construction in ₹	% of work completed	Construction Cost Incurred as on date in ₹	Cost to be incurred in ₹
1	A	10,416.83	30,000.00	31,25,04,900.00	58%	18,21,76,920.00	13,03,27,980.00
2	В	15,826.12	30,000.00	47,47,83,720.00	21%	10,06,30,200.00	37,41,53,520.00
3	С	9,670.33	30,000.00	29,01,09,810.00	81%	23,62,42,092.00	5,38,67,718.00
4	D	1,727.80	30,000.00	5,18,34,000.00	0%	-	5,18,34,000.00
T	DTAL	37,641.08		1,12,92,32,430.00	46%	51,90,49,212.00	61,01,83,218.00

**Other Expenditure Cost:** 

Sr. No.	Tower No.	Cost in ₹		
1	A	6,02,55,675.00		
2	В	9,17,06,643.00		
3	С	5,57,27,303.00		
4	D	1,04,94,063.00		
	TOTAL	21,81,83,684.00		

Unsold Flats Inventory's:

Sr. No.	Wing	No. of Units	RERA Carpet Area in Sq. Ft.	Saleable Area in Sq. Ft.	Rate per Sq. Ft. on Saleable Area	Value in ₹
1	Α	85.00	70,396.75	95,035.61	3,000.00	28,51,06,836.00
2	В	90.00	1,17,323.51	1,58,386.74	3,000.00	47,51,60,214.00
3	С	53.00	44,357.15	59,882.16	3,000.00	17,96,46,467.00
4	D	12.00	17,801.93	24,032.61	3,500.00	8,41,14,137.00
TC	TAL	240.00	2,49,879.35	3,37,337.12		1,02,40,27,654.00

Sold Flats Inventory's:

Sr. No.	Wing	Comp.	No. of Flats	Total Saleable Area in Sq. Ft.	Agreement Value in ₹	Received Amount in ₹	Receivable Amount in ₹
1	Α	2 BHK	18.00	20,926.09	7,13,85,253.00	3,22,85,701.00	3,90,99,552.00
2	В	3 BHK	14.00	27,460.63	7,45,10,317.00	78,63,823.00	6,66,46,494.00
3	С	2 BHK	43.00	48,008.18	14,07,85,247.00	5,66,60,200.00	8,41,25,047.00
	Total		75.00	96,394.90	28,66,80,817.00	9,68,09,724.00	18,98,71,093.00

Total Income from the Inventory's After 100% Completion

Sr. No.	Wing	Value of Unsold Inventory in ₹	Agreement Value of Sold Inventory in ₹	Total Income in ₹
1	Α	28,51,06,836.00	7,13,85,253.00	35,64,92,089.00
2	В	47,51,60,214.00	7,45,10,317.00	54,96,70,531.00
3	С	17,96,46,467.00	14,07,85,247.00	32,04,31,714.00
4	D	8,41,14,137.00	-	8,41,14,137.00
Total		102,40,27,654.00	28,66,80,817.00	131,07,08,471.00





Property Value as on Date

6	Sr. No.	Wing	No. of Units	RERA Carpet Area in Sq. Ft.	Saleable Area in Sq. Ft.	Value after 100% completion in ₹	Deduction of Amount Received in ₹	Deduction of balance cost of construction in	Deduction of other expenditure Cost in ₹	Net Value in ₹	Developer Profit 25% on Net Value in ₹	Net Present Value in ₹
	1	A	104.00	85,970.83	1,16,060.63	35,64,92,089.00	3,22,85,701.00	13,03,27,980.00	6,02,55,675.00	13,36,22,733.00	3,34,05,683.00	10,02,17,050.00
	2	В	104.00	1,37,270.14	1,85,314.69	54,96,70,531.00	78,63,823.00	37,41,53,520.00	9,17,06,643.00	7,59,46,545.00	1,89,86,636.00	5,69,59,909.00
	3	С	96.00	79,755.06	1,07,669.33	32,04,31,714.00	5,66,60,200.00	5,38,67,718,00	5,57,27,303.00	15,41,76,493.00	3,85,44,123.00	11,56,32,370.00
	4	D	12.00	17,801.93	24,032.61	8,41,14,137.00	-	5,18,34,000.00	1,04,94,063.00	2,17,86,074.00	54,46,519.00	1,63,39,555.00
	TO	TAL	316.00	3,20,797.97	4,33,077.26	1,31,07,08,471.00	9,68,09,724.00	61,01,83,218.00	21,81,83,684.00	38,55,31,845.00	9,63,82,961.00	28,91,48,884.00

Page **34** of **59** 

Particulars	Value in ₹	Value in Cr. ₹				
Fair Market Value as on Date	28,91,48,884.00	28.91				
Realizable Value as on Date	26,02,33,996.00	26.02				
Distress Value as on Date	23,13,19,107.00	23.13				



# **Actual Site Photographs Wing A**























# Actual Site Photographs Wing A



















# Actual Site Photographs Wing B







# Actual Site Photographs Wing B

















# Actual Site Photographs Wing C







# Actual Site Photographs Wing C




















# Route Map of the property

Site u/r



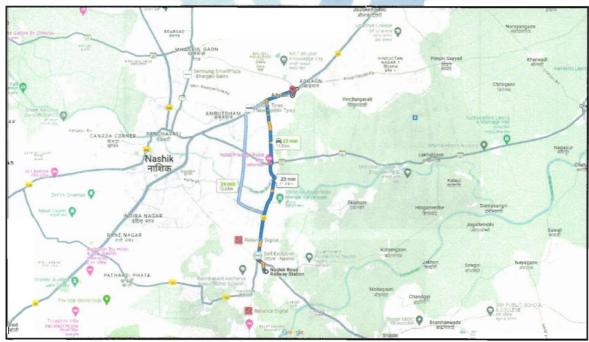


Latitude Longitude: 20°01'40.5"N 73°51'16.0"E

Note: The Blue line shows the route to site from nearest railway station (Nashik Road – 11.30 Km.)





# Ready Reckoner 2024 - 2025

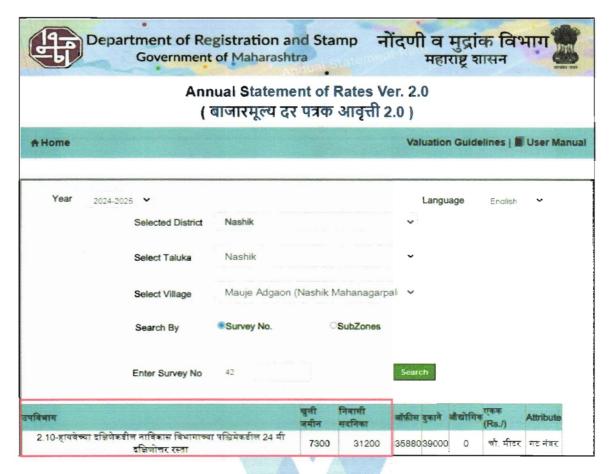






An ISO 9001: 2015 Certified Company

20104	सूची क्र.2	दुय्यम निबंधक : दु.नि. नाशिक 1
7-05-2024		<b>दस्त</b> क्रमांक : 120/2024
ote:-Generated Through eSearch lodule,For original report please		नोदंणी :
ontact concern SRO office.		Regn:83m
	गावाचे नाव: आडगांव	1
(1)विलेखाचा प्रकार	डीड ऑफ अपार्टमेंट	- Control
(2)मोबदला	3057000	
(3) बाजारभाव(भावेपटटवाच्या बाबतितपटटाकार आकारणी देतो की पटटेदार ते नमुद करावे)	3057000	
(4) भू-मापन,पोटहिस्सा व घरक्रमांक(असल्यास)	1) पालिकेचे नाव:नाशिक म.न.पा.इतर वर्णन:, इतर माहिती: , इतर माहिती: मोजे आडगःव येथील सर्व्हें नंबर 770/2+459 या मिळकती पैकी बिनशेती प्लॉट क्रमांक 27-28+29 यांसी एकूण क्षेत्र 1653. चौ . मि . या मिळकतीवर बांधण्यात येत असलेल्या " रॉयल रेसिडेन्सी ' या प्रकल्पातील सहाव्या मजल्यावरील फ्लॅट क्रमांक 601(सहाशे एक)- ' बी ' विंग यांसी क्षेत्र 64.18 चौ . मी . अधिक बाल्कनी क्षेत्र 7.51 चौ . मी . चौ . मी .(चटई)ही मिळकत( ( Survey Number : 770/2+459 ; Plot Number : 27+28+29 ; ) )	
(5) क्षेत्रफळ	64.18 ची.मीटर	
(6)आकारणी किंदा जुडी देण्यात असेल तेव्हा.		
(७) दस्तिऐदज करुन देणा-या लिङ्गन ठेवणा-या पक्षकाराचे नाव किंवा दिवाणी न्यायालयाचा हुकुमनामा किंवा आदेश असल्यास,प्रतिवादिचे नाव व पत्ता.	श्री मियांक बळवंत खौरसिया, श्री . सुनील मु . श्री सुनील ठाकरशीभाई टांक वय:-३३	दिवारी संस्था ) तर्फे भागीदार श्री . नितीन हरिकृष्ण युरोहि ठाकरमीभाई टांक , सी. ज्योती सुनीत टांक सर्वांतर्फे उ पत्ताप्लॉट नं: ६०३, माळा नं: इमारतीचे नाव: कान्हा आउगांव नाका . रोउ नं: पंचवटी, महाराष्ट्र, नाशिक . पि
(६)दस्तऐवज करून घेणा-या पक्षकाराचे व किंवा दिवाणी न्यायालयाचा हुकुननाना किंवा आदेश असल्यास,प्रतिवादिचे नाव व पत्ता	सहजानंद अपार्टमेंट, ब्लॉक नं: महालक्ष्मी कोड: 422003 पॅन नं: AMYPM7567N 2): नाव:-सौ. रेखा चंद्रकांत मृतमृते दय:	:-44; पत्ता:-प्लॉट नं:-, माल्य नं:-, इमारतीचे नाव:   नगर, रोड नं: आडगांव, महासष्ट्र, नहिराक. पिन -39, पत्ता:-प्लॉट नं:-, माल्या नं:-, इमारतीचे नाव:   नगर, रोड नं: आडगांव , महाराष्ट्र, नाशिक. पिन
(९) दरराऐदज करुन दिल्याचा दिनांक	27/12/2023	
(10)दस्त नोंडणी केल्याचा दिनांक	03/01/2024	
(11)अनुक्रमांक खेंड व पृष्ठ	120/2024	
(12)बाजारभावाप्रमाणे मुद्रांक शुल्क	100	
(13)बाजारभावाप्रमाणे नोंदणी शुल्क	100	
(14)शेरा		
मुल्यांकनासाठी विचारात घेतलेला तपश्रील:-:	मुल्यांकनाची आवश्यकता नाही क कारणाचा तपशील करारनामा अव	गरण करारनामा अलाहिदा नोंदविला आहे नाहिदा नोंदविला आहे
मुद्रांक गुल्क आकारताना निवजनेला अनुच्छेद :- :	(i) within the limits of any Musarea annexed to it.	nicipal Corporation or any Cautonment









1786104	सूची क्र.2	दुय्यम निबंधक : दु.नि. नाशिक 1
17-95-2024		दस्त क्रमांक : 1786/2023
Note:-Generated Through eSearch Module,For original report please		नोढंणी :
contact concern SRO office.		Regn:83m
	गावाचे नाव: आडगांव	
(1)विलेखाचा प्रकार	अँग्रीमेंट टू सेल	
(2)मोबदला	2911000	
(3) बाजारभाव(भाठेपटटयाच्या बाबतितपटटाकार आकारणी देतो की पटटेदार ते नमुद करावे)	2911000	
(4) भू-मापन,पोटहिस्सा व घरक्रमांक(असल्यास)	1) पालिकेचे नाव:नाशिक म.न.पा.इतर व येथील सर्व्हें नंबर 770/2+459 या मिळक 27+28+29 यांसी एकूण क्षेत्र 1653. चौ . असलेल्या " रॉयल रेसिडेन्सी ' या प्रकल्प 204 - ' बी ' विंग यांसी क्षेत्र 64.18 चौ. मी मी.(चटई)ही मिळकत( ( Survey Numb 27+28+29 ; ) )	न्ती पैकी बिनशेती प्लॉट क्रमांक मि . या मिळकतीवर बांधण्यात येत ॥तील दुसऱ्या मजल्यावरील फ्लॅट क्रमांक १. अधिक बाल्कनी क्षेत्र 7.51 चौ. मी. चौ.
(5) <b>क्षेत्रफ</b> ळ 64.18 चौ.मीटर		
(ठ)आकारणी किंवा जुडी देण्यात असेत तेव्हा.		
(7) दस्तऐवज करून देगा-यः तिहून ठेवणा-या पक्षकाराचे नाव किंवा दिवाणी न्यायालयाचा हुकुमनामा किंवा आदेश असल्यास,प्रतिवादिचे नाव व पत्ता.	। पक्षकाराचे नाव किंवा विवाणी      श्री मिशांक बळवंत खोरसिया, श्री . सुनील ठाकरशीभाई टांक , सौ. ज्यौती सुनील टांक सर्वांतर्फे ज . ।चा हुकुमनामा किंवा आदेश	
(४)दस्तऐवज करून घेणा-या यक्षकाराचे व किंवा दिवाणी न्यायालयाचा हुकुमनामा किंवा आदेश असल्यास,प्रतिवादिचे नाव व पत्ता	1): नाव:-सौ. पूनम फितेंद्र बैरागी वय:-42; पत्ता: नं: चंद्रमाई . रेणुका माता मंदीर, रोज नं: सातपूर, CCNPB2138K 2): नाव:-श्री. जितेंद्र सुभाष बैरागी वय:-44; पत्ता नं: चंद्रमाई , रेणुका माता मंदीर , रोज नं: सातपूर AUIPB3428M	महाराष्ट्र, नामिकः यिन कोठ:-422012 यॅन नं:-
(९) दस्तऐवज करून दिल्याचा दिनांक	04/02/2023	
(10)दरत नोंद्रणी केल्याचा दिनांक	17/02/2023	
(11)अनुक्रमांक.खेंड व पृष्ठ	1786/2023	
(12)बाजारभावाप्रमाधे मुद्रांक शुल्क	175000	
(13)बाजारभावाप्रमाणे नींदणी म्हुल्क	29200	
(14)शेरा	रा	
मुल्यांकनासाठी विचारात घेतलेला तपश्रील:-:		
मुद्रांक शुल्क आकारताना निवजनेला अनुष्णेद :- :	(i) within the limits of any Municipa area annexed to it.	al Corporation or any Cantonment









2697104	सूची क्र.2	दुय्यम निबंधक : दु.नि. नाशिक 1
17-05-2024	C.	दस्त क्रमांक : 2697/2023
Note:-Generated Through eSearch Module,For original report please		नोंदंणी :
contact concern SRO office.		Regn:63m
	गावाचे नाव: आडगांव	
(1)विलेखाचा प्रकार	अँग्रीमेंट टू सेल	
(2)मोबदला	वला 3057000	
(3) बाजारभाव(भावेपटटपाच्या बाबतितघटटाकार आकारणी देतो की पटटेदार ते नमुद करावे)	3057000	
(4) भू-मापन्,पोटहिस्सा व घरक्रमांक(असल्यास)	1) पालिकेचे नाव:नाशिक म.न.पा.इतर वर्णन :, इतर माहिती; मौजे आडगांव येथील सर्व्हें नंबर 770/2+459 या मिळकती पैकी बिनशेती प्लॉट क्रमांक 27–28+29 यांसी एकूण क्षेत्र 1653 .84 चौ . मि . या मिळकतीवर बांधण्यात येत असलेल्या " रॉयल रेसिडेन्सी ' या प्रकल्यातील पाचव्या मजल्यावरील फ्लॅट क्रमांक 504 - ' बी ' विंग यांसी क्षेत्र 64.18 चौ. मी. अधिक बाल्कनी क्षेत्र 7.51 चौ. मी. चौ. मी.(चटई)ही मिळकत( ( Survey Number: 770/2+459 ; Plot Number: 27+28+29 ; ) )	
(5) क्षेत्रकळ	64.18 ची.मीटर	
(6)आकारवी किया जुडी देण्यात असेल तेव्हा.		
(७) दस्सप्रेवज करून देणा-या सिंहून ठेवणा-या पक्षकाराचे नाव किंवा दिवाणी न्यायालयाचा हुकुमनामा किंवा आदेश असल्यास,प्रतिवादिचे नाव व पत्ता.	1): नाव:-में . सद्गुरू असोसिष्ट्स (भागीदारी संस्था ) तर्फे भागीदार श्री . नितीन हरिकृष्ण पुरोहित, श्री मिणांक बळवंत खोरसिया, श्री . सुनील ठाकरणीभाई टांक , सो. ज्योती सुनील टांक सर्वांतर्फे ख . मु . श्री सुनील ठाकरणीभाई टांक वय:-38 पत्ता:-प्लॉट नं: 603, भाळा नं: -, इमारतीचे नाव: कान्हा विल्डींग , सम्मट वृन्दावन , ब्लॉक नं: जुना आठगांव नाका , रोठ नं: पंचवटी, महाराष्ट्र, नामिक . पिन कोड:-422003 पन नं:-ACUF\$9650E	
(४)द्वस्तिप्रेवज करुन घेणा-या पश्चकाराचे व किंवा दिवःणी न्यायालयःचा हुंकुननामा किंवा आदेश असल्यास प्रतिवादिचे नाव व प्रता	1): नावः श्री. दिलीय काशिनाथ भागरे वयः 52: घत्ताः प्लॉट नं: -, माळा नं: -, इमारतीचे नाव: पूजा ग्रेसॉक्स, ब्लॉक नं: चांदरवरूप नगर. रोड नं: साक्री, महाराष्ट्र, धुले. पिन कोखः 424304 पॅन नं: - AOXPB8785N 2): नावः स्री. मयुरी दिलीय भागरे वयः 46: पत्ताः प्लॉट नं: -, माळा नं: -, इमस्प्रतीचे अवः पूजा ग्रेसंस्य, ब्लॉक नं: चांदरवरूप नगर. रोड नं: साक्री, महाराष्ट्र, धुले. पिन कोखः 424304 पन नं: - AOSIPB30158	
(७) दस्तोदेवन करून दिल्याचा दिनांक	13/03/2023	
(10)दस्त नोंदणीं केल्याचा दिनांक	15/03/2023	· · · · · · · · · · · · · · · · · · ·
(11)अनुक्रमांक खंड व पृष्ठ	2697/2023	
(12)बाजारभावाप्रमाधे मुद्रांक शुल्क	183500	
(23)बाजारभावाप्रमाणे नोंदणी शुल्क	30000	
्14)फोरा		
मुल्यांक नासाठी विचारात घेतलेला तथसील -:		
मुद्रांक शुल्क आकारताना निवउलेला अनुष्ठेद ः	(i) within the limits of any Munici area annexed to it.	ipal Corporation or any Cantonment





Value Nutralization Automatical Automatica

10386194	सूची क्र.2	दुय्यम निबंधक : दु.नि. नाशिक 1
17-95-2924	K 11 A 12	दस्त क्रमांक : 10386/2023
Note:-Generated Through eSearch		नोढंणी :
Module,For original report please contact concern SRO office.		Regn:t3m
	गावाचे नाव: आडगांव	·
(1)बिलेखाचा प्रकार	अँग्रीमेंट टू सेल	11 TO 12
(२)मोबटला	बंदला 3000000	
(3) बाजारभाव(भावेपटटयाच्या बाबतितपटटाकार आकारणी देतो की पटटेदार ते नमुद करावे)	2500000	
(4) भू-मापन्,पोटहिस्सा व घरक्रमांक(असल्यास)	1) पालिकेचे नाव:नाशिक म.न.पा.इतर वर्णन :, इतर माहिती: , इतर माहिती: मौजे आडगांव येथील सर्व्हें नंबर 770/2+459 यः मिळकती पैकी बिनशेती प्लॉट क्रमांक 27+28-29 यांसी एकूण क्षेत्र 1653.84 चौ . मि . या मिळकतीवर बांधण्यात येत असलेल्या " रॉयल रेसिडेन्सी ' या प्रकल्पातील तळ मजल्यावरील फ्लॅट क्रमांक जी - 102 - 'ए ' विंग यांसी क्षेत्र 55.72 चौ. मी. अधिक बाल्कनी क्षेत्र 9.30 चौ. मी. चौ. मी.(चटई)ही मिळकत( ( Survey Number : 770/2+459 ; Plot Number : 27+28+29 ; ) )	
(5) क्षेत्रफळ	55.72 चौ.मीटर	
(6)आकारणी किंवा जुडी देण्यात असेल तेव्हा.		
(7) दस्ताऐवज करून देणा-याः विहून ठेवणा-या पक्षकाराचे नाव किंवा दिवाणी न्यायालयाचा हुकुमनामा किंवा आदेश असल्यास,प्रतिवादिचे नाव व पत्ता.	1): नाव:-मे . सद्गुरू असोसिएट्स (भागीदारी संस्था ) तर्फे भागीदार श्री . नितीन हरिकृष्ण पुरोहित, श्री मिशांक बळवंत खोरसिया, श्री . सुनील ठाकरशीभाई टांक , सी. ज्योती सुनील टांक सर्वांतर्फे ज . मु . श्री सुनील ठाकरशीभाई टांक वय:-38 पत्ता:-प्लॉट नं: ६०३, माळा नं: -, इमारतीचे नाव: कान्हा बिल्डींग , सम्राट वृन्दावन , ब्लॉक नं: जुना आडगांव नाका , रोड नं: पंचवटी, महाराष्ट्र, नाशिक . पिन कोड:-422003 पॅन नं:-ACUFS0650E	
(8)दरतप्रेवज करून घेणा-या पक्षकाराचे व किंवा दिवाणी न्यायालयाचा हुकुमनामा किंवा आदेश असल्यास,प्रतिवादिचे नाव व पत्ता	ग   साकार रो हाऊसेस , ब्लॉक नं: स्वामी समर्थ नगर, रोड नं: आडगांव, महाराष्ट्र, नाशिक : पिन	
(9) दस्तऐवज करुन दिल्याचा दिनांक	17/10/2023	
(10)दस्त नोंदणी केल्याचा दिनांक	18/10/2023	
(11)अनुक्रमांक,खंड व पृष्ठ	10386/2023	
(12)बाजारभावाप्रमाणे मुद्रांक शुल्क	180000	
(13)बाजारभावाप्रमाणे नोंदणी सुल्क	30000	
(14)शेरा		
मुल्यांकनासाठी विचारात घेतलेला तपशील:-:		
मुद्रांक शुल्क आकारताना निवडलेला अनुच्छेद :-:	(i) within the limits of any Municipa area annexed to it.	al Corporation or any Cantonment






421104	सूची क्र.2	दुय्यम निबंधक : दु.नि. नाशिक 1
7-05-2024	-	दस्त क्रमांक : 2421/2024
Note:-Generated Through eSearch Module,For original report please		नोढंणी :
contact concern SRO office.		Regn:63m
	गावाचे नाव: आडगांव	
(1)विलेखाचा प्रकार	डीड ऑफ अपार्टमेंट	
(2)मोबदला	2700000	
(3) बाजारभाव(भाडेघटटदाच्या बाबतितघटटाकार आकारणी देतो की घटटेदार ते नमुद करावे)	2468500	
(4) भू-मापन,पोटहिस्सा व घरक्रमांक(असल्यास)	1) पालिकेचे नाव:नाश्कि म.न.पा.इतर वर्णन: इतर माहिती: , इतर माहिती: मौजे आडगांव येथील सर्व्हें नंबर 770/2+459 या मिळकती पैकी बिनशेती प्लॉट क्रमांक 27+28+29 यांसी एकूण क्षेत्र 1653.84 चौ . मि . या मिळकतीवर बांधण्यात येत असलेल्या " रॉयल रेसिडेन्सी ' या प्रकल्पातील चौथ्या मजल्यावरील फ्लॅट क्रमांक 402 - ' बी ' विंग यांसी क्षेत्र 64.18 चौ. मी. अधिक बाल्कनी क्षेत्र 7.51 चौ. मी. चौ. मी.(चटई)ही मिळकत( ( Survey Number : 770/2+459 ; Plot Number : 27-28+29 ; ))	
(5) क्षेत्रफळ	64.18 चौ.मीटर	
(6)आकारणी किं <b>वा जुडी दे</b> ण्यात असेल तेव्हा.		
(7) दस्तेपेदज करुन देणा-या तिहून ठेवणा-या यक्षकाराचे नाव किंवा दिवाणी न्यायालयाचा हुकुमनामा किंवा आदेश असल्यास,प्रतिवादिचे नाव व पत्ता.	श्री मिशांक बळवंत खौरसिया, श्री. सुनील ठा मु. श्री सुनील ठाकरशीभाई टांक वय:-38 पर	री संस्था ) तर्फे भागीदार श्री . नितीन हरिकृष्ण पुरोहित करशीभाई टांक , सौ. ज्योती सुनील टांक सर्वांतर्फे ख . ता:-प्लॉट नं: ६०३, माळा नं: -, इमारतीचे नाव: कान्हा उगांव नाका , रोड नं: पंचवटी, महाराष्ट्र, नाशिक. पिन
(६)दस्तिऐवज करून घेणा-या पक्षकाराचे व किंवा दिवाणी न्यायालयाचा हुकुमनामा किंवा आदेश असल्यास,प्रतिवादिचे नाव व पत्ता	रेसिछेन्सी अपार्टमेंट, ब्लॉक नं: वी मार्ट च्या म कोड:-422003 पॅन नं:-AVQPT0322D 2): नाव:-सौ. पूजा शरद ठोके वय:-27; पत्ता	-प्लॉट नं: -, माळा नं: -, इमारतीचे नाव: रॉयल गागे . रोड नं: आडगांव, महाराष्ट्र, नाशिक. धिन १:-प्लॉट नं: -, माळा नं: -, इमारतीचे नाव: रॉयल गागे , रोड नं: आडगांव . महाराष्ट्र, नाशिक. पिन
(९) दस्तपेवज करून दिल्याचा दिनांक	27/02/2024	
(10)दस्त नोंद्रणी केल्याचा दिनांक	05/03/2024	
(11)अनुक्रमांक,खंड व पृष्ठ	2421/2024	
(12)बाजारभावाप्रमाधे मुद्रांक शुल्क	100	
(13)बाजारभावाप्रमाग्रे मोंदणी मुल्क	100	
(14)शेरा		
मुल्यांकनासाठी विचारस्त घेतलेला तपशील:-:	मुल्यांकनाची आवश्यकता नाही कार कारणाचा तपशील दस्तप्रकारनुसार	ण दस्तप्रकारनुसार आवश्यक नाही आवश्यक नाही
मुद्रांक शुल्कं आकारताना निवडलेला अनुच्छेद :- :	(i) within the limits of any Municarea annexed to it.	cipal Corporation or any Cantonment

















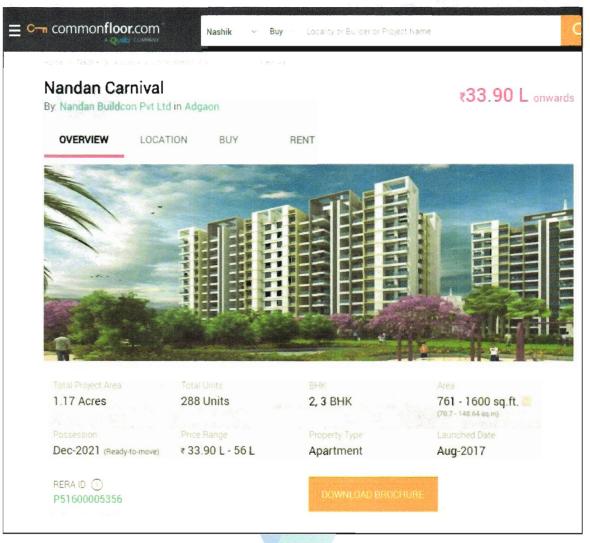







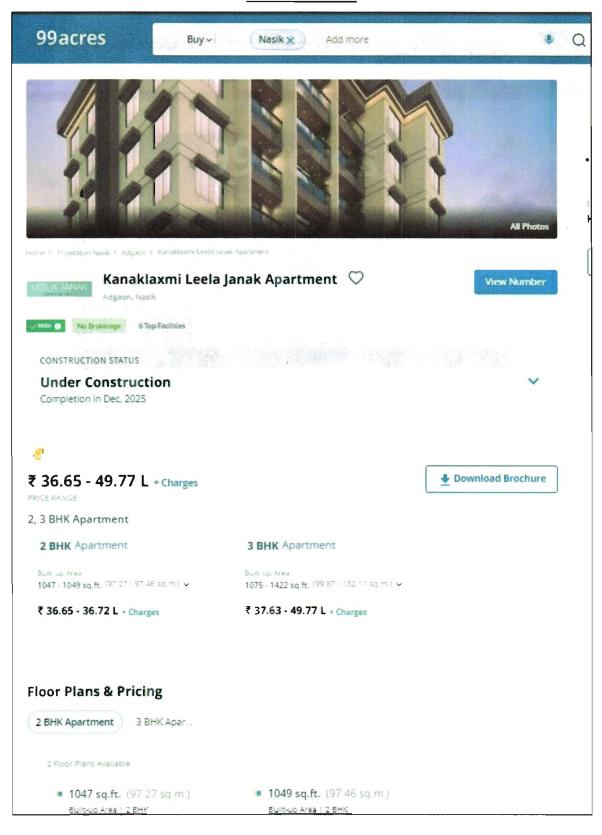




Since 1989

Vastukala Consultants (I) Pvt. Ltd.

An ISO 9001: 2015 Certified Company



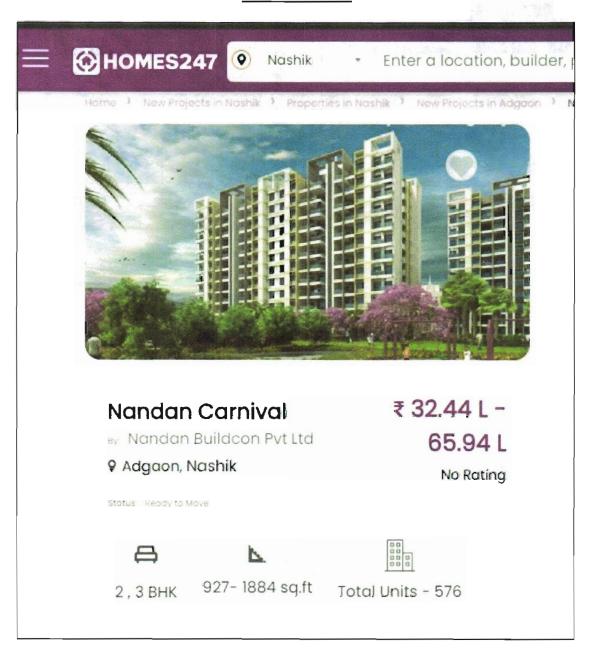





As a result of my appraisal and analysis, it is my considered opinion that the realizable Value of the above property in the prevailing condition with aforesaid specification is (As per table attached to the report)

Place: Mumbai Date: 18.05.2024

For VASTUKALA CONSULTANTS (I) PVT. LTD.

Sharadkumar Chalikwar Digitally signed by Sharadkumar Chalikwar DN: cn=Sharadkumar Chalikwar o=Vastukala Consultants (I) Pv1. Ltd., ou=Mumbai, email=cmd@vastukala.org, c=IN Date: 2024.05 18 17:41:09 +05'30'

Auth. Sign.

Director Sharadkumar B. Chalikwar

Govt. Reg. Valuer

Chartered Engineer (India)

Reg. No. (N) CCIT/1-14/52/2008-09

Enclosures		
	Declaration-cum-undertaking from the valuer (Annexure- I)	Attached
	Model code of conduct for valuer - (Annexure - II)	Attached



An ISO 9001: 2015 Certified Company

### **DECLARATION FROM VALUERS**

#### I, hereby declare that:

- a. The information furnished in my valuation report dated 17.05.2024 is true and correct to the best of my knowledge and belief and I have made an impartial and true valuation of the property.
- b. I have no direct or indirect interest in the property valued;
- c. I/ my authorized representative have personally inspected the property on 25.04.2024 The work is not sub contracted to any other valuer and carried out by myself.
- d. I have not been convicted of any offence and sentenced to a term of Imprisonment;
- e. I have not been found guilty of misconduct in my professional capacity.
- f. I have read the Handbook on Policy, Standards and procedure for Real Estate Valuation, 2011 of the IBA and this report is in conformity to the "Standards" enshrined for valuation in the Part - B of the above handbook to the best of my ability.
- g. I have read the International Valuation Standards (IVS) and the report submitted to the Bank for the respective asset class is in conformity to the "Standards" as enshrined for valuation in the IVS in "General Standards" and "Asset Standards" as applicable. The valuation report is submitted in the prescribed format of the bank.
- h. I abide by the Model Code of Conduct for empanelment of valuer in the Bank. (Annexure III A signed copy of same to be taken and kept along with this declaration)
- I am registered under Section 34 AB of the Wealth Tax Act, 1957.
- j. I am Chairman & Managing Director of the company, who is competent to sign this valuation report.
- k. Further, I hereby provide the following information.





Sr. No.	Particulars	Valuer comment
1.	Background information of the asset being valued;	The property under consideration is developed by M/s. Nandan Buildcon Pvt. Ltd.
2.	Purpose of valuation and appointing authority	As per the request from Union Bank of India, SAMB Fort Branch to assess Market value of the property for SARFAESI (Securitisation and Reconstruction of Financial Assets and Enforcement of Security Interest Act, 2002) purpose.
3.	Identity of the valuer and any other experts involved in the valuation;	Sharadkumar B. Chalikwar – Regd. Valuer Manoj B. Chalikwar – Regd. Valuer Prayush P. Parekh – Senior Valuation Engineer Saiprasad Patil – Valuation Engineer
4.	Disclosure of valuer interest or conflict, if any;	We have no interest, either direct or indirect, in the property valued. Further to state that we do not have relation or any connection with property owner / applicant directly or indirectly. Further to state that we are an independent Valuer and in no way related to property owner / applicant
5.	Date of appointment, valuation date and date of report;	Date of Appointment – 24.04.2024 Valuation Date – 16.05.2024 Date of Report – 16.05.2024
7.	Inspections and/or investigations undertaken;  Nature and sources of the information used or relied upon;	<ul> <li>Physical Inspection done on 25.04.2024</li> <li>Market Survey at the time of site visit</li> <li>Ready Reckoner rates / Circle rates</li> <li>Online search for Registered Transactions</li> <li>Online Price Indicators on real estate portals</li> <li>Enquiries with Real estate consultants</li> <li>Existing data of Valuation assignments carried out by us</li> </ul>
8.	Procedures adopted in carrying out the valuation and valuation standards followed:	Sales Comparative Method
9.	Restrictions on use of the report, if any;	This valuation is for the use of the party to whom it is addressed and for no other purpose. No responsibility is accepted to any third party who may use or rely on the whole or any part of this valuation. The valuer has no pecuniary interest that would conflict with the proper valuation of the property.
10.	Major factors that were taken into account during the valuation;	Current market conditions, demand and supply position, residential land size, location, sustained demand for residential land, all round development of commercial and residential application in the locality etc.
11.	Caveats, limitations and disclaimers to the extent they explain or elucidate the limitations faced by valuer, which shall not be for the purpose of limiting his responsibility for the valuation report.	Attached







# Assumptions, Disclaimers, Limitations & Qualifications

# Value Subject to Change

The subject appraisal exercise is based on prevailing market dynamics as on 18th May 2024 and does not take into account any unforeseeable developments which could impact the same in the future.

### **Our Investigations**

We are not engaged to carry out all possible investigations in relation to the subject property. Where in our report we identify certain limitations to our investigations, this is to enable the reliant party to instruct further investigations where considered appropriate or where we recommend as necessary prior to reliance. Vastukala Consultants India Pvt. Ltd. (VCIPL) is not liable for any loss occasioned by a decision not to conduct further investigations

# **Assumptions**

Assumptions are a necessary part of undertaking valuations. VCIPL adopts assumptions for the purpose of providing valuation advise because some matters are not capable of accurate calculations or fall outside the scope of our expertise, or out instructions. The reliant party accepts that the valuation contains certain specific assumptions and acknowledge and accept the risk of that if any of the assumptions adopted in the valuation are incorrect, then this may have an effect on the valuation.

# Information Supplied by Others

The appraisal is based on the information provided by the client. The same has been assumed to be correct and has been used for appraisal exercise. Where it is stated in the report that another party has supplied information to VCIPL, this information is believed to be reliable but VCIPL can accept no responsibility if this should prove not to be so.

#### **Future Matters**

To the extent that the valuation includes any statement as to a future matter, that statement is provided as an estimate and/or opinion based on the information known to VCIPL at the date of this document. VCIPL does not warrant that such statements are accurate or correct.

### Map and Plans

Any sketch, plan or map in this report is included to assist the reader while visualising the property and assume no responsibility in connection with such matters.

#### Site Details

Based on inputs received from Client's representative and site visit conducted, we understand that the subject property is currently a Building Under Construction work is in progress contiguous and non-agricultural land parcel admeasuring as per table attached to the report and developer in the name of M/s. Nandan Buildcon Pvt. Ltd.. Further, VCIPL has assumed that the subject property is free from any encroachment and is available as on the date of the appraisal.

## Property Title

Based on our discussion with the Client, we understand that the subject property is developed by M/s. Nandan Buildcon Pvt. Ltd.. For the purpose of this appraisal exercise, we have assumed that the subject property has a clear title and is free from any encumbrances, disputes and claims. VCIPL has made no further enquiries with the relevant local authorities in this regard and does not certify the property as having a clear and marketable title. Further, no legal advice regarding the title and ownership of the subject property has been obtained for the purpose of this appraisal exercise. It has been assumed that the title deeds are clear and marketable.

## **Environmental Conditions**

We have assumed that the subject property is not contaminated and is not adversely affected by any existing or proposed environmental law and any processes which are carried out on the property are regulated by environmental legislation and are properly licensed by the appropriate authorities.

#### Town Planning

The permissible land use, zoning, achievable FSI, area statement adopted for purpose of this valuation is based on the information provided by the Client's representative and the same has been adopted for this valuation purpose. VCIPL has assumed the same to be correct and permissible. VCIPL has not validated the same from any authority.



Since 1989

Vastukala Consultants (I) Pvt. Ltd.

Aniso 9001: 2015 Certified Company



#### Area

Based on the information provided by the Client's representative, we understand that the subject property is a Building Under Construction work is in progress, contiguous and non-agricultural land parcel admeasuring as per table attached to the report.

### Condition & Repair

In the absence of any information to the contrary, we have assumed that there are no abnormal ground conditions, nor archaeological remains present which might adversely affect the current or future occupation, development or value of the property. The property is free from rat, infestation, structural or latent defect. No currently known deleterious or hazardous materials or suspect techniques will be used in the construction of or subsequent alteration or additions to the property and comments made in the property details do not purport to express an opinion about, or advise upon, the condition of uninspected parts and should not be taken as making an implied representation or statement about such parts

#### Valuation Methodology

For the purpose of this valuation exercise, the valuation methodology used is Direct Comparison Approach Method and proposed Current Use / Existing Use premise is considered for this assignment.

The Direct Comparison Approach involves a comparison of the property being valued to similar properties that have actually been sold in arms - length transactions or are offered for sale. This approach demonstrates what buyers have historically been willing to pay (and sellers willing to accept) for similar properties in an open and competitive market and is particularly useful in estimating the value of the land and properties that are typically traded on a unit basis.

In case of inadequate recent transaction activity in the subject micro-market, the appraiser would collate details of older transactions. Subsequently, the appraiser would analyse rental / capital value trends in the subject micro-market in order to calculate the percentage increase / decrease in values since the date of the identified transactions. This percentage would then be adopted to project the current value of the same.

Where reliance has been placed upon external sources of information in applying the valuation methodologies, unless otherwise specifically instructed by Client and/or stated in the valuation, VCIPL has not independently verified that information and VCIPL does not advise nor accept it as reliable. The person or entity to whom the report is addressed acknowledges and accepts the risk that if any of the unverified information in the valuation is incorrect, then this may have an effect on the valuation.

## Not a Structural Survey

We state that this is a valuation report and not a structural survey

#### Other

All measurements, areas and ages quoted in our report are approximate

#### Legal

We have not made any allowances with respect to any existing or proposed local legislation relating to taxation on realization of the sale value of the subject property. VCIPL is not required to give testimony or to appear in court by reason of this appraisal report, with reference to the property in question, unless arrangement has been made thereof. Further, no legal advice on any aspects has been obtained for the purpose of this appraisal exercise

#### Property specific assumptions

Based on inputs received from the client and site visit conducted, we understand that the subject property is currently in owner possession, contiquous land parcel.

# ASSUMPTIONS, CAVEATS, LIMITATION AND DISCLAIMERS

- 1. We assume no responsibility for matters of legal nature affecting the property appraised or the title thereto, nor do we render our opinion as to the title, which is assumed to be good and marketable.
- 2. The property is valued as though under responsible ownership.
- 3. It is assumed that the property is free of liens and encumbrances.
- 4. It is assumed that there are no hidden or unapparent conditions of the subsoil or structure that would render it more or less valuable. No responsibility is assumed for such conditions or for engineering that might be required to discover such factors.
- 5. There is no direct/ indirect interest in the property valued.
- 6. The rates for valuation of the property are in accordance with the Govt. approved rates and prevailing market rates



Since 1989

Vastukala Consultants (I) Pvt. Ltd.

An ISO 9001: 2015 Certified Company



#### MODEL CODE OF CONDUCT FOR VALUERS

# {Adopted in line with Companies (Registered Valuers and Valuation Rules, 2017)}

All valuers empanelled with bank shall strictly adhere to the following code of conduct:

### Integrity and Fairness

- 1. A valuer shall, in the conduct of his/its business, follow high standards of integrity and fairness in all his/its dealings with his/its clients and other valuers.
- 2. A valuer shall maintain integrity by being honest, straightforward, and forthright in all professional relationships.
- 3. A valuer shall endeavour to ensure that he/it provides true and adequate information and shall not misrepresent any facts or situations.
- 4. A valuer shall refrain from being involved in any action that would bring disrepute to the profession.
- 5. A valuer shall keep public interest foremost while delivering his services.

### Professional Competence and Due Care

- 6. A valuer shall render at all times high standards of service, exercise due diligence, ensure proper care and exercise independent professional judgment.
- 7. A valuer shall carry out professional services in accordance with the relevant technical and professional standards that may be specified from time to time.
- 8. A valuer shall continuously maintain professional knowledge and skill to provide competent professional service based on up-to-date developments in practice, prevailing regulations / quidelines and techniques.
- 9. In the preparation of a valuation report, the valuer shall not disclaim liability for his/its expertise or deny his/its duty of care, except to the extent that the assumptions are based on statements of fact provided by the company or its auditors or consultants or information available in public domain and not generated by the valuer.
- 10. A valuer shall not carry out any instruction of the client insofar as they are incompatible with the requirements of integrity, objectivity and independence.
- 11. A valuer shall clearly state to his client the services that he would be competent to provide and the services for which he would be relying on other valuers or professionals or for which the client can have a separate arrangement with other valuers.

#### Independence and Disclosure of Interest

- 12. A valuer shall act with objectivity in his/its professional dealings by ensuring that his/its decisions are made without the presence of any bias, conflict of interest, coercion, or undue influence of any party, whether directly connected to the valuation assignment or not.
- 13. A valuer shall not take up an assignment if he/it or any of his/its relatives or associates is not independent in terms of association to the company.
- 14. A valuer shall maintain complete independence in his/its professional relationships and shall conduct the valuation independent of external influences.
- 15. A valuer shall wherever necessary disclose to the clients, possible sources of conflicts of duties and interests, while providing unbiased services.
- 16. A valuer shall not deal in securities of any subject company after any time when he/it first becomes aware of the possibility of his / its association with the valuation, and in accordance with the Securities and Exchange Board of India (Prohibition of Insider Trading)Regulations,2015 or till the time the valuation report becomes public, whichever is earlier.
- 17. A valuer shall not indulge in "mandate snatching" or offering "convenience valuations" in order to cater to a company or client's needs.
- 18. As an independent valuer, the valuer shall not charge success fee. (Success fees may be defined as a compensation / incentive paid to any third party for successful closure of transaction. In this case, approval of credit proposals).
- 19. In any fairness opinion or independent expert opinion submitted by a valuer, if there has been a prior engagement in an unconnected transaction, the valuer shall declare the association with the company during the last five years.

An ISO 9001: 2015 Certified Company



VASTUKALA

Vastukala Consultants (I) Pvt. Ltd.

#### Confidentiality

20. A valuer shall not use or divulge to other clients or any other party any confidential information about the subject company, which has come to his / its knowledge without proper and specific authority or unless there is a legal or professional right or duty to disclose.

## Information Management

- 21. A valuer shall ensure that he/ it maintains written contemporaneous records for any decision taken, the reasons for taking the decision, and the information and evidence in support of such decision. This shall be maintained so as to sufficiently enable a reasonable person to take a view on the appropriateness of his /its decisions and actions.
- 22. A valuer shall appear, co-operate and be available for inspections and investigations carried out by the authority, any person authorised by the authority, the registered valuers organisation with which he/it is registered or any other statutory regulatory body.
- 23. A valuer shall provide all information and records as may be required by the authority, the Tribunal, Appellate Tribunal, the registered valuers organisation with which he/it is registered, or any other statutory regulatory body.
- 24. A valuer while respecting the confidentiality of information acquired during the course of performing professional services, shall maintain proper working papers for a period of three years or such longer period as required in its contract for a specific valuation, for production before a regulatory authority or for a peer review. In the event of a pending case before the Tribunal or Appellate Tribunal, the record shall be maintained till the disposal of the case.

### Gifts and hospitality:

- 25. A valuer or his / its relative shall not accept gifts or hospitality which undermines or affects his independence as a valuer.
  - Explanation: For the purposes of this code the term 'relative' shall have the same meaning as defined in clause (77) of Section 2 of the Companies Act, 2013 (18 of 2013).
- 26. A valuer shall not offer gifts or hospitality or a financial or any other advantage to a public servant or any other person with a view to obtain or retain work for himself / itself, or to obtain or retain an advantage in the conduct of profession for himself / itself.

## Remuneration and Costs.

- 27. A valuer shall provide services for remuneration which is charged in a transparent manner, is a reasonable reflection of the work necessarily and properly undertaken, and is not inconsistent with the applicable rules.
- 28. A valuer shall not accept any fees or charges other than those which are disclosed in a written contract with the person to whom he would be rendering service.

## Occupation, employability and restrictions.

- 29. A valuer shall refrain from accepting too many assignments, if he/it is unlikely to be able to devote adequate time to each of his/ its assignments.
- 30. A valuer shall not conduct business which in the opinion of the authority or the registered valuer organisation discredits the profession.





### DEFINITION OF VALUE FOR THIS SPECIFIC PURPOSE

This exercise is to assess Project Valuation of the property under reference as on 18th May 2024

The term Fair Market Value is defined as

"The most probable price, as of a specified date, in cash, terms equivalent to cash, or in other precisely revealed terms for which the specified property rights would sell after reasonable exposure in a competitive market under all conditions requisite to a fair sale, with the buyer and seller each acting prudently knowledgeably and for self interest assuming that neither is under undue duress".

Fundamental assumptions and conditions presumed in this definition are:

- 1. Buyer and seller are motivated by self-interest.
- 2. Buyer and seller are well informed and are acting prudently.
- 3. The property is exposed for a reasonable time on the open market.
- 4. Payment is made in cash or equivalent or in specified financing terms.

### DECLARATION OF PROFESSIONAL FEES CHARGED

We hereby declare that, our professional fees are not contingent upon the valuation findings. However, if the statute AND/OR clients demands that, the fees should be charged on the percentage of assessed value then, with the full knowledge of the AND/OR end user, it is being charged accordingly.

# VALUATION OF THE PROPERTY PREMISES

Considering various parameters recorded herein above, existing economic scenario, and the information that is available with reference to the development of neighborhood and method selected for valuation, we are of the opinion that, the property premises can be assessed and valued for this particular purpose as per the details provided.

For VASTUKALA CONSULTANTS (I) PVT. LTD.

Chalikwar

Sharadkumar Challis DN. cn=Sharadkumar Challiswar.
p=Vzste/kala Consultants (I) Pvt. Ltd., pu=Mumbai, email=cmd@vast ukala.org

Date: 2924.95.18 17:41:3/8+05'30" Director Auth. Sign.

Sharadkumar B. Chalikwar

Govt. Reg. Valuer Chartered Engineer (India)

Reg. No. (N) CCIT/1-14/52/2008-09



